Ref. No.: Pri/ /2026 Date: 16/09/2026

To,
The Project Manager,
Construction & Design Services (C&DS),
Office of Project Manager, Unit–35,
798, Sector -7 (Near Jain Temple) Awas Vikas Colony
Sikandara, Agra, Uttar Pradesh.
(Email -cdsupjn35@gmail.com)

Subject: Submission of Weekly Progress Report for Firozabad City for the period of 12 to 15 /09/2026.

Reference: 1. Letter of Acceptance (LOA) Letter No. 2473/G.M.(Ni-9)/e-Tender/2026, dated 10/08/2026 issued by C&DS, U.P. Jal Nigam.
2. Our Acknowledgement Letter no. Pri/1183/2026, dated.18.08.2026

Respected Sir,

With reference to the above-mentioned subject and the meeting held on 18th September 2026, we hereby submit the Weekly Progress Report for the period from 12 th to 15 th September 2026 for your kind information

Thanking you,

PRIMOVE Infrastructure Development Consultants Pvt. Ltd. PUNE

Sunil Warade
Assistant General Manager

Encl : Weekly Progress Report

Primove Infrastructure Development Consultants Pvt. Ltd.
www.primoveindia.com
C-3, 304 B, Saudamini Complex, Bhusari Colony, Paud Road, Pune 411 038 India
Tel: +91202528 0200 I 01 E: info@primoveindia.com
CIN: U74140PN1999PTC013664

WEEKLY PROGRESS REPORT-Firozabad

Reporting Period: 12/10/2026 to 15/10/2026

Project Name: Survey, Collection of Data, Preparation of Integrated Urban Storm Water Drainage Master Plan (IUSWDMP) and other allied works for **Municipal Corporation Firozabad**, Uttar Pradesh, India

1. Progress Summary

Activity	Progress / Status
City area	35.49 sq. km **(As per RFP)** 35.08 sq.km (**As per KML**)
Static points	- Planned - 5 Nos - Completed - 5 Nos (100%)
GCP points	- Planned - 86 Nos - Completed - 86 Nos (100%)
LiDAR drone survey	- Data acquisition started on 24/09/2026 - Data acquisition Completed on 28/09/2026 - Area Covered – 35.5 Sq.km - Data processing Status – In Progress
LiDAR drone survey Area excluded due to restricted area	- Name-NA
DGPS survey	- DGPS commenced on 28/08/2026 - Deployment reported as 1 base and 3 rovers on dated 07/10/2026 - Survey team members – 6 Nos - Calibration report submitted on 22/09/2026
Survey of Primary drains	- Primary Drains As per OSM Planned – 40 km - Completed Length up to previous week: 40.7 Km; - Completed length during the reporting period – 17.8 km (Extended survey till outfall); - Surveyed with alignment and invert levels only: 58.5 kms; - Cumulative length 58.5 kms (100 %)
Out Falls identified till date	- 3; (Subject to Change)
Road Survey	- Road Length as per OSM Planned -740 km - Completed Length up to previous week: - 77.355 km; - Completed length during the reporting period – 38.93 km; - Cumulative length 116.28 km (15.7 %)
Secondary & tertiary Drains Covered	- Completed Length up to previous week: - 38.93 km; - Completed length during the reporting period – 9.62 km; - Cumulative length 48.55 km

Inception report	- Submitted on 16/09/2026

2. Correspondence and Survey Activities

Activity	Date / Details
LiDAR survey letter submitted by PriMove to PM, C&DS	09/09/2026
LiDAR survey – drone details submitted	18/09/2026
Police permission received from CP	19/09/2026
LiDAR drone survey flying started (data acquisition)	24/09/2026
LiDAR drone survey flying completed (data acquisition)	28/09/2026
DGPS survey start date	28/08/2026
DGPS calibration report submitted	22/09/2026
Number of DGPS teams deployed	1 base station and 3 rover units
DGPS survey start date	28/08/2026
Inception report	16/09/2026
Meeting with PM, C&DS	08/10/2026
Survey Site Visit by C&DS officials	Nil
City area and Ward boundary KMZ file based on secondary data submitted to PM office for Verification from Nagar Nigam	10/10/2026
Verification received from Nagar Nigam	Nil
Survey Data submitted to PM office for Verification	Nil
Survey Verification done by PM office	07/10/2026

3. Drain Survey / Mapping Progress

Item	Progress / Details
Primary drains planned as per OSM	40.7 km (tentative; as per OSM)
Primary drains completed up to last report	40.7 km
Primary drains completed during reporting period	17.8 km (Extended survey till outfall)
Primary drains cumulative total shown	58.5 km
Road length as per OSM planned	758 km
Road Survey Completed up to last week	77.355 km
Road Survey Completed in this week	38.93 km
Cumulative length	116.28 km
Secondary drains completed up to last report	0.96 km
Secondary drains completed during reporting period	0 km
Secondary drains cumulative total shown	0.96 km
Secondary / tertiary drain areas reported	Dak Bangla, Saraswati Nagar, Lalpur, Asafabad Durgesh Nagar, Taaron Wali Bagiya, Makka Coloney, Sant Nagar, Habiba Ganj

4. Primary Drain Reaches Completed

- Rehna - nala starts from Tapa Khordun and ends at Yamuna River.
- Nal band ChouRaha nala - starts at Jheel ki puliya and finally drains into Yamuna River Via Nal band Chouraha.
- Pampa nehar - starts at daulatpur and ends at Fatehpur, Anandipur Via Bamba chouraha

5. Road Survey Completed/ongoing in wards

Ward Number	Ward Name	Area	Status
Ward No:14	Dak Bangla	0.133 sq.km	Completed
Ward No :13	Saraswati Nagar	1.500 sq.km	Completed
Ward No :21	Lalpur	1.699 sq.km	Completed
Ward No :22	Asafabad	0.421 sq.km	Completed
Ward No :47	Durgesh Nagar	0.259 sq.km	Completed
Ward No :55	Taaron Wali Bagiya	0.454 sq.km	Completed
Ward No :60	Makka Coloney	0.086 sq.km	Completed
Ward No :63	Chhaparia	0.206 sq.km	Completed
Ward No :19	Sant Nagar	1.50 sq.km	In Progress
Ward No :58	Habiba Ganj	0.246 sq.km	In Progress
Ward No: 27	Pemeshwar Gate	0.173 sq.km	In Progress

6. Survey Plan for Next Week

- **Road survey, Secondary & Tertiary Drains**

Ward Number	Ward Name	Area
Ward No :19	Satya naga	1.507 sq.km
Ward No: 50	Naya Rasoolpur	0.091 sq.km
Ward No: 58	Habibganj	0.246 sq.km


7. IMD Data Status

A formal request letter has been submitted to the India Meteorological Department (IMD), Delhi Office, for the procurement of rainfall data pertaining to Firozabad


Item	Progress / Details
Submission of request letter to IMD for IDF Curve data	28/09/2026
Payment done for IDF data	15/10/2026
Expected date for receiving IDF data	10 to 15 days


8. Photographs

Tertiary Drains

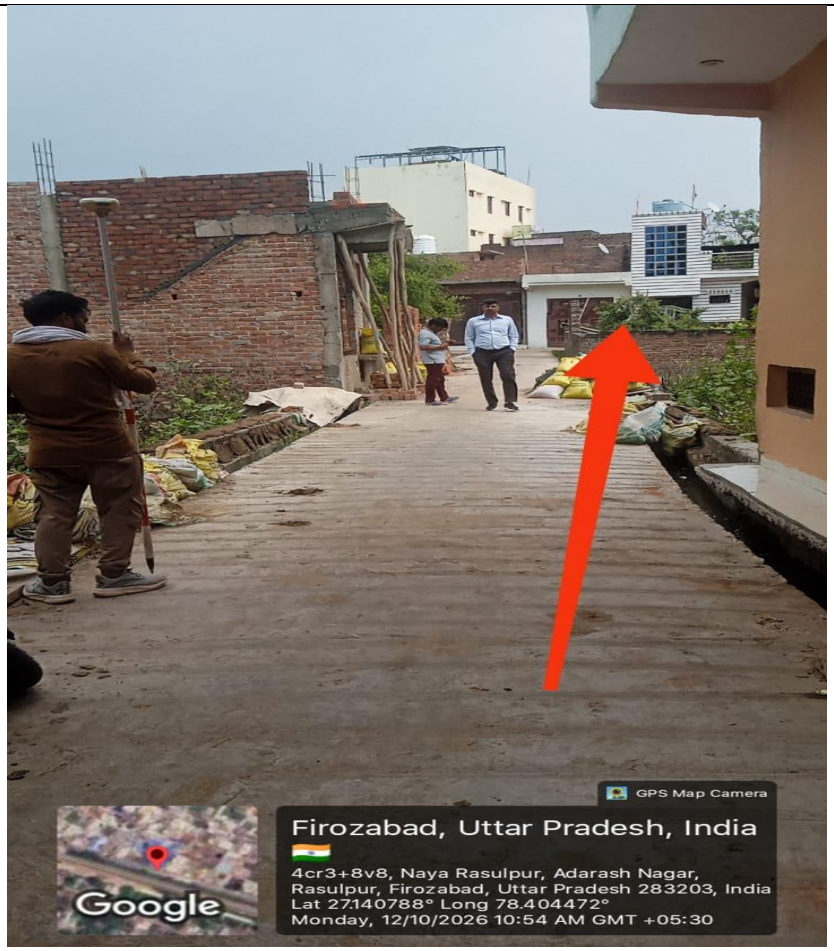



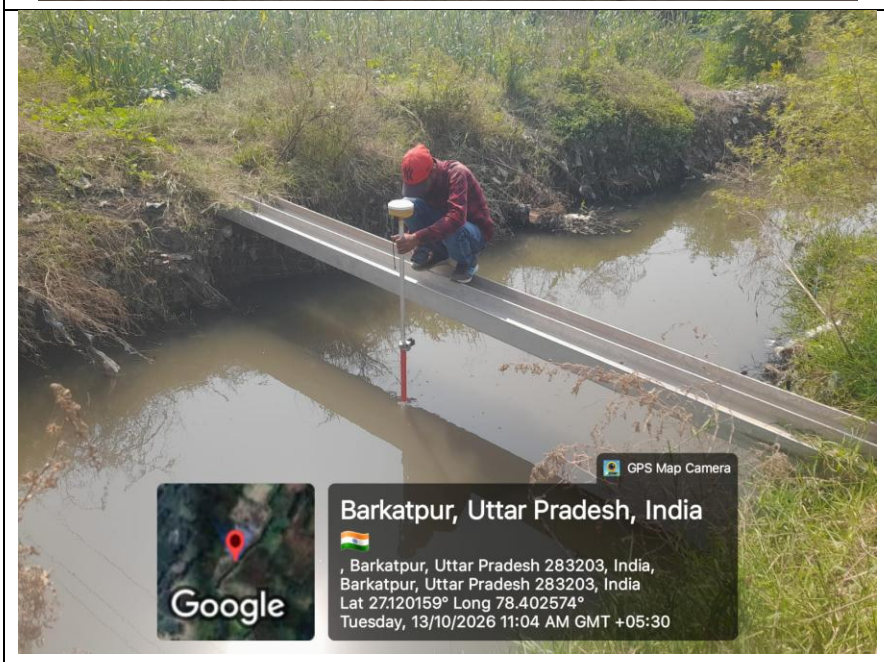

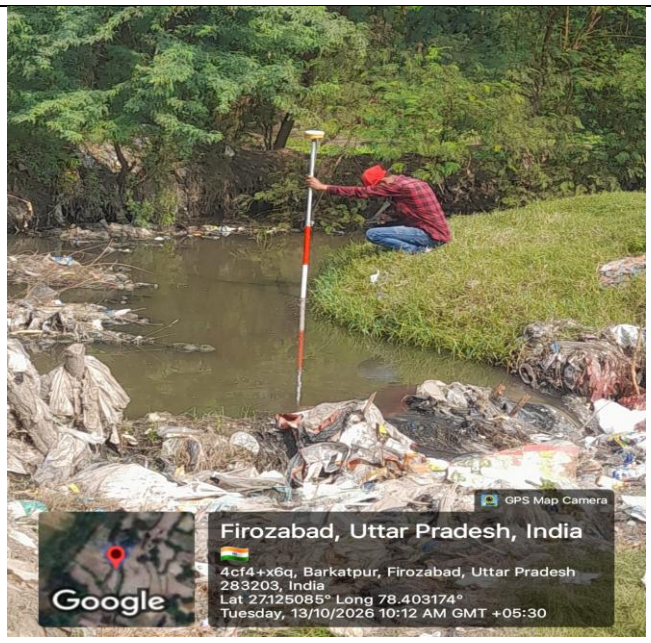

Tertiary Drains









9. Static Points Map

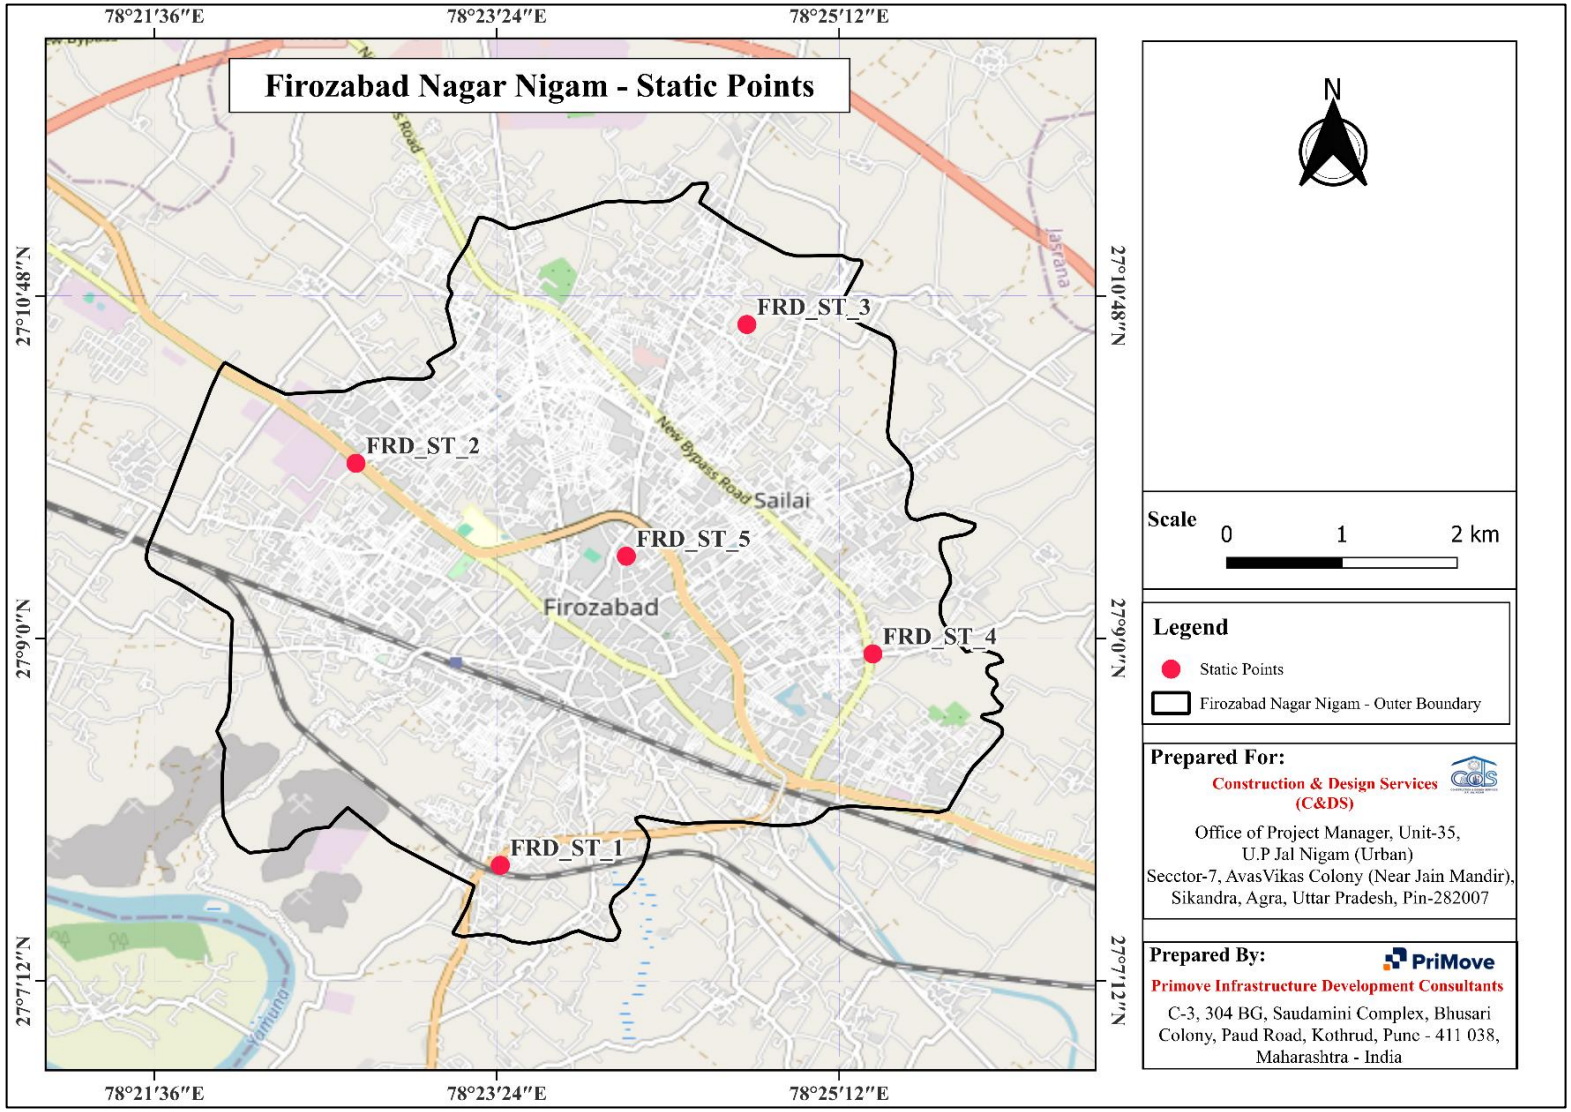


Figure 1: Firozabad Nagar Nigam – Static Points

10. GCP's Map

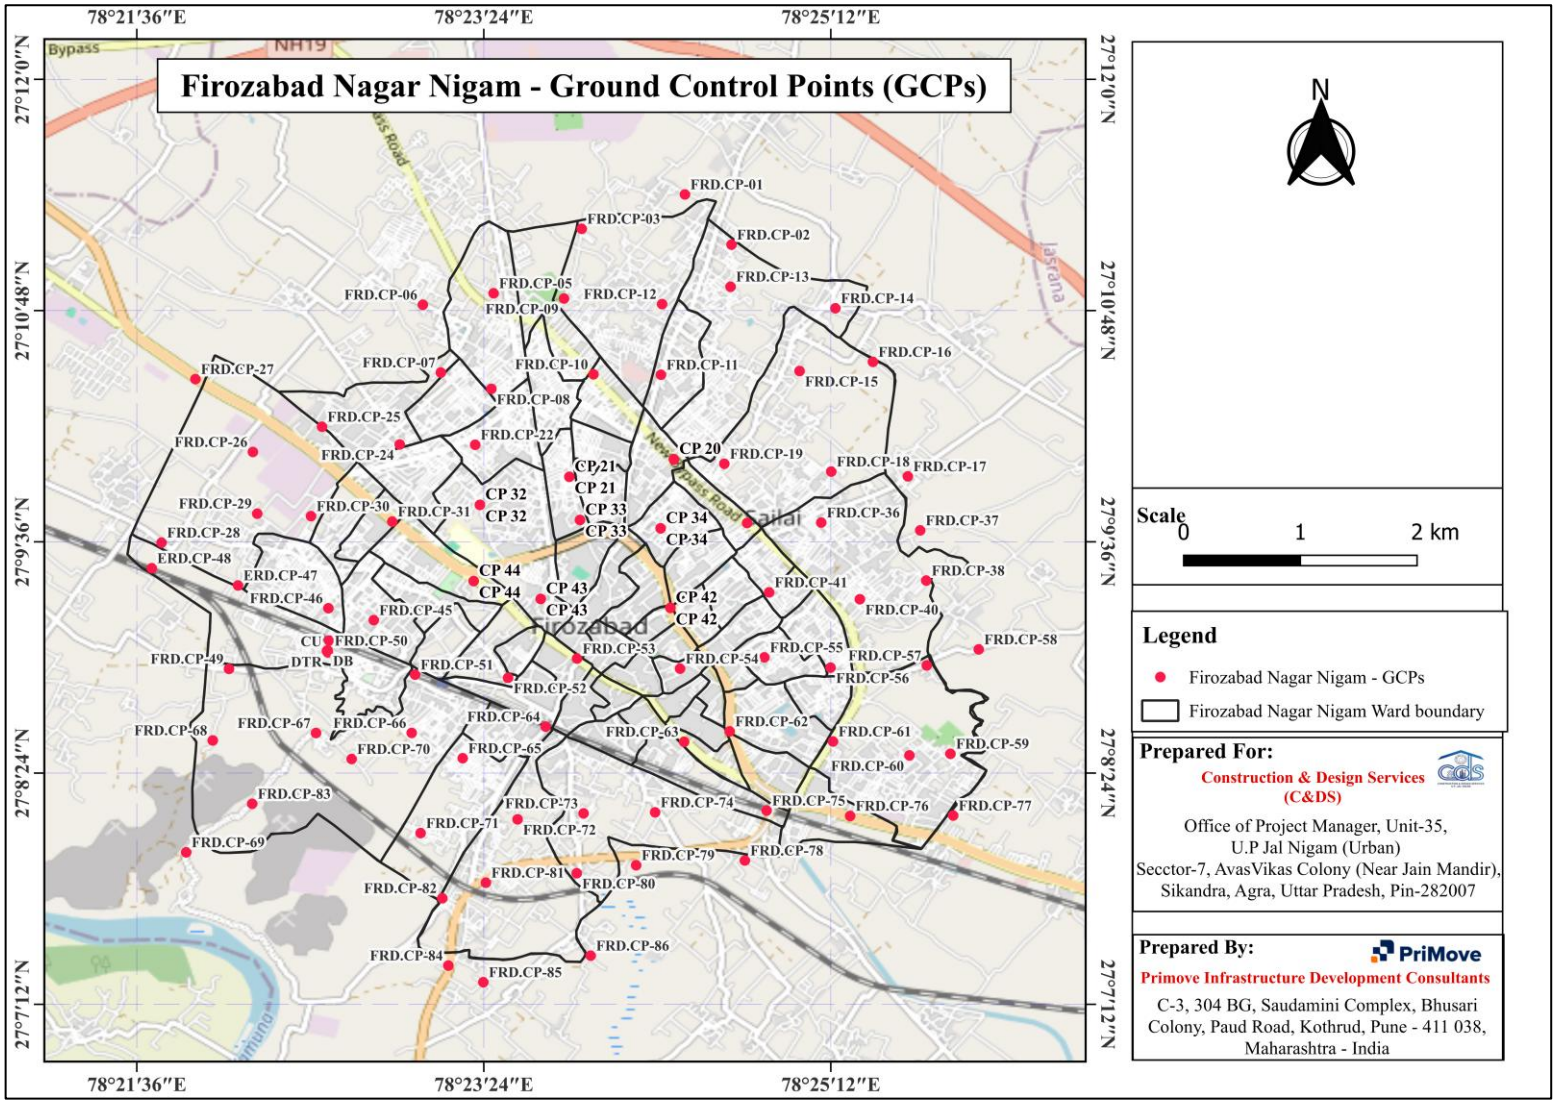


Figure 2: Firozabad Nagar Nigam – Ground Control Points (GCPs)

11. Surveyed Drains till 14th October


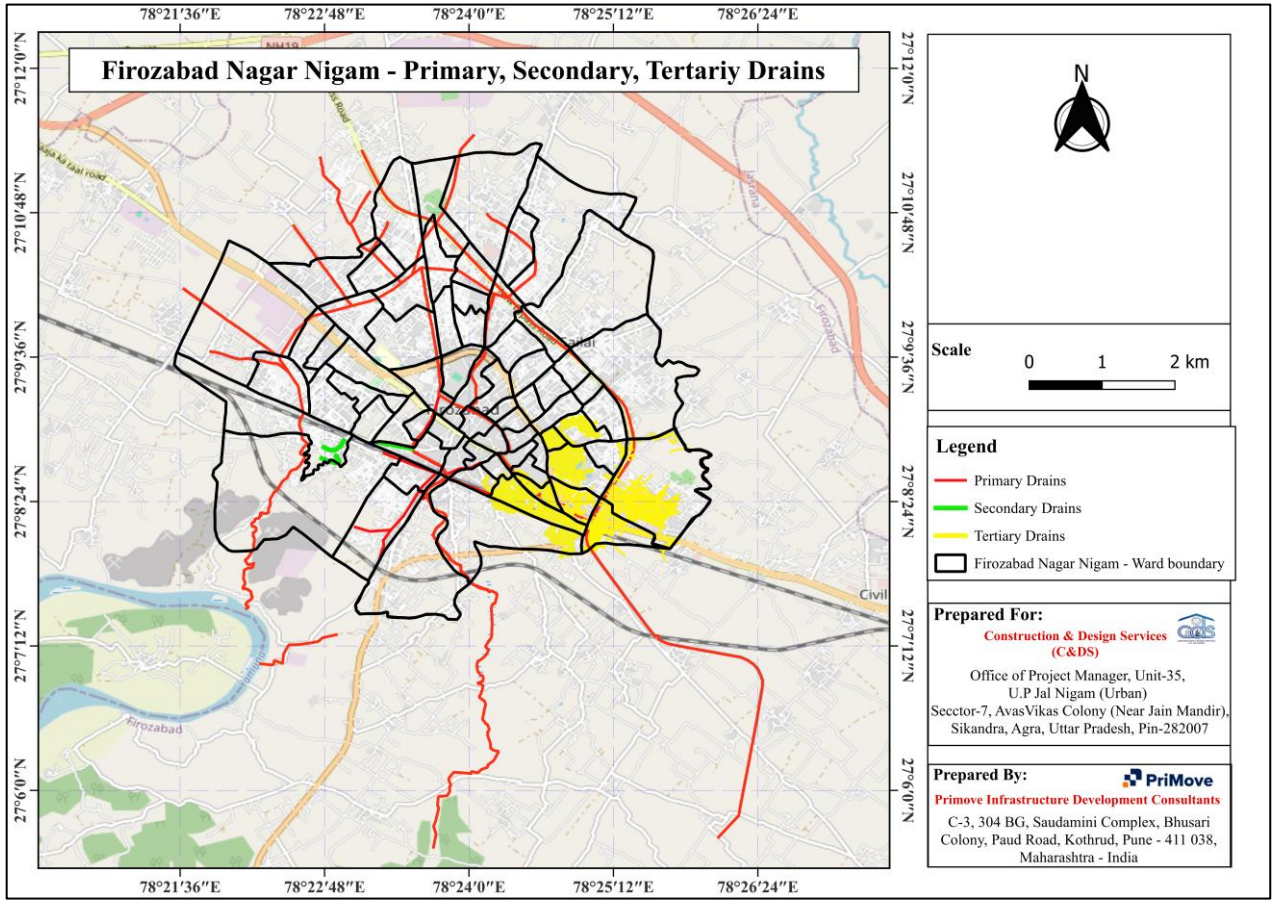


Figure 3: Survey Progress of Firozabad Nagar Nigam as on 14-10-2026

Note: Survey activities on 15th October include tertiary drain survey in the wards 19, 27 and 58 which are still in progress

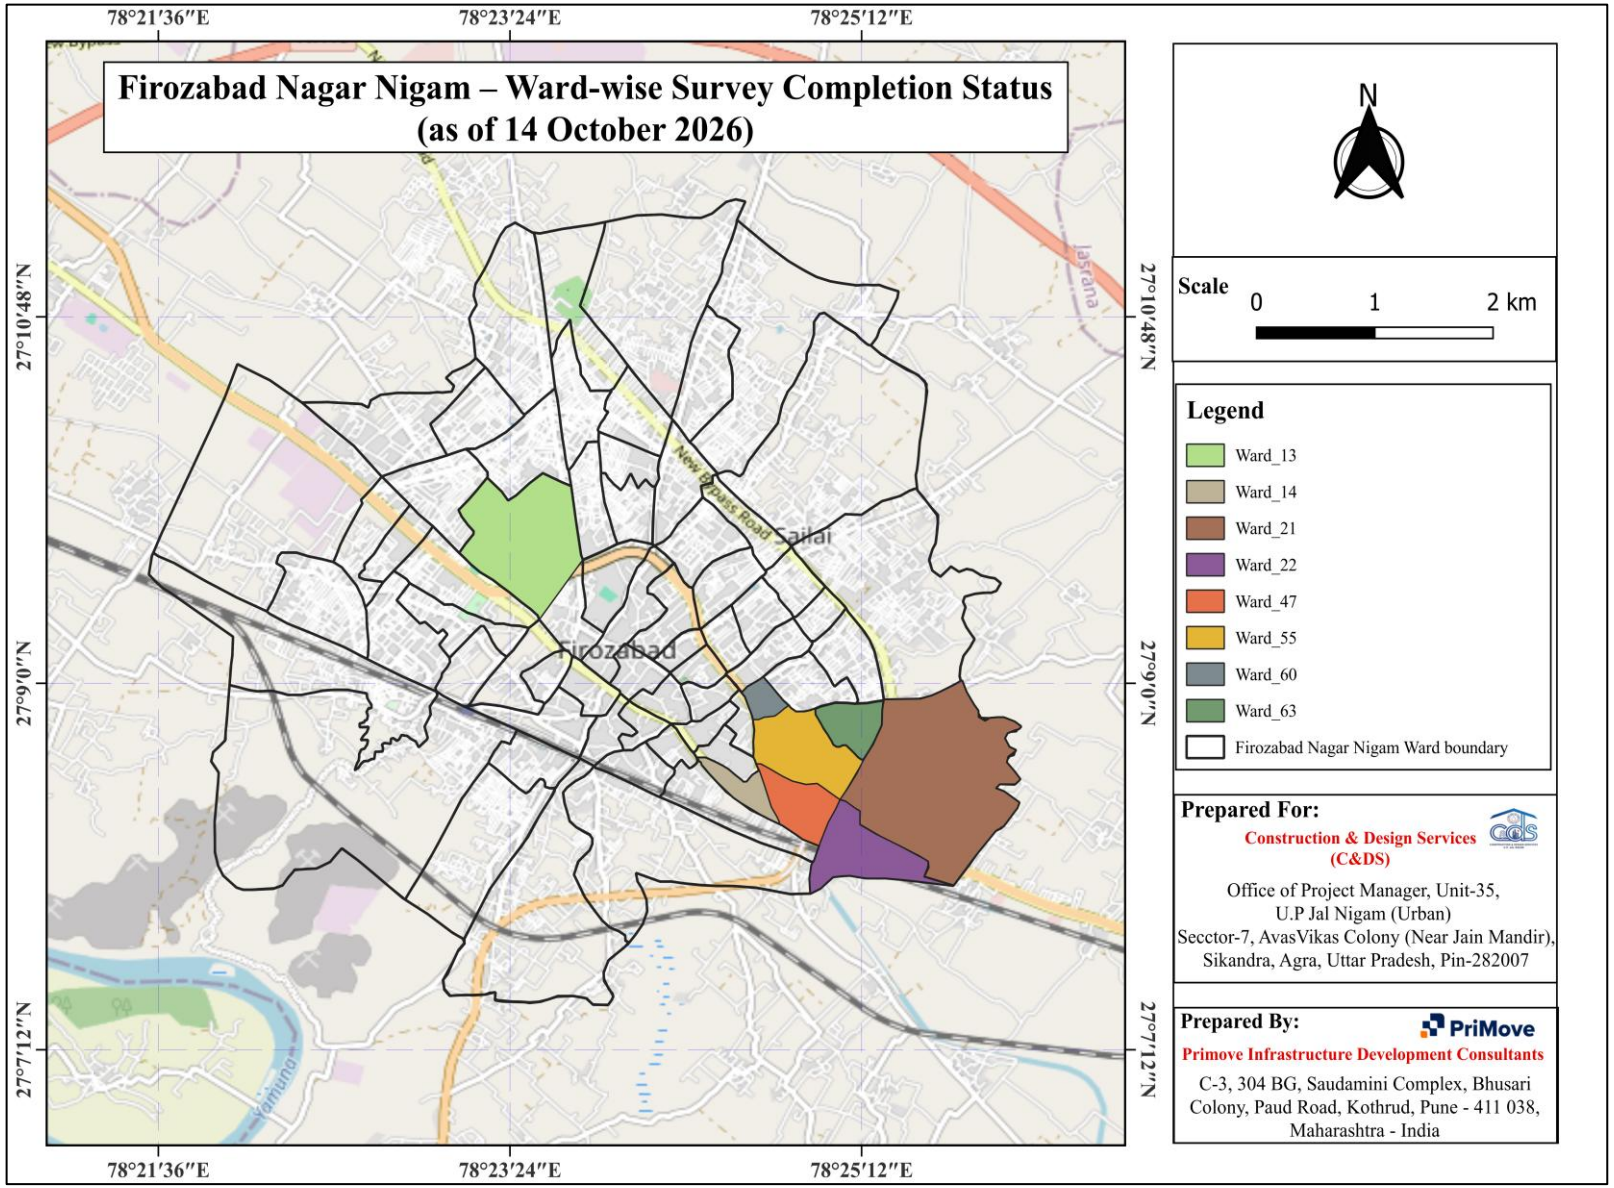

Completed Wards are colored and rest of the wards will be completed according to the ward wise schedule

Submitted by: PriMove Infrastructure Consultants Pvt. Ltd. **Date:** 16-10-2026
