Ref. No.: Pri/ /2026 Date: 23/10/2026

To,
The Project Manager,
Construction & Design Services (C&DS),
Office of Project Manager, Unit–35,
798, Sector -7 (Near Jain Temple) Awas Vikas Colony
Sikandara, Agra, Uttar Pradesh.
(Email -cdsupjn35@gmail.com)

Subject: Submission of Weekly Progress Report for Firozabad City for the period of 30/10/2026 to 05/11/2026.

Reference: 1. Letter of Acceptance (LOA) Letter No. 2473/G.M.(Ni-9)/e-Tender/2026, dated 10/08/2026 issued by C&DS, U.P. Jal Nigam.
2. Our Acknowledgement Letter no. Pri/1183/2026, dated.18.08.2026

Respected Sir,

With reference to the above-mentioned subject and the meeting held on 18th September 2026, we hereby submit the Weekly Progress Report for the period from 23rd to 29th October 2026 for your kind information

Thanking you,

PRIMOVE Infrastructure Development Consultants Pvt. Ltd. PUNE

Sunil Warade
Assistant General Manager

Encl : Weekly Progress Report

WEEKLY PROGRESS REPORT-Firozabad

Reporting Period: 30/10/2026 to 05/11/2026

Project Name: Survey, Collection of Data, Preparation of Integrated Urban Storm Water Drainage Master Plan (IUSWDMP) and other allied works for **Municipal Corporation Firozabad**, Uttar Pradesh, India

1. Progress Summary

Activity	Progress / Status
City area	35.49 sq. km **(As per RFP)** 35.08 sq.km (**As per KML**)
Static points	- Planned - 5 Nos - Completed - 5 Nos **(100%)**
GCP points	- Planned - 86 Nos - Completed - 86 Nos **(100%)**
LiDAR drone survey	- Data acquisition started on 24/09/2026 - Data acquisition Completed on 28/09/2026 - Area Covered – 35.5 Sq.km
DGPS survey	- DGPS commenced on 28/08/2026 - Deployment reported as 1 base and 3 rovers - Survey team members – 6 Nos - Calibration report submitted on 22/09/2026
Survey of Primary drains	- Completed Length: 58.5 Km; **(100 %)**
Out Falls identified till date	- 3
Road Survey	- Road Length as per OSM Planned -740 km - Completed Length up to previous week: - **197.515 km**; - Completed length during the reporting period –**43.5 kms;** - Cumulative length: **241.015 km**
Secondary & tertiary Drains Covered	- Completed Length up to previous week: - **128.785 km;** - Completed length during the reporting period – **43.5 km (Secondary: 0.989 km, Tertiary: 42.511)** - Cumulative length- **km (Secondary: 7.624 km, Tertiary: 164.661 km)**
Inception report	- Submitted on 16/09/2026

2. Correspondence and Survey Activities

Activity	Date / Details
LiDAR survey letter submitted by PriMove to PM, C&DS	09/09/2026
LiDAR survey – drone details submitted	18/09/2026

Police permission received from CP	19/09/2026
LiDAR drone survey flying started (data acquisition)	24/09/2026
LiDAR drone survey flying completed (data acquisition)	28/09/2026
DGPS survey start date	28/08/2026
DGPS calibration report submitted	22/09/2026
Number of DGPS teams deployed	1 base station and 3 rover units
DGPS survey start date	28/08/2026
Inception report	16/09/2026
Meeting with PM, C&DS	08/10/2026
Survey Site Visit by C&DS officials	07/10/2026, 17/10/2026, 02/11/2026
City area and Ward boundary KMZ file based on secondary data submitted to PM office for Verification from Nagar Nigam	10/10/2026
Survey Data submitted to PM office for Verification	07/10/2026
Survey Verification done by PM office	07/10/2026

3. Drain Survey / Mapping Progress

Item	Progress / Details
Primary drains cumulative total shown	**58.5 km (100% completed)**
Road length as per OSM planned	758 km
Road Survey Completed up to last week	**197.515 km**
Road Survey Completed in this week	43.5 km
Cumulative length	**241.015 km**
Secondary drains completed up to last report	6.635 km
Secondary drains completed during reporting period	0.989 km
Secondary drains cumulative total shown	**7.624 km**
Secondary / tertiary drain areas reported	Dak Bangla, Saraswati Nagar, Lalpur, Asafabad, Durgesh Nagar, Taaron Wali Bagiya, Makka Coloney, Sant Nagar, Habiba Ganj, Pemeshwar Gate, Basad, Nagla Gulariya, Azad Nagar, Labour Colony, Ram Nagar, Nagla Vishnu

4. Primary Drain Reaches Completed

- Rehna - nala starts from Tapa Khordun and ends at Yamuna River.
- Nal band ChouRaha nala - starts at Jheel ki puliya and finally drains into Yamuna River Via Nal band Chouraha.
- Pampa nehar - starts at daulatpur and ends at Fatehpur, Anandipur Via Bamba chouraha

5. Road Survey Completed/ongoing in wards

Ward Number	Ward Name	Area	Status
Ward No:14	Dak Bangla	0.133 sq.km	Completed
Ward No :30	Lemon Garden	0.376 sq.km	Completed
Ward No :21	Lalpur	1.699 sq.km	Completed
Ward No :22	Asafabad	0.421 sq.km	Completed
Ward No :47	Durgesh Nagar	0.259 sq.km	Completed
Ward No :55	Taaron Wali Bagiya	0.454 sq.km	Completed
Ward No :60	Makka Coloney	0.086 sq.km	Completed
Ward No :63	Chhaparia	0.206 sq.km	Completed
Ward No :19	Sant Nagar	1.50 sq.km	Completed
Ward No :58	Habiba Ganj	0.246 sq.km	Completed
Ward No: 27	Pemeshwar Gate	0.173 sq.km	Completed
Ward No: 18	Basad	1.64 sq.km	Completed
Ward No: 62	Nagla Gulariya	1.68 sq.km	Completed
Ward No: 6	Azad Nagar	0.245 sq.km	Completed
Ward No: 48	Labour Colony	1.229 sq.km	Completed
Ward No: 42	Ram Nagar	0.889 sq.km	Completed
Ward No: 45	Nagla Vishnu	3.234 sq.km	Completed

6. Survey Plan for Next Week

- **Road survey, Secondary & Tertiary Drains**

Ward Number	Ward Name	Area	Status
Ward No: 35	Nagla Bhau	0.604 sq.km	In Progress
Ward No: 36	Nagla Pachiya	0.506 sq.km	In Progress
Ward No: 25	Dholpura	2.326 sq.km	In Progress

7. IMD Data Status

A formal request letter has been submitted to the India Meteorological Department (IMD), Delhi Office, for the procurement of rainfall data pertaining to Firozabad

Item	Progress / Details
Submission of request letter to IMD for IDF Curve data	28/09/2026
Payment done for IDF data	15/10/2026
Expected date for receiving IDF data	15/11/2026

8. Photographs

Secondary & Tertiary Drains










Secondary & Tertiary Drains






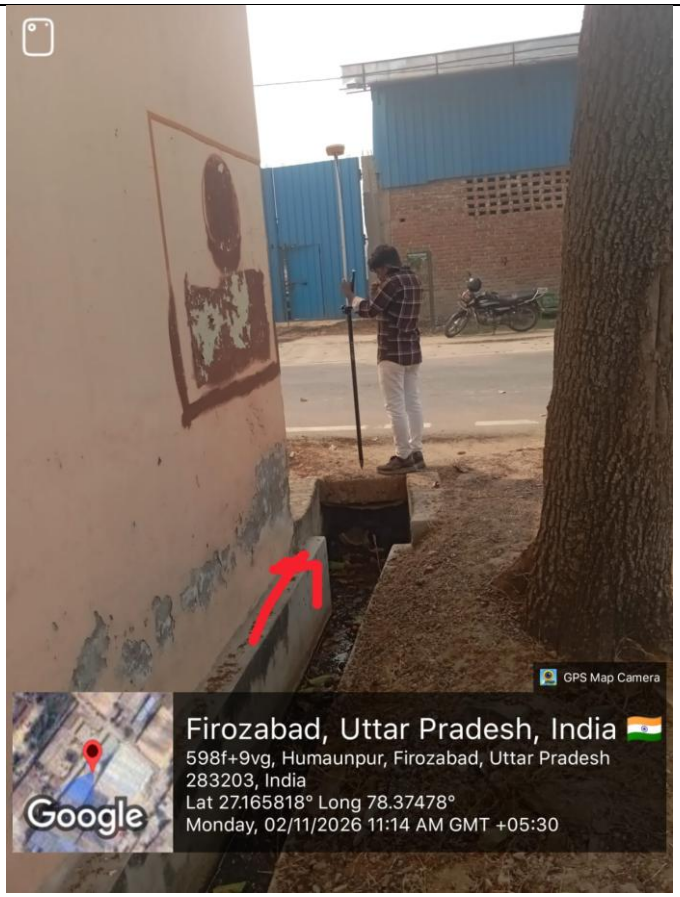



Secondary & Tertiary Drains

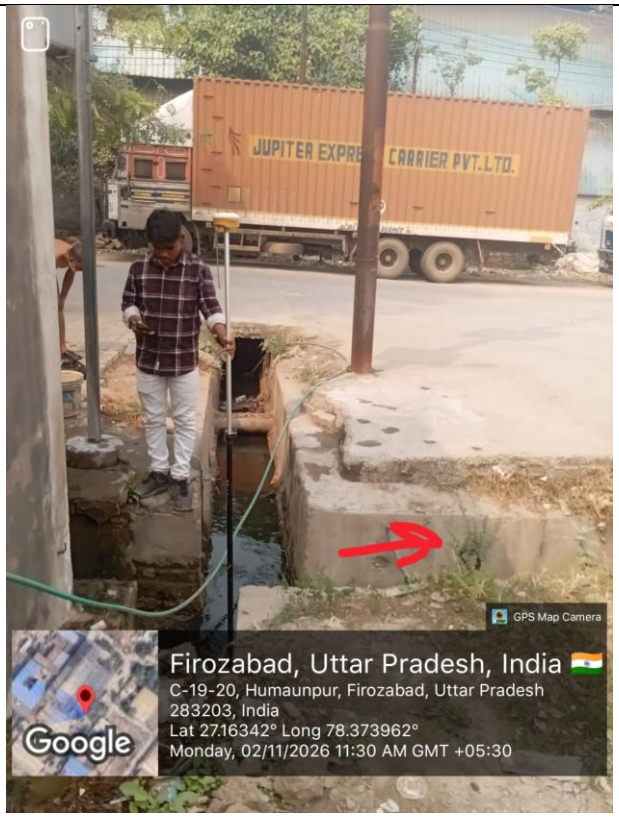







Secondary & Tertiary Drains










Secondary & Tertiary Drains



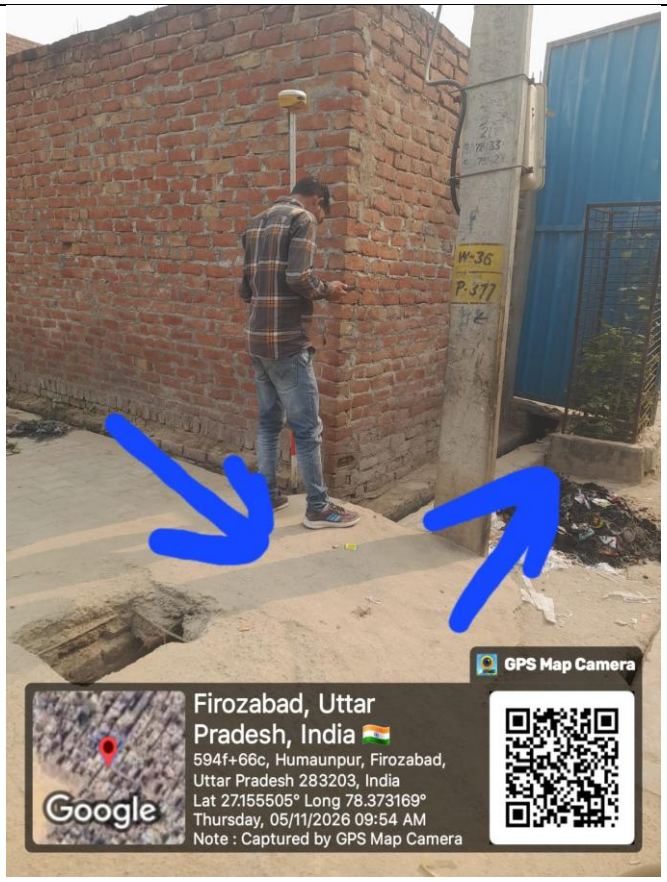

9. Static Points Map

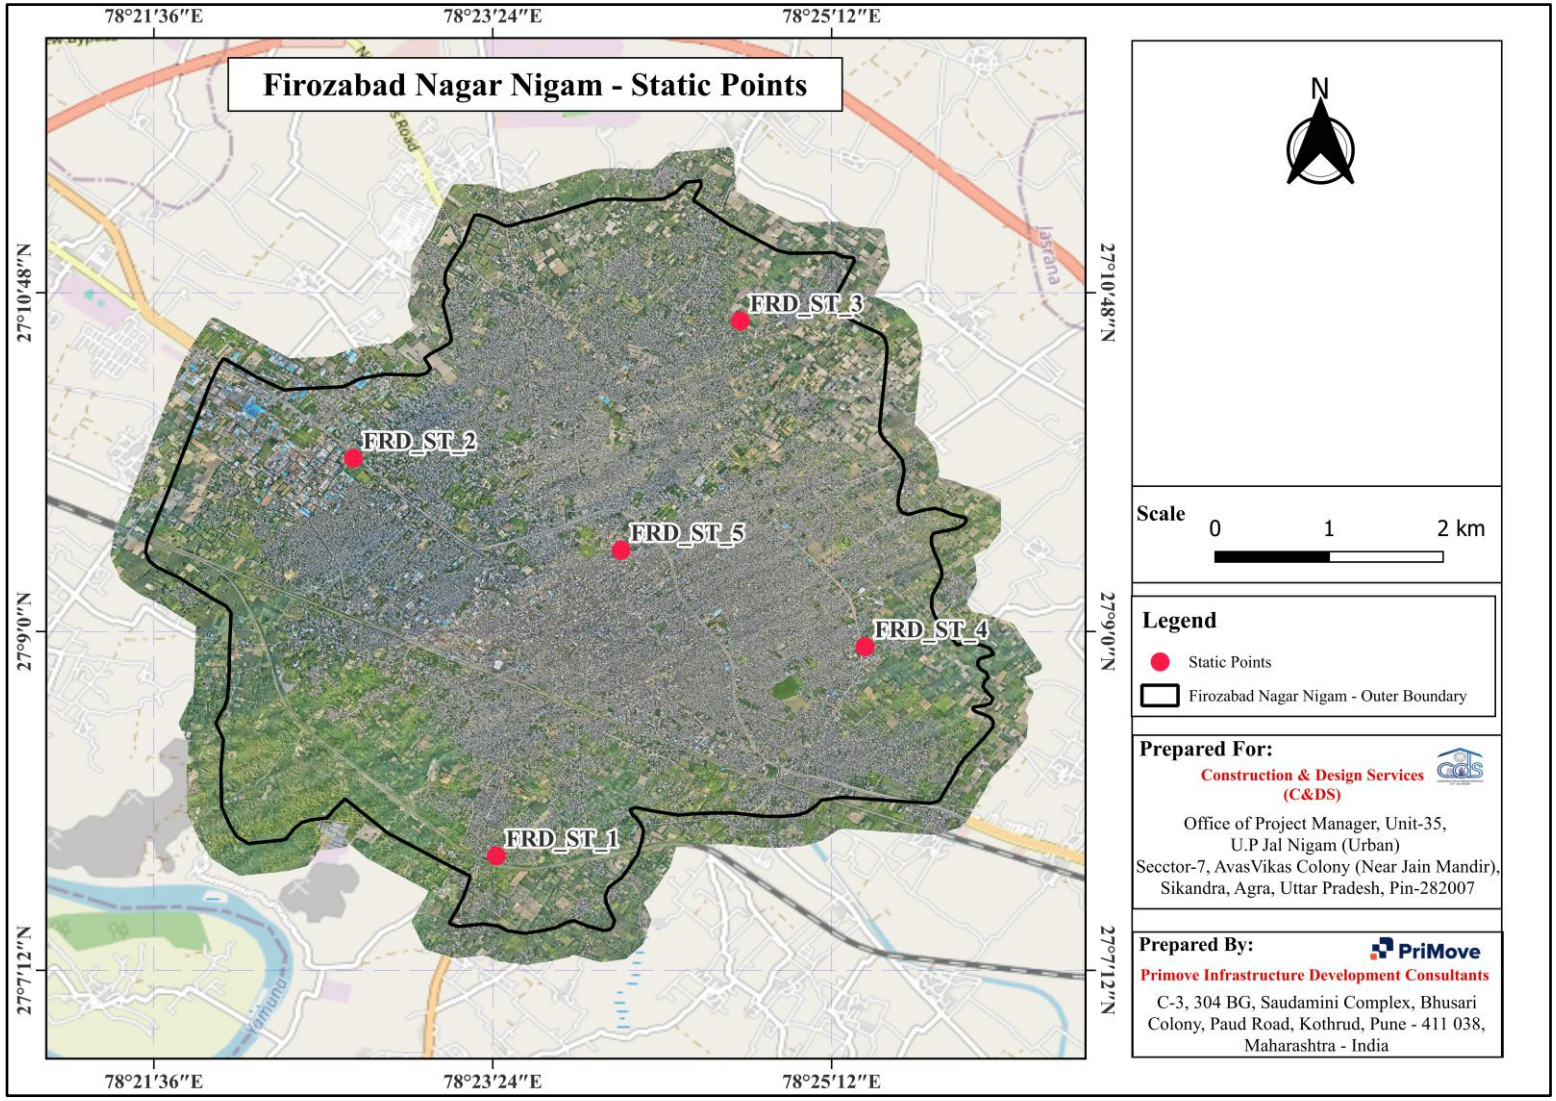


Figure 1: Firozabad Nagar Nigam – Static Points

10. GCP's Map

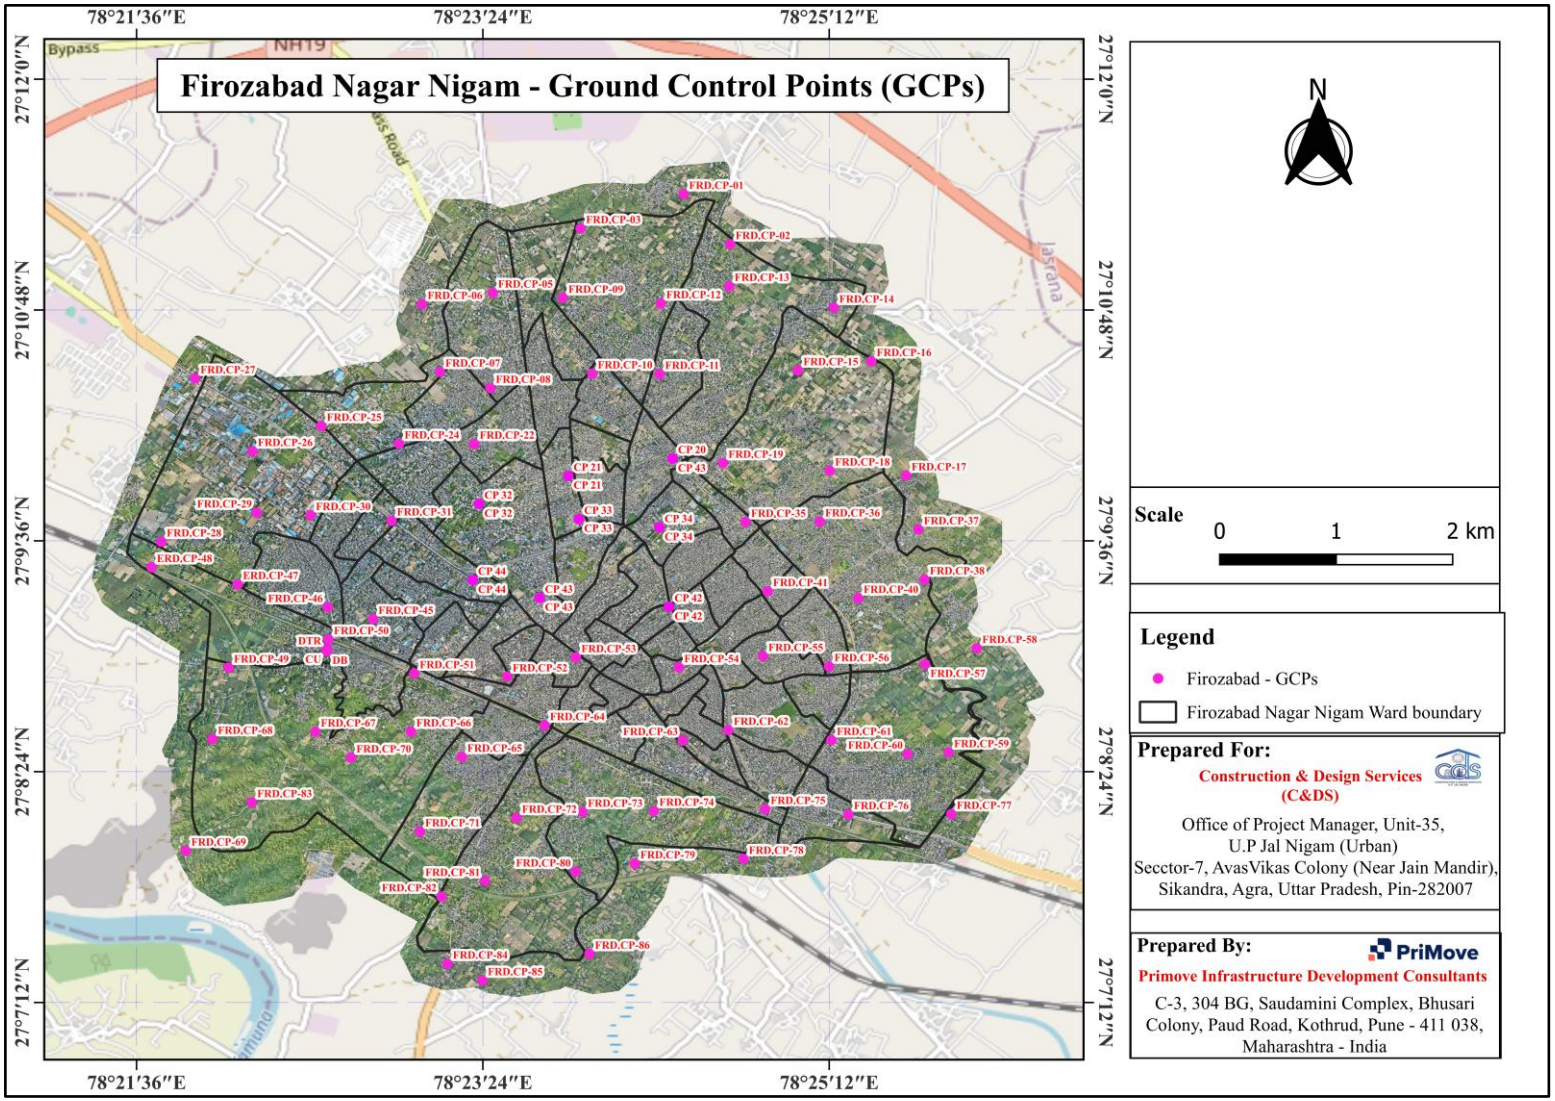


Figure 2: Firozabad Nagar Nigam – Ground Control Points (GCPs)

11. Drone Survey Flight Coverage

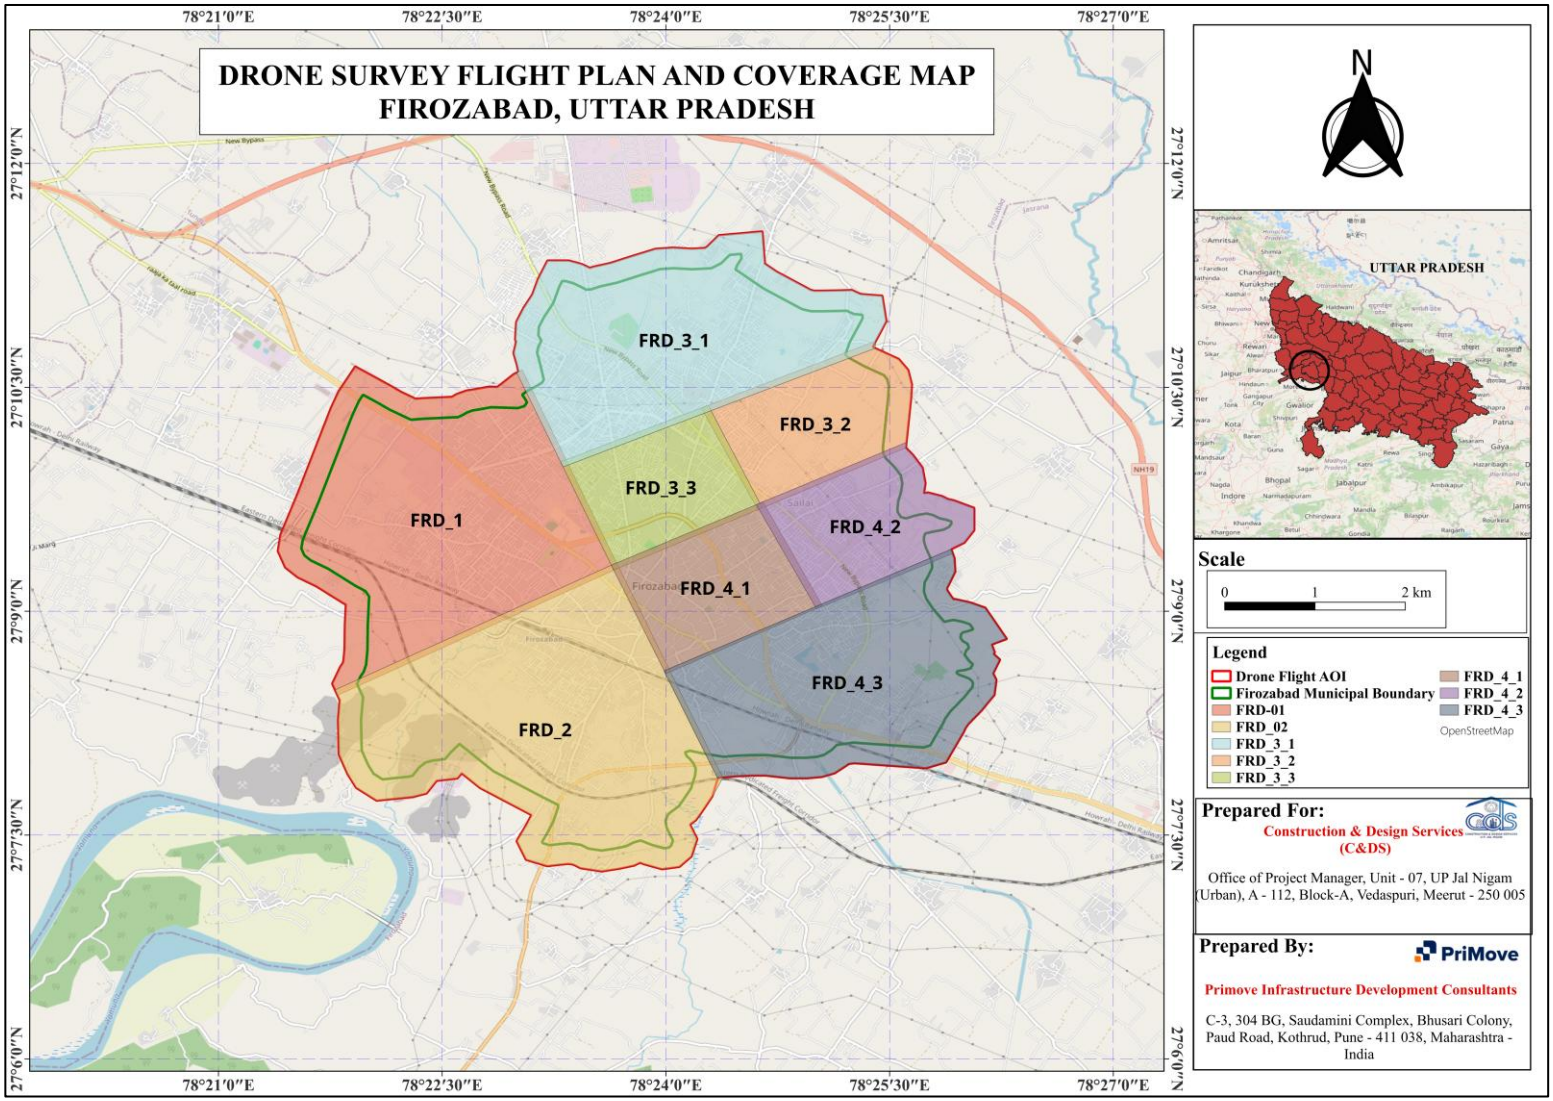


Figure 3: Drone Survey Flight Block Delineation and Acquisition Coverage Firozabad Nagar Nigam

12. Surveyed Drains till 5th November

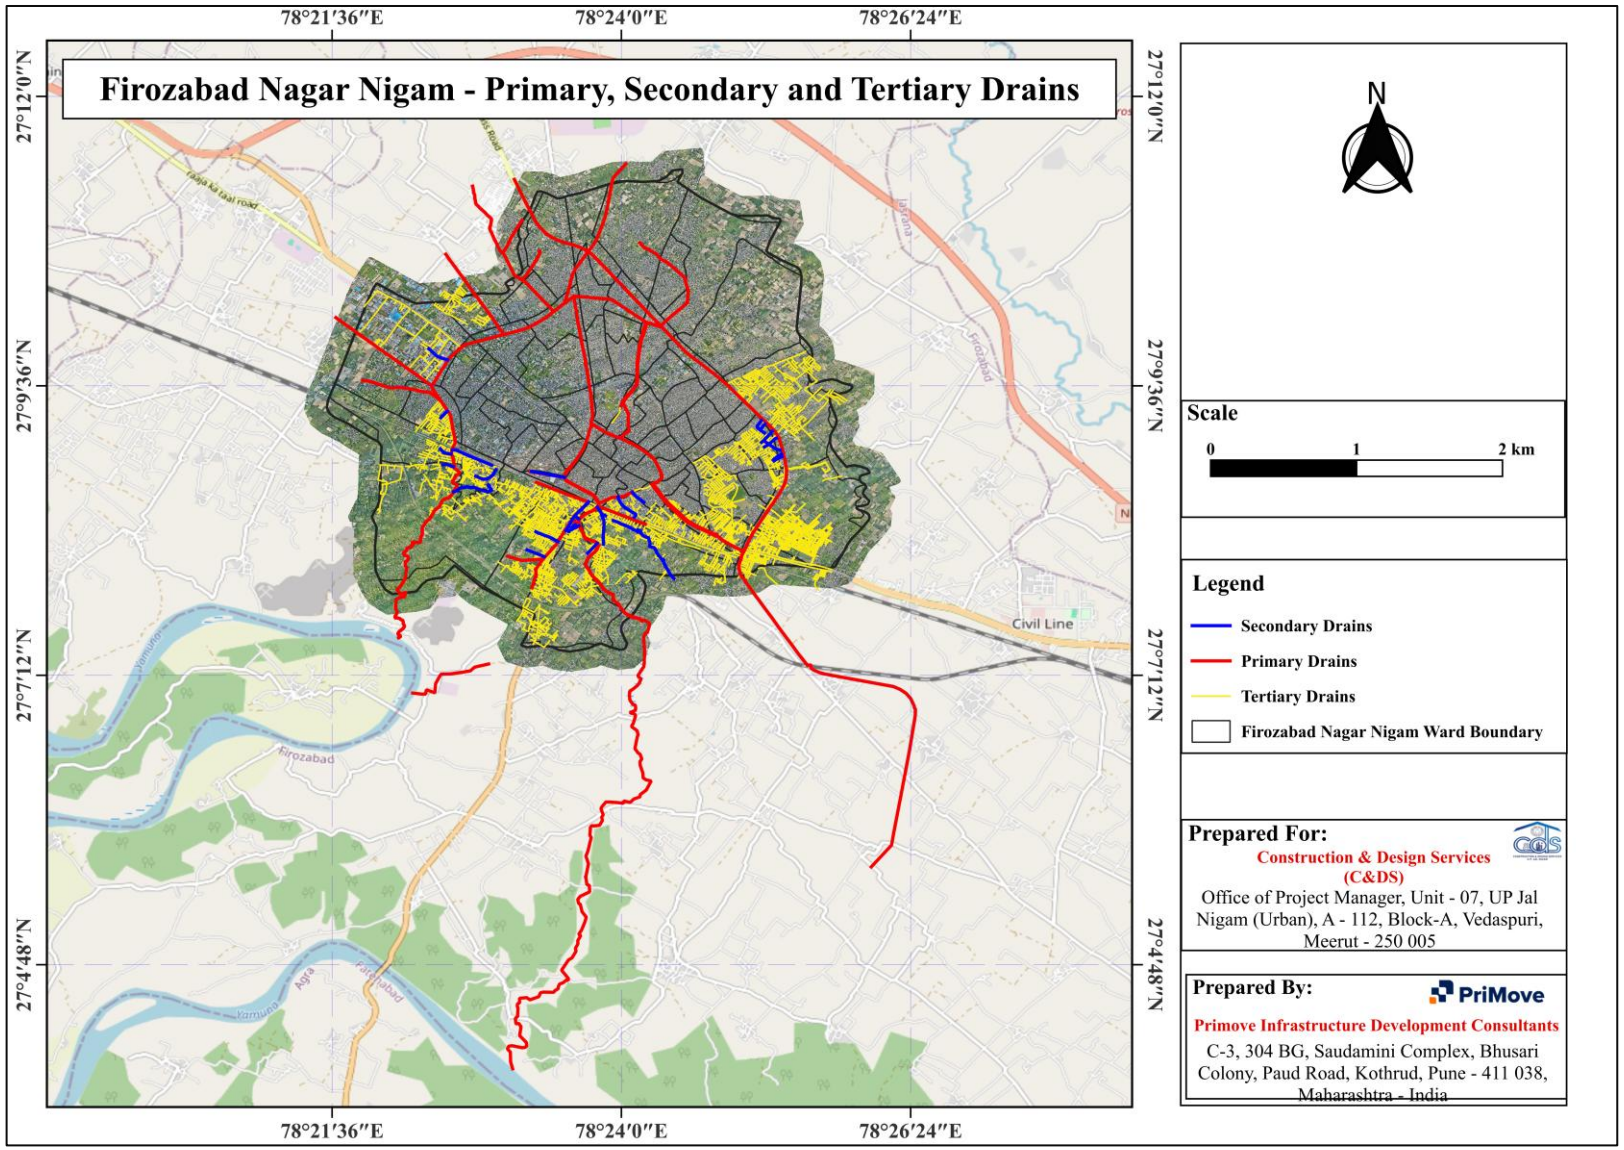


Figure 4: Survey Progress of Firozabad Nagar Nigam as on 06-11-2026

13. Ortho Rectified Image (ORI) for Firozabad

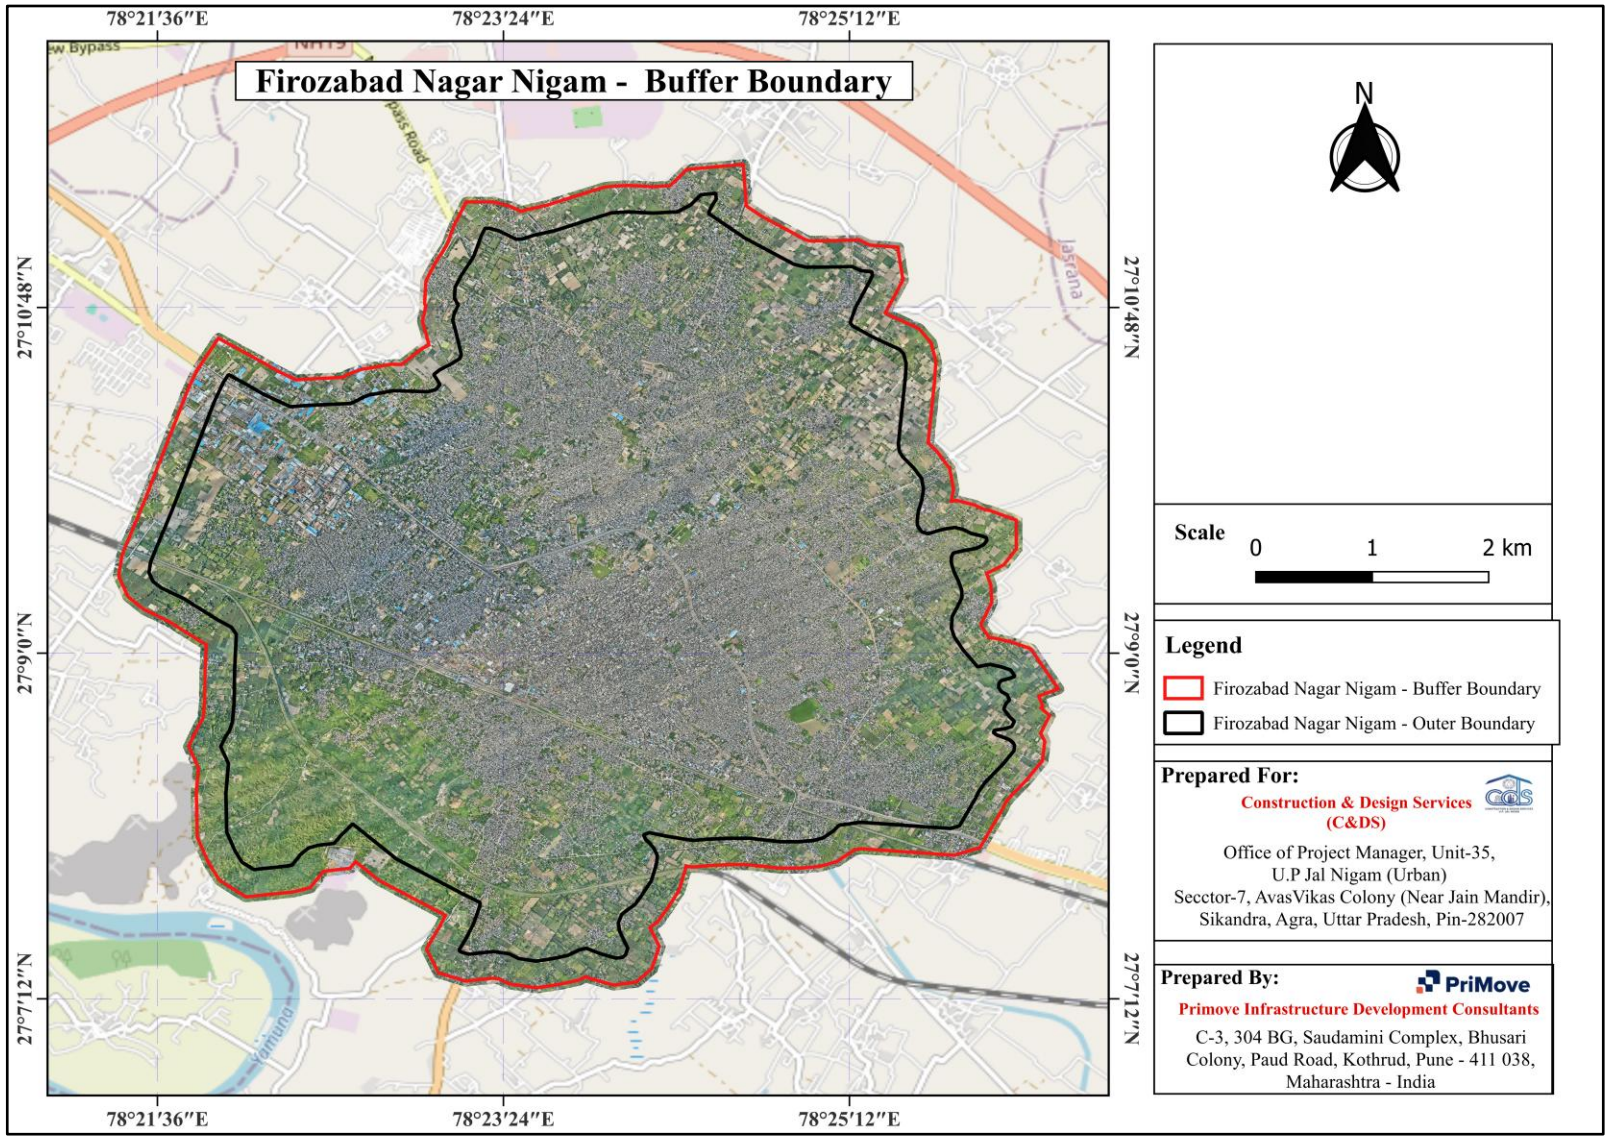


Figure 5: Firozabad Nagar Nigam – Ortho Rectified Image

14. Survey Completion Status Ward wise

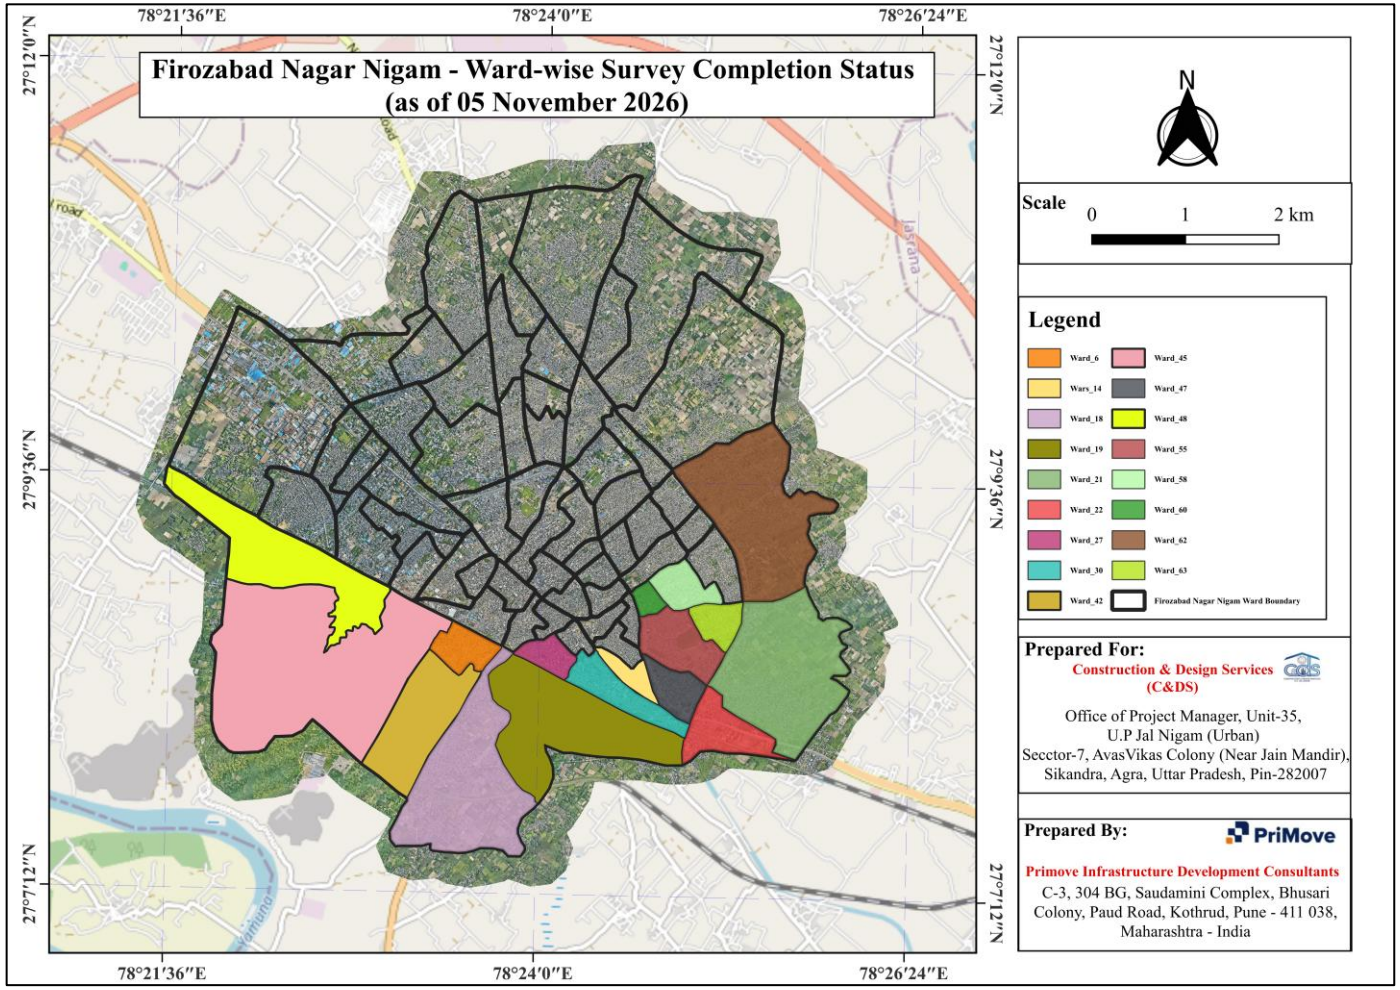


Figure 6: Survey Progress of Firozabad Nagar Nigam as on 06-11-2026

Completed Wards are colored and rest of the wards will be completed according to the ward wise schedule

Submitted by: PriMove Infrastructure Consultants Pvt. Ltd. **Date:** 06-11-2026
