Weekly Progress Review Report – GHAZIABAD

Week: 13/09/2026 to 23/09/2026

1. Survey Status

Survey Component	Total	Completed till 17th Sep 2026 (number and %)	Completed this week (number and %)	Planned for Coming Week (%)	Teams Mobilized as of today
GCPs for Drone Survey	Not Started	Nil	Not applicable	100%	Not started
Static Points for DGPS Survey	7/10	7/10; 70%	Completed	Nil	Not Started
DGPS Survey of Drains	In Progress	17 km	25 km covered (17–23 Sept)	Primary and Secondary Drain Mapping	1 DGPS Base 2 Rovers 3 Members
Drone Survey Area	sq.km	Awaiting Permission	Awaiting Permission	Tentative as permission for flying is required	Not Stared

2. Survey Progress of First Week (Till 17Th September)

a) **GCPs Marking - Nill**
b) **Static Points for DGPS Survey – 7 Points completed**
c) **DGPS Drain Survey – Covered 45 km**

3. DETAILS OF SURVEY TEAM & DGPS/ROVER EQUIPMENT – GHAZIABAD

DATE	DGPS BASE	ROVER	MEMBERS
9/9/2026	1	2	3
10/9/2026	1	2	3
11/9/2026	1	2	3
12/9/2026	1	2	3
13/9/2026	1	2	3
14/9/2026	1	2	3
15/9/2026	1	2	3
16/9/2026	1	2	3
17/9/2026	1	2	3
18/9/2026	1	2	3
19/9/2026	1	2	3
20/9/2026	1	2	3
21/9/2026	1	2	3

22/9/2026	1	2	3
23/9/2026	1	2	3
24/9/2026	1	2	3

4. DGPS Survey of Drains

DGPS-based cross-section surveying of the Ghaziabad Nagar Nigam drain network commenced on **13 September 2026** and has continued through **23 September 2026**. The survey is being carried out by the field survey teams in coordination with the **Ghaziabad base crew**. The survey includes capturing critical cross-sectional and hydraulic features such as **drain top and bottom edges, bed left and right points, bank top left and right points, manhole rim levels, culvert details, water levels, and nala top and bed points**. All survey observations are referenced to **Temporary Benchmarks (TBMs)** established from the project base station to ensure consistent and reliable elevation control across the surveyed drain network.

Date	Stretch covered (km)	Remarks
13-09-26	2.62	The Drain survey was carried out in the Wave City and Mehrauli areas
14-09-26	4.4	
15-09-26	2.6	
16-09-26	3.85	
17-09-26	3.2	
18-09-26	6.6	Primary drain survey (Nagar Nigam to Police line)
19-09-26	3.5	Primary drain survey
20-09-26	3.75	Primary drain survey (Sanjay Nagar Sec 7 to Swastik Plus Academy)
21-09-26	5.08	Swastik plus academy to lohamandi Rajnagar sec2 to rajnagar sec11 Note: Some sections could not be accessed during the survey, resulting in distances of more than 200 m between consecutive surveyed points. These inaccessible sections have been identified and marked so that necessary action will be taken in the future.
22-09-26	3.25	
23-09-26	2.8	

5. Lidar Survey - Permission Letter yet to be sent for approval.

6. Reconnaissance survey

A three-day field reconnaissance survey was carried out from 18 to 19 September 2026 by a five-member PriMove team (Manukuri Sainath, Sooryadev, Swarnima Rai, Dummu Kalyan and Dakshitha M V) covering the principal stormwater drainage corridors, major

drains, outfalls and waterlogging-prone areas within Ghaziabad Nagar Nigam, including their interface with the Hindon River. The survey focused on assessing existing drainage conditions, hydraulic constraints, outfall conditions and key waterlogging hotspots to support the subsequent DGPS/topographic survey and hydraulic modelling. Detailed observations are presented in the Reconnaissance Survey chapter of the Inception Report, with a summary of the key findings provided below.

i) Survey Programme

Day	Date	Area / Corridor	Major Activities
Day 1	18 Sept 2026	RDC Nala & Sahaberi Nala corridors	Reconnaissance of **RDC Nala and Sahaberi Nala**, including inspection of drain continuity, feeder/secondary drains, culverts and crossings, visible choking/siltation, local drainage constraints and waterlogging-prone locations. The ongoing **DGPS/topographic survey activities** were also observed.
Day 2	19 Sept 2026	Raj Nagar Extension – Hindon River outfall corridor	Inspection of the **outfall discharging towards the Hindon River**, drainage network in the **Raj Nagar Extension** area, and the **canal/drain connection leading to the Hindon River**. Existing crossings, drainage connectivity, hydraulic constraints and surrounding waterlogging-prone areas were also reviewed.

7. Instrument Calibration

The DGPS equipment deployed for the survey has been calibrated and is within the validity period. The calibration certificate has been submitted as supporting documentation for the survey equipment to the concerned Project Manager in charge.

8. Report Status

Report	Status	Comments
Inception Report	Report submitted to Project Manager	Sent on 16th September 2026

9. Static Points



Figure 1 Survey Static Point ST-01 Karhera Colony



Figure 2 Survey Static Point ST-02 Rajnagar Extension



Figure 3 Survey Static Point ST-03 Gokuldham Colony



Figure 4 Survey Static Point ST-04 Piplehda



Figure 5 Survey Static Point ST-05 Wave City



Figure 6 Survey Static Point ST-06 Vijaya Nagar

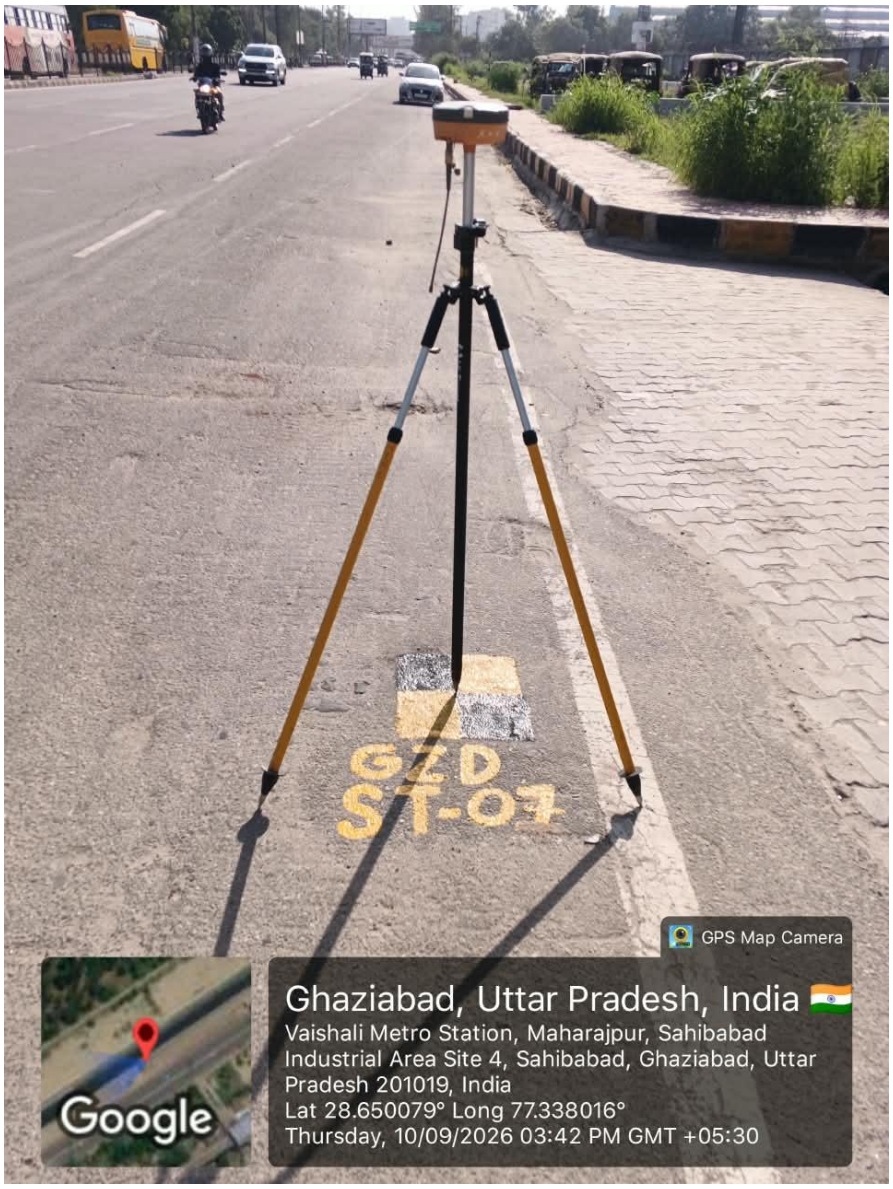


Figure 7 Survey Static Point ST-07 Vaishali Metro station

10. Site Survey Photographs of Second Week (Till 23rd September)




GPS Map Camera
Google
Ghaziabad, Uttar Pradesh, India
Jfxh+xrm, Shahpur, Shahpur Bamheta, Ghaziabad, Uttar Pradesh 201002, India
Lat 28.649897° Long 77.479387°
Thursday, 17/09/2026 10:42 AM GMT +05:30


GPS Map Camera
Google
Ghaziabad, Uttar Pradesh, India
Jfxh+vq7, Jaipuriya, Crossings Republik, Ghaziabad, Uttar Pradesh 201002, India
Lat 28.649805° Long 77.479389°
Thursday, 17/09/2026 10:43 AM GMT +05:30

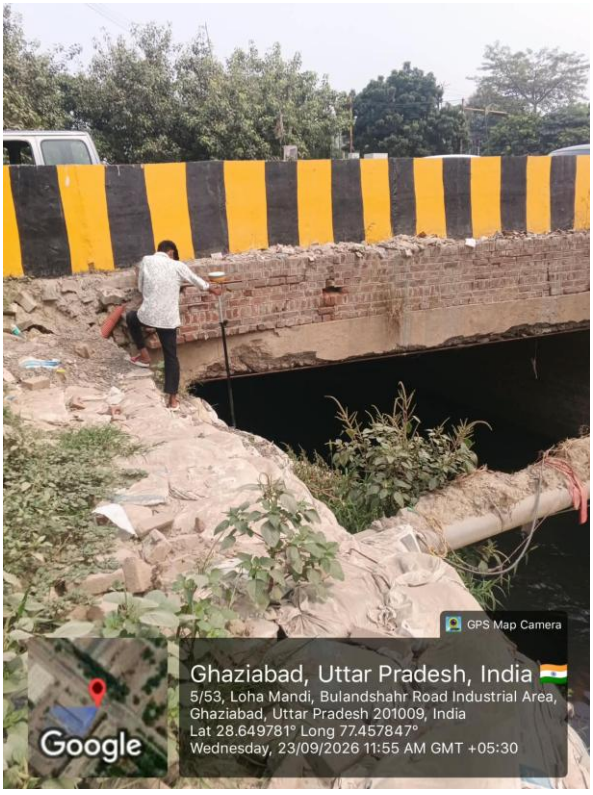

GPS Map Camera
Google
Ghaziabad, Uttar Pradesh, India
E115, Loha Mandi, Bulandshahr Road Industrial Area, Ghaziabad, Uttar Pradesh 201009, India
Lat 28.649961° Long 77.458178°
Wednesday, 23/09/2026 12:31 PM GMT +05:30


GPS Map Camera
Google
Ghaziabad, Uttar Pradesh, India
Jfv2+4qc, Upsidc Industrial Area, Bulandshahr Road Industrial Area, Ghaziabad, Uttar Pradesh 201009, India
Lat 28.64274° Long 77.451873°
Wednesday, 23/09/2026 03:25 PM GMT +05:30

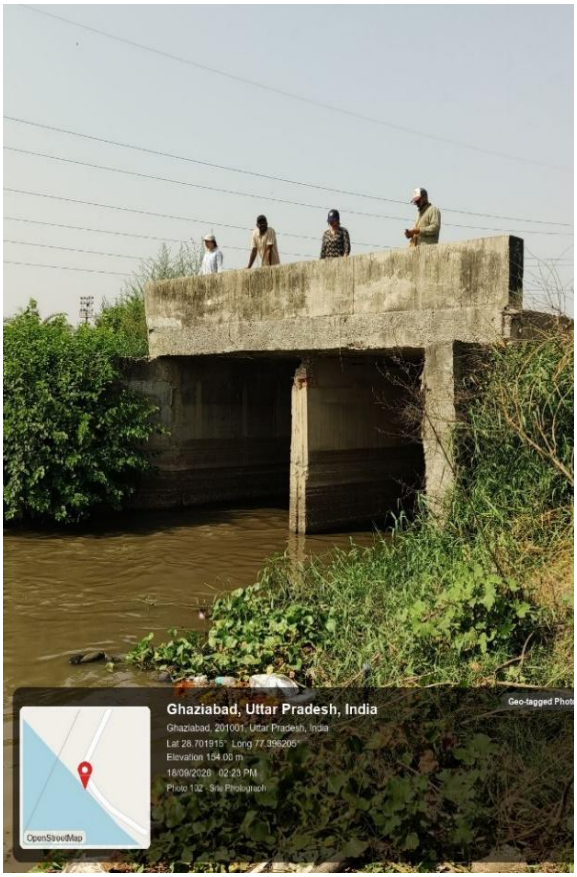

GPS Map Camera
Google
Ghaziabad, Uttar Pradesh, India
Jcpw+89, Sector 13, Bulandshahr Road Industrial Area, Ghaziabad, Uttar Pradesh 201009, India
Lat 28.636162° Long 77.445832°
Wednesday, 23/09/2026 05:35 PM GMT +05:30


GPS Map Camera
Google
Ghaziabad, Uttar Pradesh, India
5/53, Loha Mandi, Bulandshahr Road Industrial Area, Ghaziabad, Uttar Pradesh 201009, India
Lat 28.649685° Long 77.457775°
Wednesday, 23/09/2026 11:54 AM GMT +05:30


GPS Map Camera
Google
Ghaziabad, Uttar Pradesh, India
5/53, Loha Mandi, Bulandshahr Road Industrial Area, Ghaziabad, Uttar Pradesh 201009, India
Lat 28.649772° Long 77.457886°
Wednesday, 23/09/2026 11:56 AM GMT +05:30

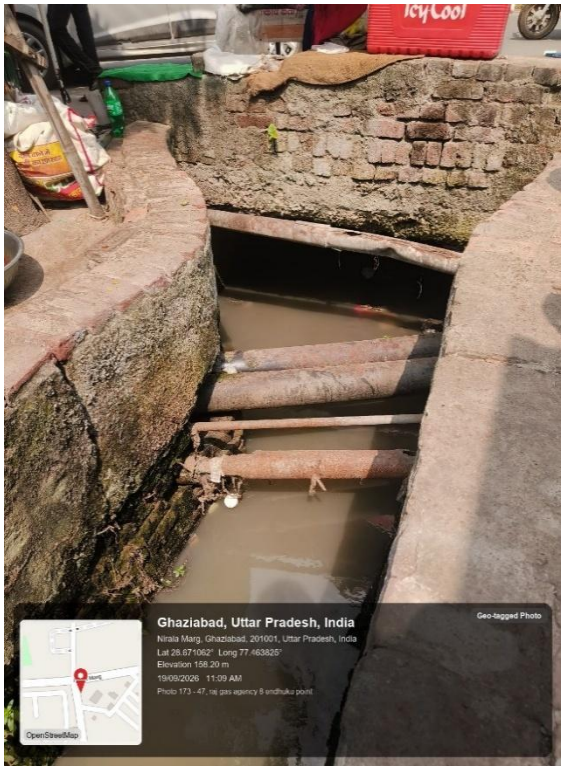

GPS Map Camera
Google
Ghaziabad, Uttar Pradesh, India
5/53, Loha Mandi, Bulandshahr Road Industrial Area, Ghaziabad, Uttar Pradesh 201009, India
Lat 28.649781° Long 77.457847°
Wednesday, 23/09/2026 11:55 AM GMT +05:30

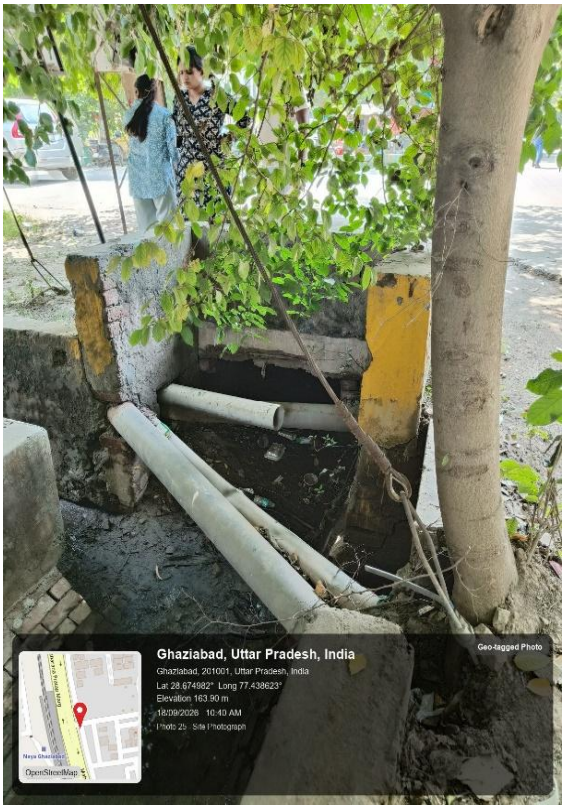
11. Photographic Documentation of Field Reconnaissance










Ghaziabad, Uttar Pradesh, India
Ghaziabad, 201001, Uttar Pradesh, India
Lat 28.674982° Long 77.438623°
Elevation 163.90 m
16/09/2026 10:40 AM
Photo 25 - Site Photograph
Geo-tagged Photo
OpenStreetMap


संजीव झा
पूर्व महानगर मंत्री
राघव टॉक
भाजपा कार्यकर्ता
मोहित टॉक
भाजपा कार्यकर्ता
Ghaziabad, Uttar Pradesh, India
Ghaziabad, 201001, Uttar Pradesh, India
Lat 28.679473° Long 77.460632°
Elevation 171.60 m
16/09/2026 11:02 AM
Photo 34 - RDC Nala starting point
Geo-tagged Photo
OpenStreetMap
