WEEKLY PROGRESS REPORT-GHAZIABAD

Reporting Period: 07/10/2026 to 13/10/2026

Project Name: Survey, Collection of Data, Preparation of Integrated Urban Storm Water Drainage Master Plan (IUSWDMP) and other allied works for **Municipal Corporation Ghaziabad**, Uttar Pradesh, India

1. Progress Summary

Activity	Progress / Status
City area	171 sq. km
Static points	- Planned - 8 Nos - Completed - 8 Nos (100%)
GCP points	- Planned - 540 Nos - Completed - 0 Nos
LiDAR drone survey	- Permission Letter yet to be submitted
LiDAR drone survey Area excluded due to restricted area	- 80% is in red zone
DGPS survey	- DGPS commenced on 13/09/2026 - Deployment reported as 1 base and 2 rovers - Survey team members – 3 Nos - Calibration report submitted on 22/09/2026
Survey of Primary drains	- Primary Drains As per OSM Planned – 223 km - Completed Length up to previous week: 69.28 Km - Completed length during the reporting period – 16.3 km; - Cumulative length 75.2 km (33.72%) - Surveyed with alignment and invert levels only: 30 km - Surveyed for alignment: 45 km
Out Falls identified till date	- Shahberi Nala Outfall - Raj Nagar Extension Outfall - Outfall near Hindon Ghat
Road Survey	- Road Length as per OSM Planned -3450 km - Completed Length up to previous week: 95.9 Km - Completed length during the reporting period 5.9 km; - Cumulative length 101.8 km
Secondary /tertiary Drains Covered	- Completed Length up to previous week: 26.62 Km - Completed length during the reporting period: 0km; - Cumulative length 26.62 km
Inception report	- Submitted on 16/09/2026

2. Correspondence and Survey Activities

Activity	Date / Details

LiDAR survey letter submitted by PriMove to PM, C&DS	Yet to be Submitted
LiDAR survey – drone details submitted	-
Police permission received from CP	-
LiDAR drone survey flying started (data acquisition)	-
LiDAR drone survey flying completed (data acquisition)	-
DGPS survey start date	13/09/2026
DGPS calibration report submitted	22/09/2026
Number of DGPS teams deployed	1 base station and 2 rover units
DGPS survey start date	13/09/2026
Inception report	16/09/2026
Meeting with PM, C&DS	29/09/2026
Survey Site Visit by C&DS officials	-

3. Drain Survey / Mapping Progress

Item	Progress / Details
Primary drains planned as per OSM	223 km (tentative; as per OSM)
Primary drains completed up to last report	69.28 km
Primary drains completed during reporting period	16.3 km
Primary drains cumulative total shown	75.2 km
Road length as per OSM planned	3450 km
Road Survey Completed up to last week	95.9 km
Road Survey Completed in this week	16.3km
Cumulative length	101.8 km
Secondary/Tertiary drains completed up to last report	26.62 km
Secondary/Tertiary drains completed during reporting period	0 km
Secondary/ Tertiary drains cumulative total shown	26.62 km
Secondary / tertiary drain areas reported	Sadarpur Residential Area, Mehrauli/Aditya World City Road (nh-24/NH-9 ke pass), Shani Mandir Road, wave City

4. Primary Drain Reaches Completed

- Raj Nagar Extension Nala
- Shahberi Nala
- Dasna- Kushaliya Nala
- RDC Nala
- Lal Kuan Nala
- Sikrod Nala
- Loha Mandi Nala
- Hapur Chungi Nala

- Sanajay Nagar Main Drain

5. Road Survey Completed/ongoing in wards

- 101.8 km has been covered


6. Survey Plan for Next Week

- **Primary drains**
  - RDC Nala Inver levels need to be Rechecked/Resurveyed
  - Depth checks need to be performed at Hapur Chungi, Chipyana to Sadarpur, and Shahid Sthal to Navjivan Ashram.


7. IMD Data Status

A formal request letter has been submitted to the India Meteorological Department (IMD), Delhi Office, for the procurement of rainfall data pertaining to Ghaziabad.

8. Surveyed Drains till 12th October 2026

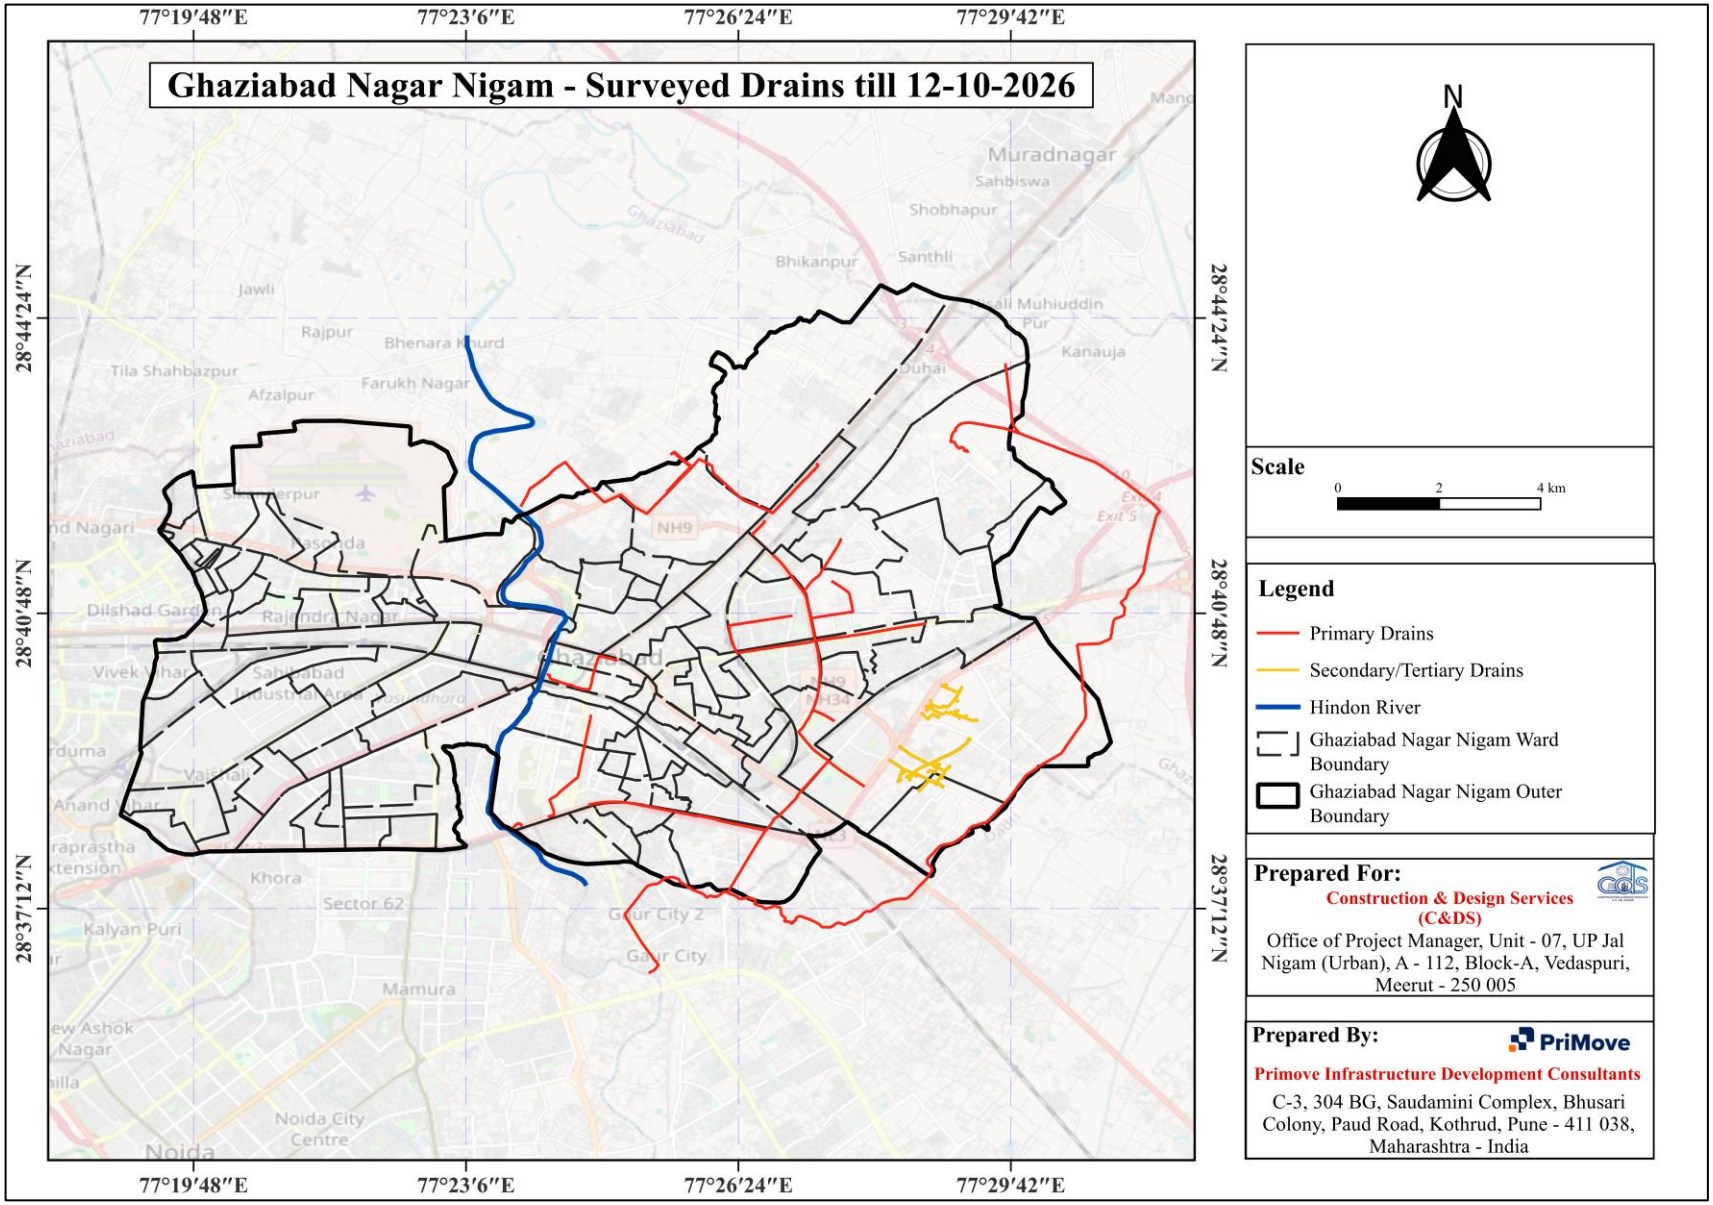

9. DGPS Static Points

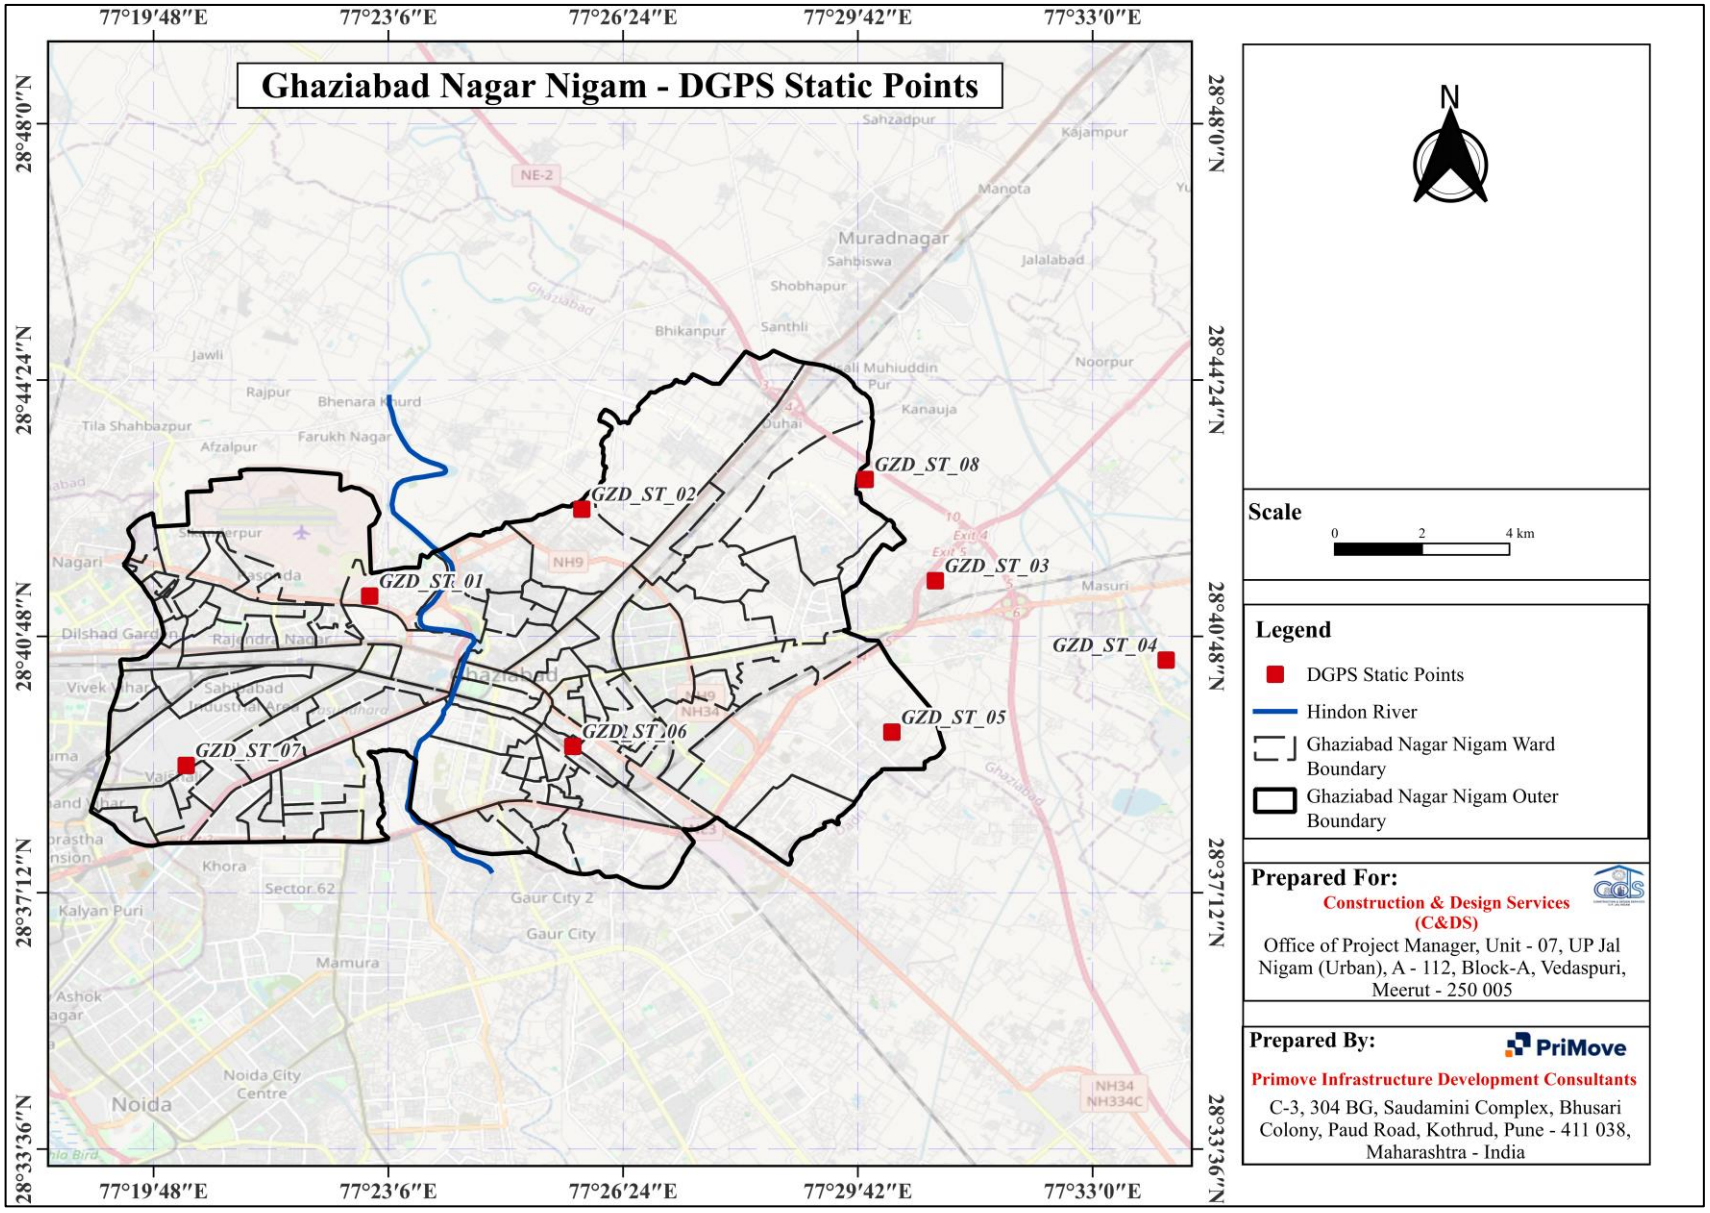


6. Photographs

Primary Drains







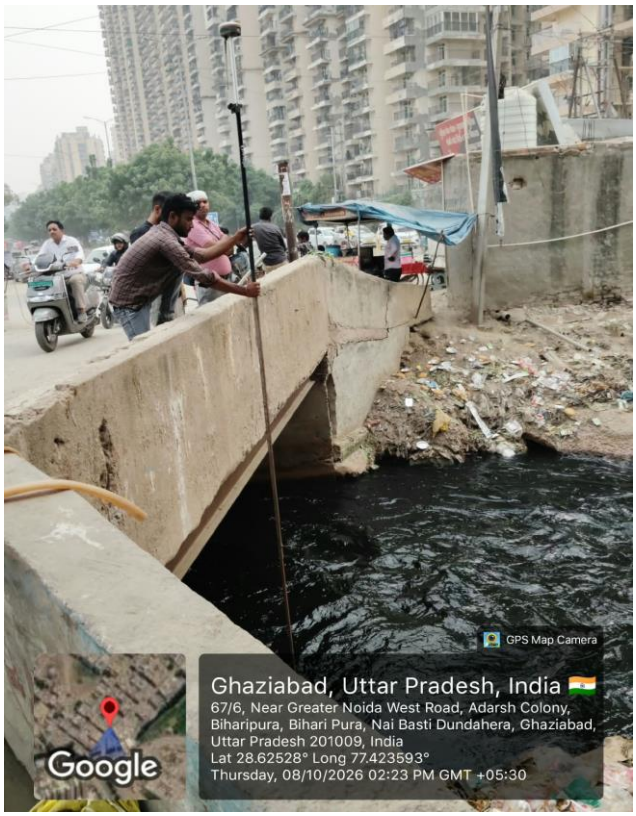

Primary Drains









Primary Drains









Submitted by: PriMove Infrastructure Consultants Pvt. Ltd. **Date:** 14/10/2026
