Ref. No.: Pri/ /2026 Date: 23/10/2026

To,

The Project Manager,

Construction & Design Services (C&DS),

Office of Project Manager, Unit– 7,

A-212, Vedvyaspuri Colony, Near Subharti University

Meerut, Uttar Pradesh. (Email -cds.unit7@gmail.com)

Subject: Submission of Weekly Progress Report for Ghaziabad City for the period of 16 to 22/10/2026.

Reference: 1. Letter of Acceptance (LOA) Letter No. 2473/G.M.(Ni-9)/e-Tender/2026, dated 10/08/2026 issued by C&DS, U.P. Jal Nigam.
2. Our Acknowledgement Letter no. Pri/1183/2026, dated.18.08.2026

Respected Sir,

With reference to the above-mentioned subject and the meeting held on 18th September 2026, we hereby submit the Weekly Progress Report for the period from 16th to 22nd October 2026 for your kind information

PRIMOVE Infrastructure Development Consultants Pvt. Ltd. PUNE

Thanking you,

Sunil Warade

Assistant General Manager

Encl : Weekly Progress Report

WEEKLY PROGRESS REPORT-GHAZIABAD

Reporting Period: 16/10/2026 to 22/10/2026

Project Name: Survey, Collection of Data, Preparation of Integrated Urban Storm Water Drainage Master Plan (IUSWDMP) and other allied works for **Municipal Corporation Ghaziabad**, Uttar Pradesh, India

- **Progress Summary**

Activity	Progress / Status
City area as per RFP	225 sq. km
City area as per KML	171 sq. km
Static points	• Planned - 6 Nos • Completed - 6 Nos (100%)
LiDAR survey	• Status – To be carried out using helicopter-mounted LiDAR. Agency finalization is under process
DGPS survey	• DGPS commenced on 13/09/2026 • Deployment reported as 1 base and 2 rovers • Survey team members – 3 Nos • Calibration report submitted on 22/09/2026
Survey of Primary drains	• Primary Drains As per OSM Planned - 223 km • Completed Length up to previous week - 75.2 Km • Completed length during the reporting period taking Invert Levels – 14.9km; • Cumulative length - 83 km (37.2%) • Surveyed with alignment and invert levels – 54.9 km • Surveyed for alignment - 28 km
Out Falls identified till date	• Shahberi Nala Outfall • Raj Nagar Extension Outfall • Outfall near Hindon Ghat
Road Survey	• Road Length as per OSM Planned - 3450 km • Completed Length up to previous week – 101.8 Km • Completed length during the reporting period 7.9 km;

	• Cumulative length – 109.7 km
Secondary /tertiary Drains Covered	• Completed Length up to previous week - 26.62 Km • Completed length during the reporting period - 0km; • Cumulative length - 26.62 km
Inception report	• Submitted 16/09/2026

- **Correspondence and Survey Activities**

Activity	Date / Details
DGPS survey start date	13/09/2026
DGPS calibration report submitted	22/09/2026
Number of DGPS teams deployed	1 base station and 2 rover units
Inception report	16/09/2026
Meeting with PM, C&DS	29/09/2026
Survey Site Visit by C&DS officials	-

- **Drain Survey / Mapping Progress**

Item	Progress / Details
Primary drains planned as per OSM	223 km (tentative; as per OSM)
Primary drains completed up to last report	75.2 km
Primary drains completed during reporting period	7.8 km
Primary drains cumulative total shown	83 km
Survey completed for alignment	83 km
Survey completed with alignment and invert levels	54.9 km
Road length as per OSM planned	3450 km
Road Survey Completed up to last week	101.8 km
Road Survey Completed this week	7.8 km
Cumulative length	109.7 km
Secondary/Tertiary drains completed up to last report	26.62 km
Secondary/Tertiary drains completed during reporting period	0 km
Secondary/ Tertiary drains cumulative total shown	26.62 km
Secondary / tertiary drain areas reported	Sadarpur Residential Area, Mehrauli/Aditya World City Road, Shani Mandir Road, Wave City, Balle Market,01,Shahpur Bamheta.

- **Primary Drain Reaches Completed**
- Raj Nagar Extension Nala

- Shahberi Nala
- Dasna- Kushaliya Nala
- RDC Nala
- Lal Kuan Nala
- Sikrod Nala
- Loha Mandi Nala
- Hapur Chungi Nala
- Sanajay Nagar Main Drain

- **Survey Plan for Next Week**
- **Primary drains**
- RDC Nala, Shahberi Nala, Chipyana to Sadarpur, Shahid Sthal to Navjivan Ashram Invert levels will be taken.

- **IMD Data Status**

- A formal request letter has been submitted to the India Meteorological Department (IMD), Delhi Office, for the procurement of rainfall data pertaining to Ghaziabad.

Item	Progress / Details
Submission of request letter to IMD for IDF Curve data	Submitted on 28/09/2026
Payment for IDF data	Completed on 15/10/2026
Expected date for receiving IDF data	10 to 15 days

-


-

- **Classification and Distribution of Surveyed Utility Points (17th -20th October 2026)**


• Utilities	• Description	• Number of Points
• Trees	• Trees and Tree-offset points	• 308

• Electric	• Poles, transformers, lines, signal, electric box	• 381
• Water	• Water tank, tower, hand pump	• 42
• Buildings	• Buildings, shop, rooms, boundary wall	• 77
• Landmarks	• Temple, statue, police post. Gate, signboard	• 16

- **Survey Progress till 22nd October 2026**

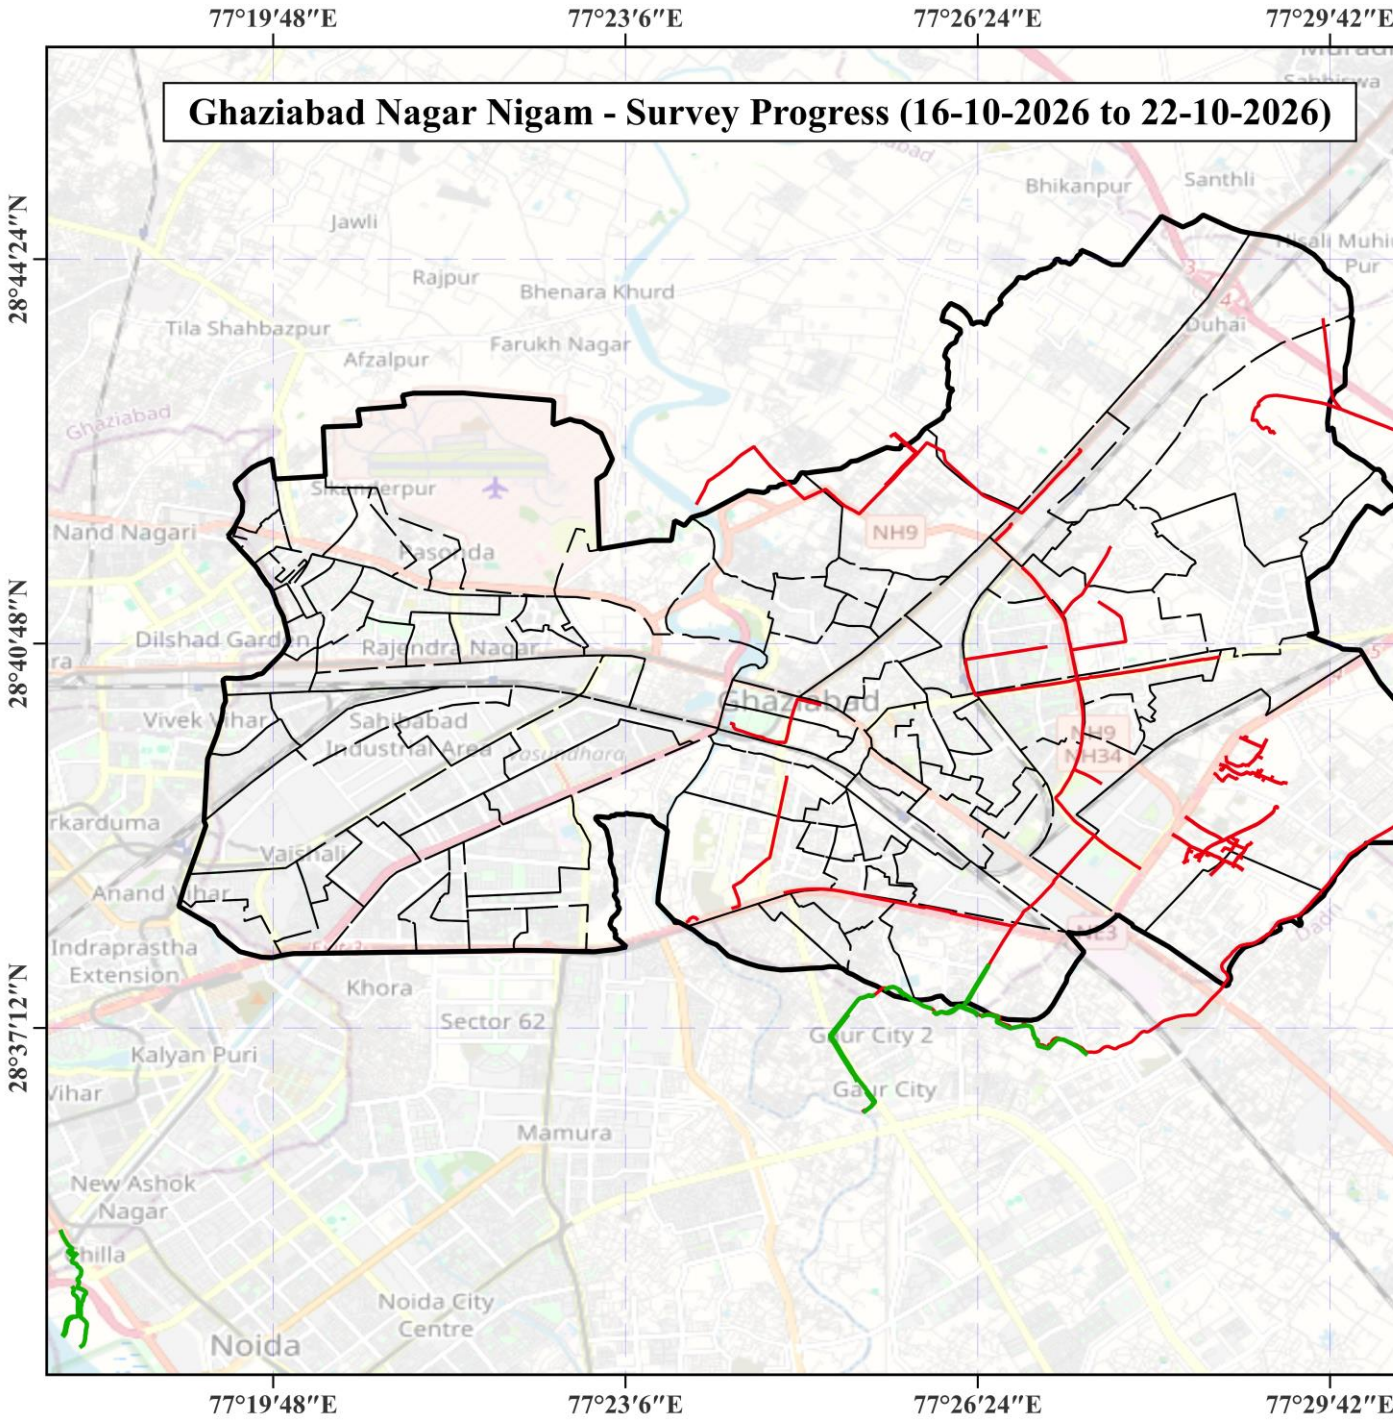


- **DGPS Static Points**

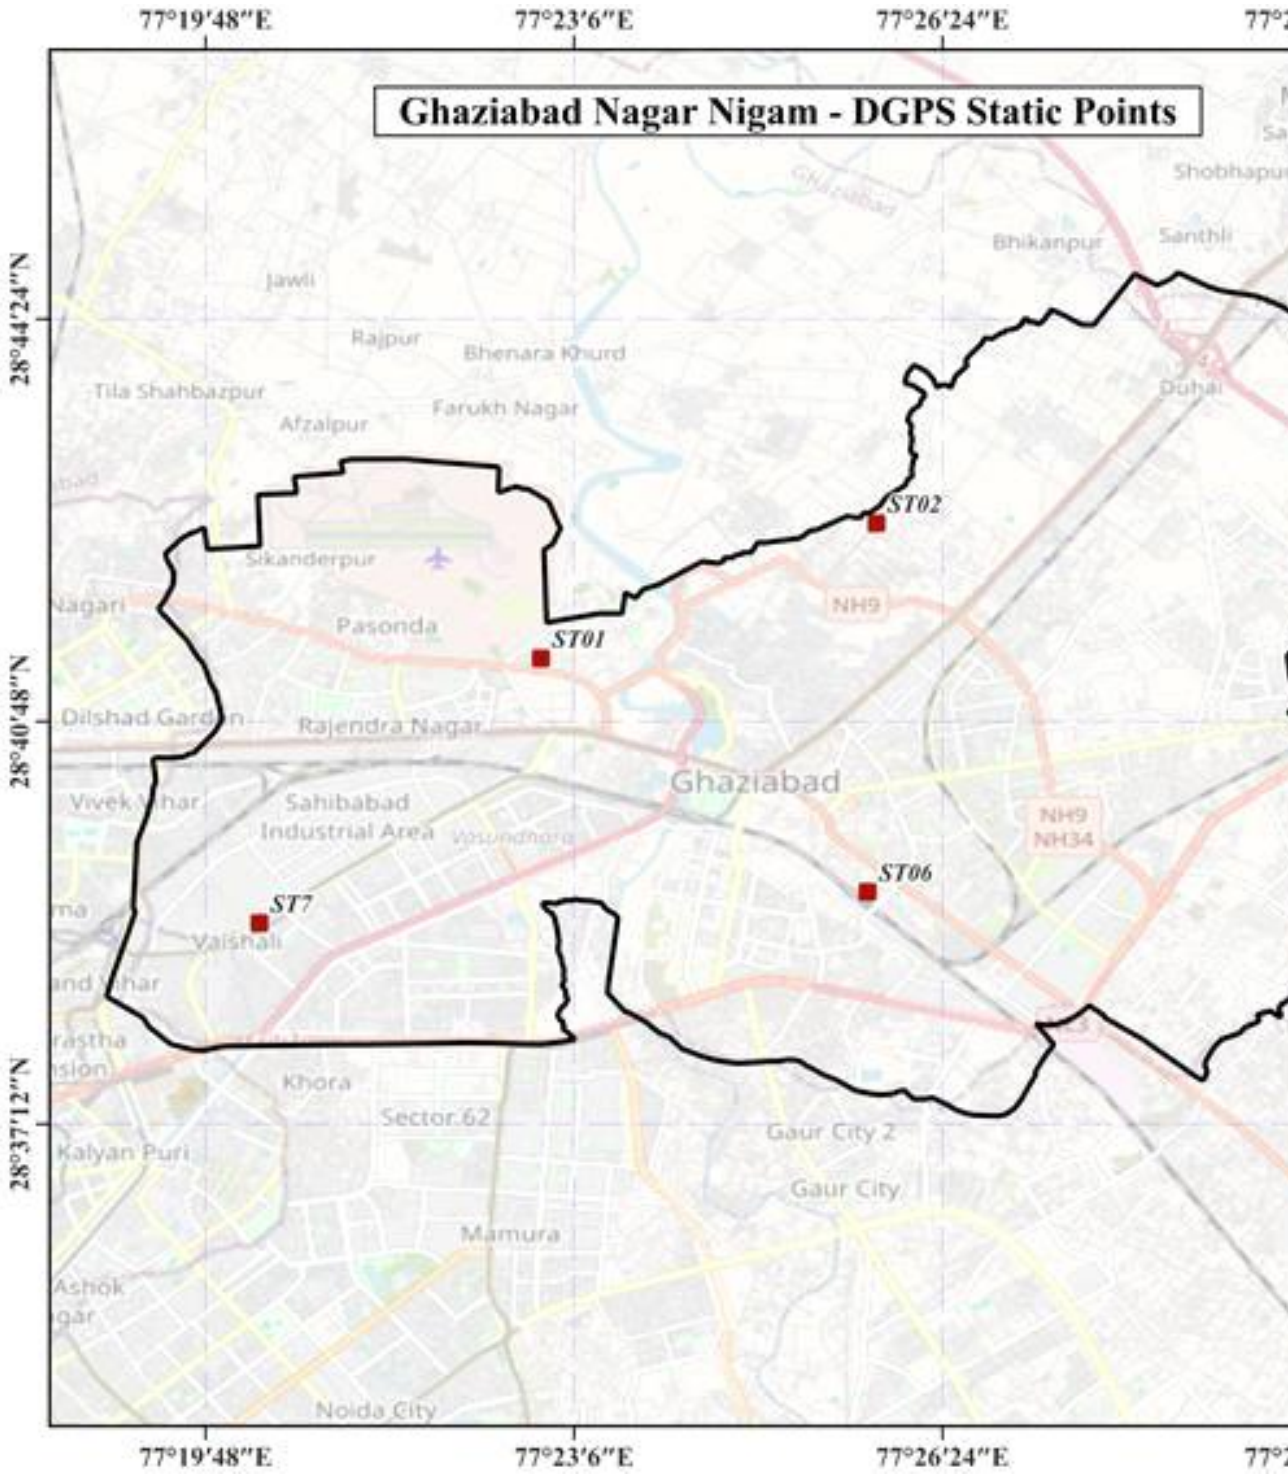



- **Photographs**

• Survey Photographs from 16/10/2026 – 22/10/2026

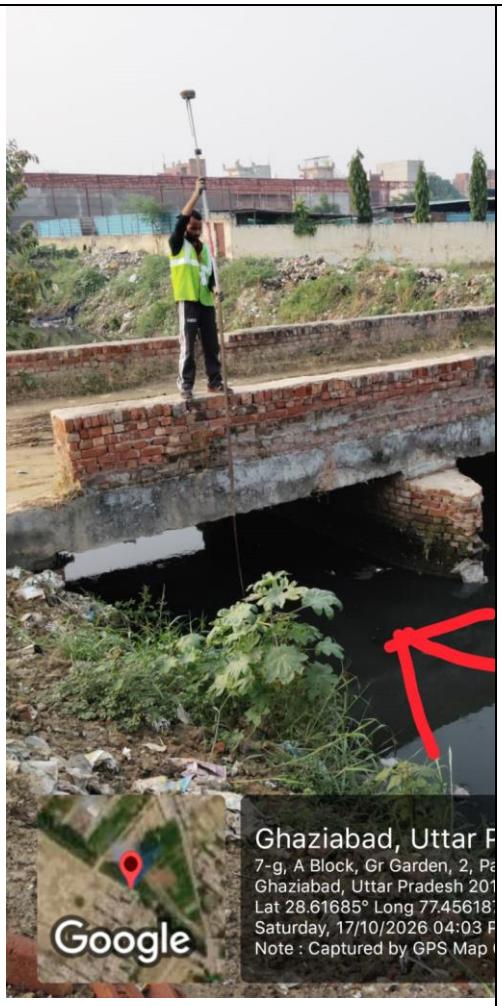- 
Google
Ghaziabad, Uttar
7-g, A Block, Gr Garden, 2,
Ghaziabad, Uttar Pradesh 201
Lat 28.61685° Long 77.45618
Saturday, 17/10/2026 04:03
Note : Captured by GPS Map


- 
GPS Map Cam
Google
Ghaziabad, Uttar Pradesh, Ind
Jcff+mfp, Gaur City 2, Ghaziabad, Uttar Prade
201009, India
Lat 28.624325° Long 77.423525°
Sunday, 18/10/2026 02:35 PM GMT +05:30

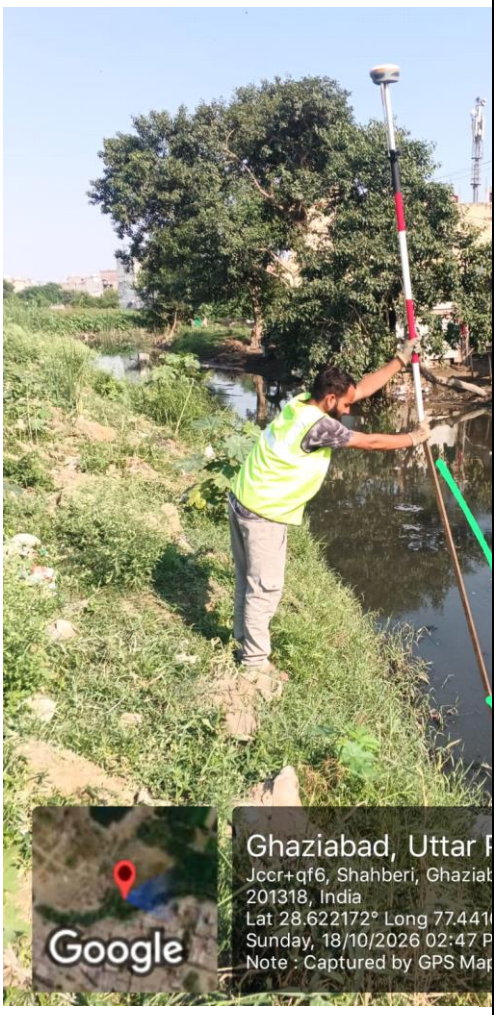

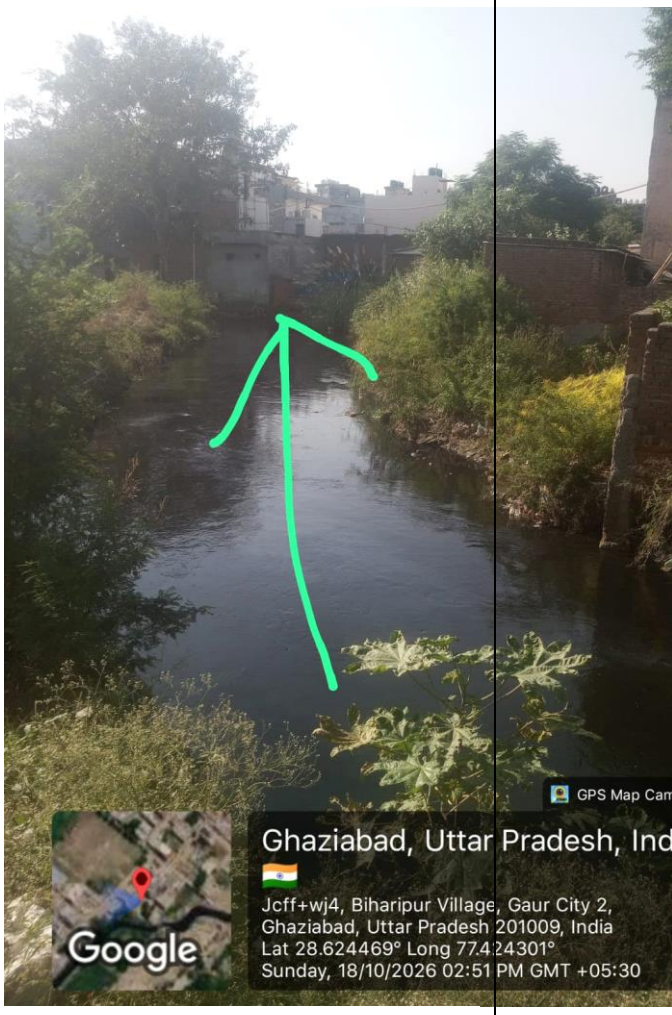


- Survey Photographs from 16/10/2026 – 22/10/2026



- 
Google
Ghaziabad, Uttar
Shop, Street 7, Chipiyana Bu
Pradesh 201318, India
Lat 28.621012° Long 77.443
Sunday, 18/10/2026 03:19 P
Note : Captured by GPS Map

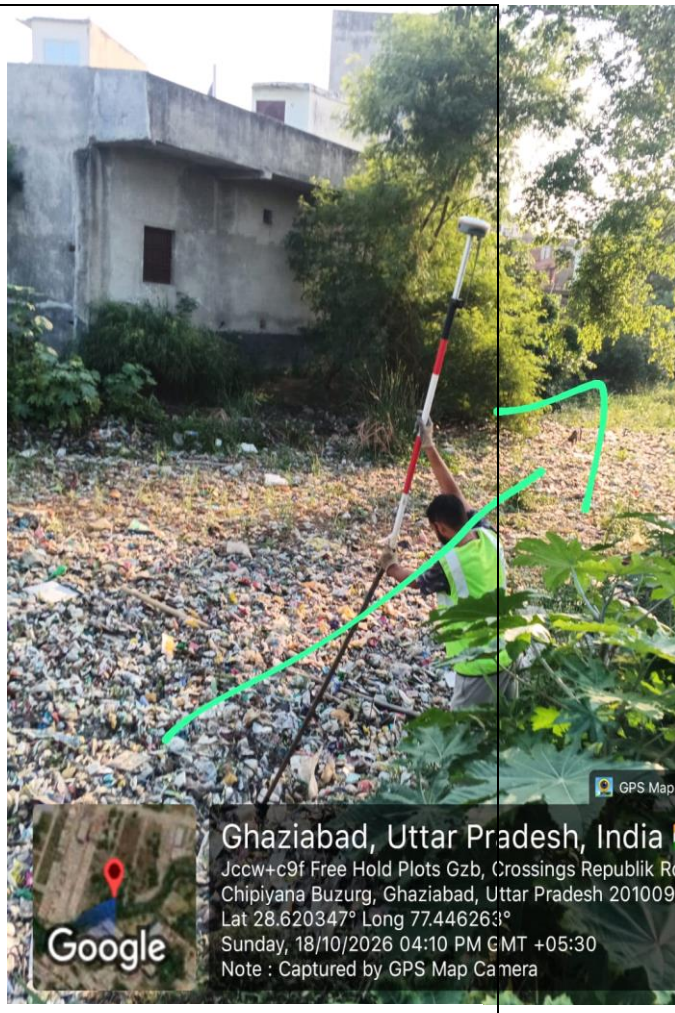- 
Google
Ghaziabad, Uttar Pradesh, India
Jccw+c9f Free Hold Plots Gzb, Crossings Republik R
Chipiyana Buzurg, Ghaziabad, Uttar Pradesh 201009
Lat 28.620347° Long 77.446263°
Sunday, 18/10/2026 04:10 PM GMT +05:30
Note : Captured by GPS Map Camera




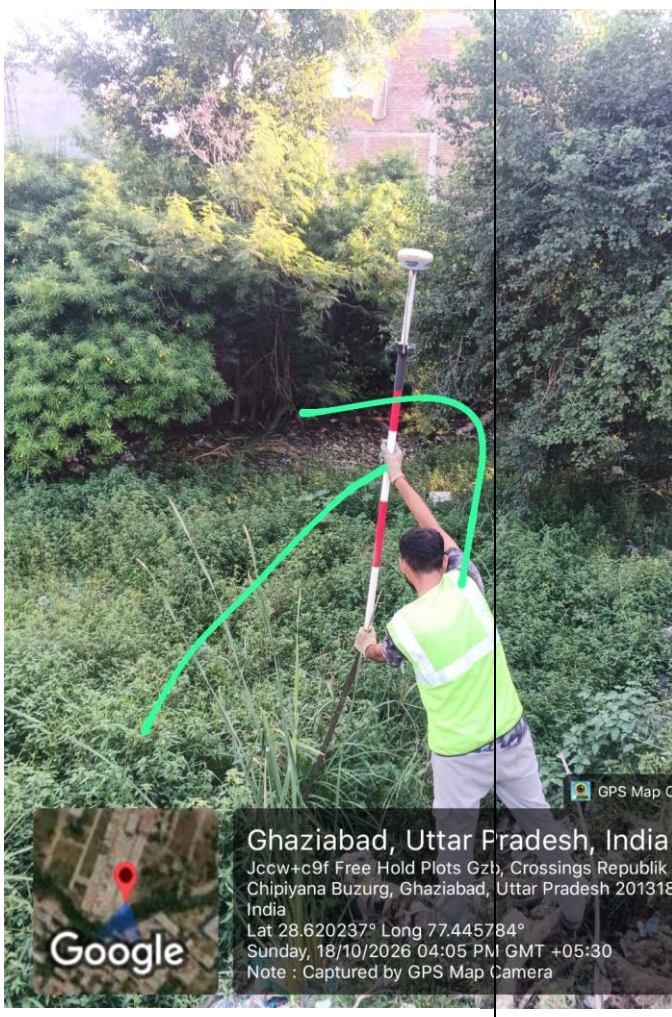

- Survey Photographs from 16/10/2026 – 22/10/2026

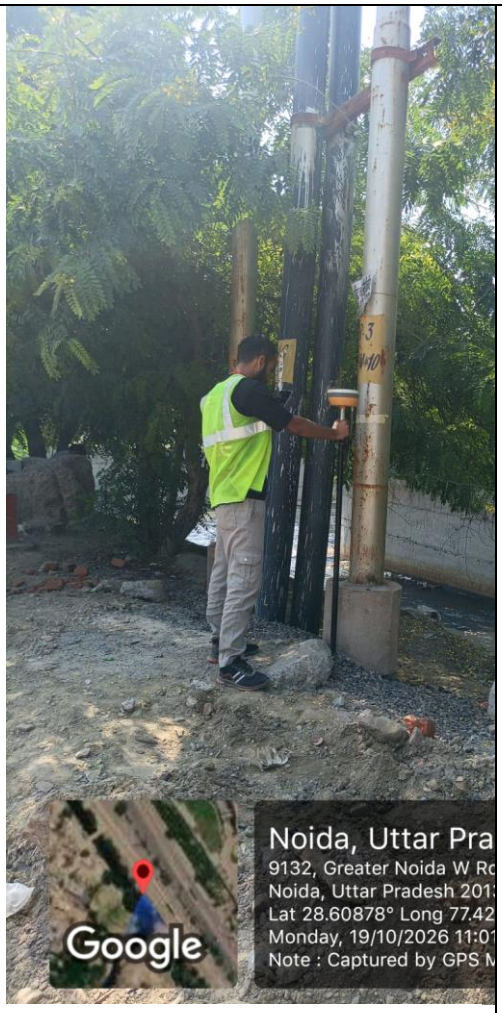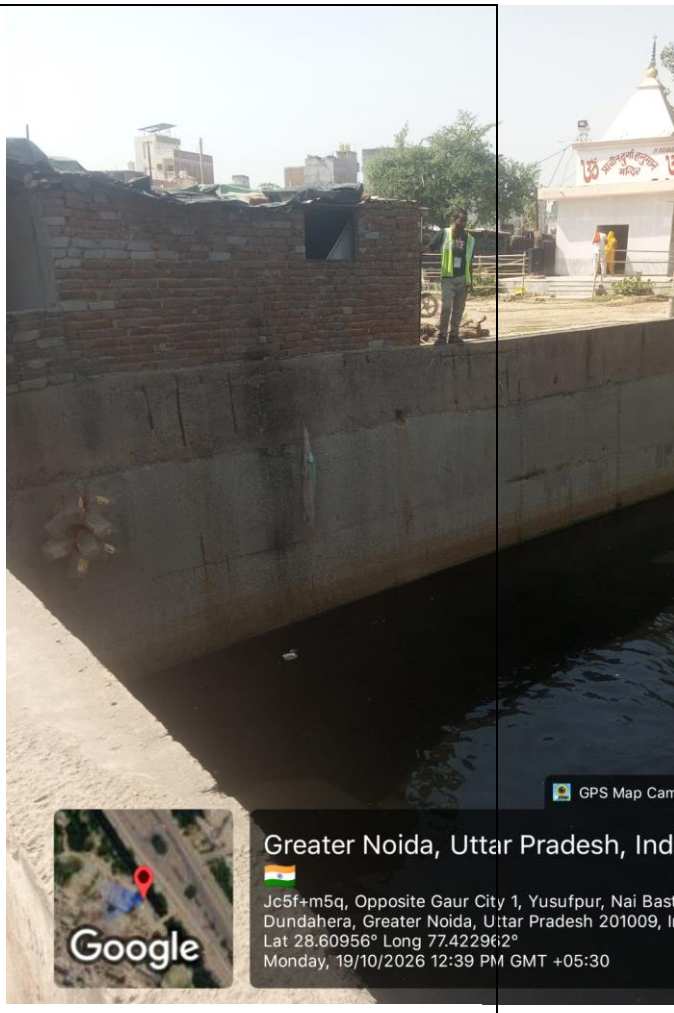- 
Noida, Uttar Pra
Google
- 
GPS Map Cam
Greater Noida, Uttar Pradesh, Ind
Google



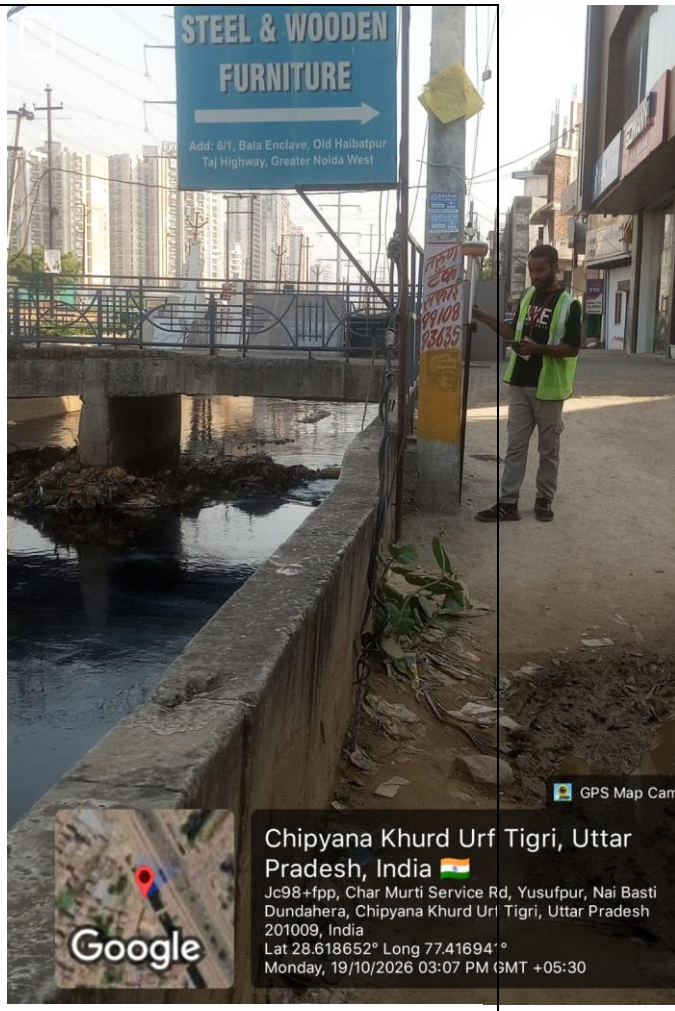

Submitted by: PriMove Infrastructure Consultants Pvt. Ltd. **Date:** 23/10/2026
