Ref. No.: Pri/ /2026 Date: 06/11/2026

To,
The Project Manager,
Construction & Design Services (C&DS),
Office of Project Manager, Unit– 7,
A-212, Vedvyaspuri Colony, Near Subharti University
Meerut, Uttar Pradesh. (Email -cds.unit7@gmail.com)

Subject: Submission of Weekly Progress Report for Ghaziabad City for the period of 30 to 05/11/2026.

Reference: 1. Letter of Acceptance (LOA) Letter No. 2473/G.M.(Ni-9)/e-Tender/2026, dated 10/08/2026 issued by C&DS, U.P. Jal Nigam.
2. Our Acknowledgement Letter no. Pri/1183/2026, dated.18.08.2026

Respected Sir,

With reference to the above-mentioned subject and the meeting held on 18th September 2026, we hereby submit the Weekly Progress Report for the period from 30th to 05th October 2026 for your kind information

Thanking you,

PRIMOVE Infrastructure Development Consultants Pvt. Ltd. PUNE

Sunil Warade
Assistant General Manager

Encl : Weekly Progress Report

WEEKLY PROGRESS REPORT-GHAZIABAD

Reporting Period: 30/10/2026 to 06/11/2026

Project Name: Survey, Collection of Data, Preparation of Integrated Urban Storm Water Drainage Master Plan (IUSWDMP) and other allied works for **Municipal Corporation Ghaziabad**, Uttar Pradesh, India

1. Progress Summary

Activity	Progress / Status
City area as per RFP	225 sq. km
City area as per KML	171 sq. km
Static points	- Planned - 6 Nos - Completed - 6 Nos (100%)
LiDAR survey	- Status – To be carried out using helicopter-mounted LiDAR. Agency finalization is under process
DGPS survey	- DGPS commenced on 13/09/2026 - Deployment reported on 30/10/2026 as 2 base and 3 rovers - Deployment reported on 31/10/2026 as 3 base and 4 rovers - Deployment reported on 01/11/2026 as 2 base and 3 rovers - Deployment reported on 02/11/2026 as 4 base and 8 rovers - Deployment reported on 03/11/2026 as 4 base and 9 rovers - Deployment reported on 04/11/2026 and 05/11/2026 as 4 base and 11 rovers - Survey team members – 15 Nos - Calibration report submitted on 22/09/2026
Survey of Primary drains	- Primary Drains As per OSM Planned - 223 km - Completed Length up to previous week – 104.3 Km - Cumulative length – 160.5 km (71.97%) - Surveyed for alignment – 56.2 km
Out Falls identified till date	- Shahberi Nala Outfall - Raj Nagar Extension Outfall - Outfall near Hindon Ghat - Hindon cut outfall to Yamuna River
Road Survey	- Road Length as per OSM Planned - 3450 km - Completed Length up to previous week – 104.3 Km - Completed length during the reporting period 102.1 km;

	- Cumulative length – 206.4 km
Secondary /tertiary Drains Covered	- Completed Length up to previous week – 26.62 Km - Completed length during the reporting period – 45.9km; - Cumulative length – 72.52 km
Inception report	- Submitted 16/09/2026

2. Correspondence and Survey Activities

Activity	Date / Details
DGPS survey start date	13/09/2026
DGPS calibration report submitted	22/09/2026
Deployment reported on 30/10/2026	2 base and 3 rovers
Deployment reported on 31/10/2026	3 base and 4 rovers
Deployment reported on 01/11/2026	2 base and 3 rovers
Deployment reported on 02/11/2026	4 base and 8 rovers
Deployment reported on 03/11/2026	4 base and 9 rovers
Deployment reported on 04/11/2026 and 05/11/2026	4 base and 11 rovers
Inception report	16/09/2026
Meeting with PM, C&DS	29/09/2026
Survey Site Visit by C&DS officials	-

3. Drain Survey / Mapping Progress

Item	Progress / Details
Primary drains planned as per OSM	223 km (tentative; as per OSM)
Primary drains completed up to last report	104.3 km
Primary drains completed during reporting period	56.2 km
Primary drains cumulative total shown	160.5 km
Survey completed for alignment	56.2 km
Road length as per OSM planned	3450 km
Road Survey Completed up to last week	206.4 km
Road Survey Completed this week	102.1 km
Cumulative length	206.4 km
Secondary/Tertiary drains completed up to last report	26.62 km
Secondary/Tertiary drains completed during reporting period	45.9km
Secondary/ Tertiary drains cumulative total shown	75.52 km
Secondary / tertiary drain areas reported	Sadarpur Residential Area, Mehrauli/Aditya World City Road, Shani Mandir Road, Wave City, Balle Market,01,Shahpur Bamheta, Bikaner chowk, Surya nagar, Sidharth Vihar, Head Police Station Vaishali, Anand Vihar Railway Line, GOUR City, Sikandarpur, Kaushambi Metro Station, Dr Baba Sahed Park, Kavi Nagar, Loha Mandi Railway Track,

4. Primary Drain Reaches Completed

- Raj Nagar Extension Nala
- Shahberi Nala
- Dasna- Kushaliya Nala
- RDC Nala

- Lal Kuan Nala
- Sikrod Nala
- Loha Mandi Nala
- Hapur Chungi Nala
- Sanajay Nagar Main Drain
- Kalia Bhatta Nala
- Ashok Nagar
- Khora Colony

5. Survey Plan for Next Week

- **Primary drains**

- Dasna Drain and Hindon Cut Invert levels will be taken.

- **Secondary/Tertiary drains**


- Ward wise (91,84,65,22) drain surveys covering the secondary and tertiary drain.
- Drain Survey of Raj Nagar Extension and Loha Mandi.

6. IMD Data Status


A formal request letter has been submitted to the India Meteorological Department (IMD), Delhi Office, for the procurement of rainfall data pertaining to Ghaziabad Nagar Nigam. Additionally, a forwarding letter dt. 16/10/2026 has been issued by C&DS to facilitate and expedite the data procurement process.

Item	Progress / Details
Submission of request letter to IMD for IDF Curve data	Submitted on 28/09/2026
Submission of Additional Request Letter	16/10/2026
Payment for IDF data	Completed on 15/10/2026
Expected date for receiving IDF data	15th November 2026

7. Survey Progress this week October 2026

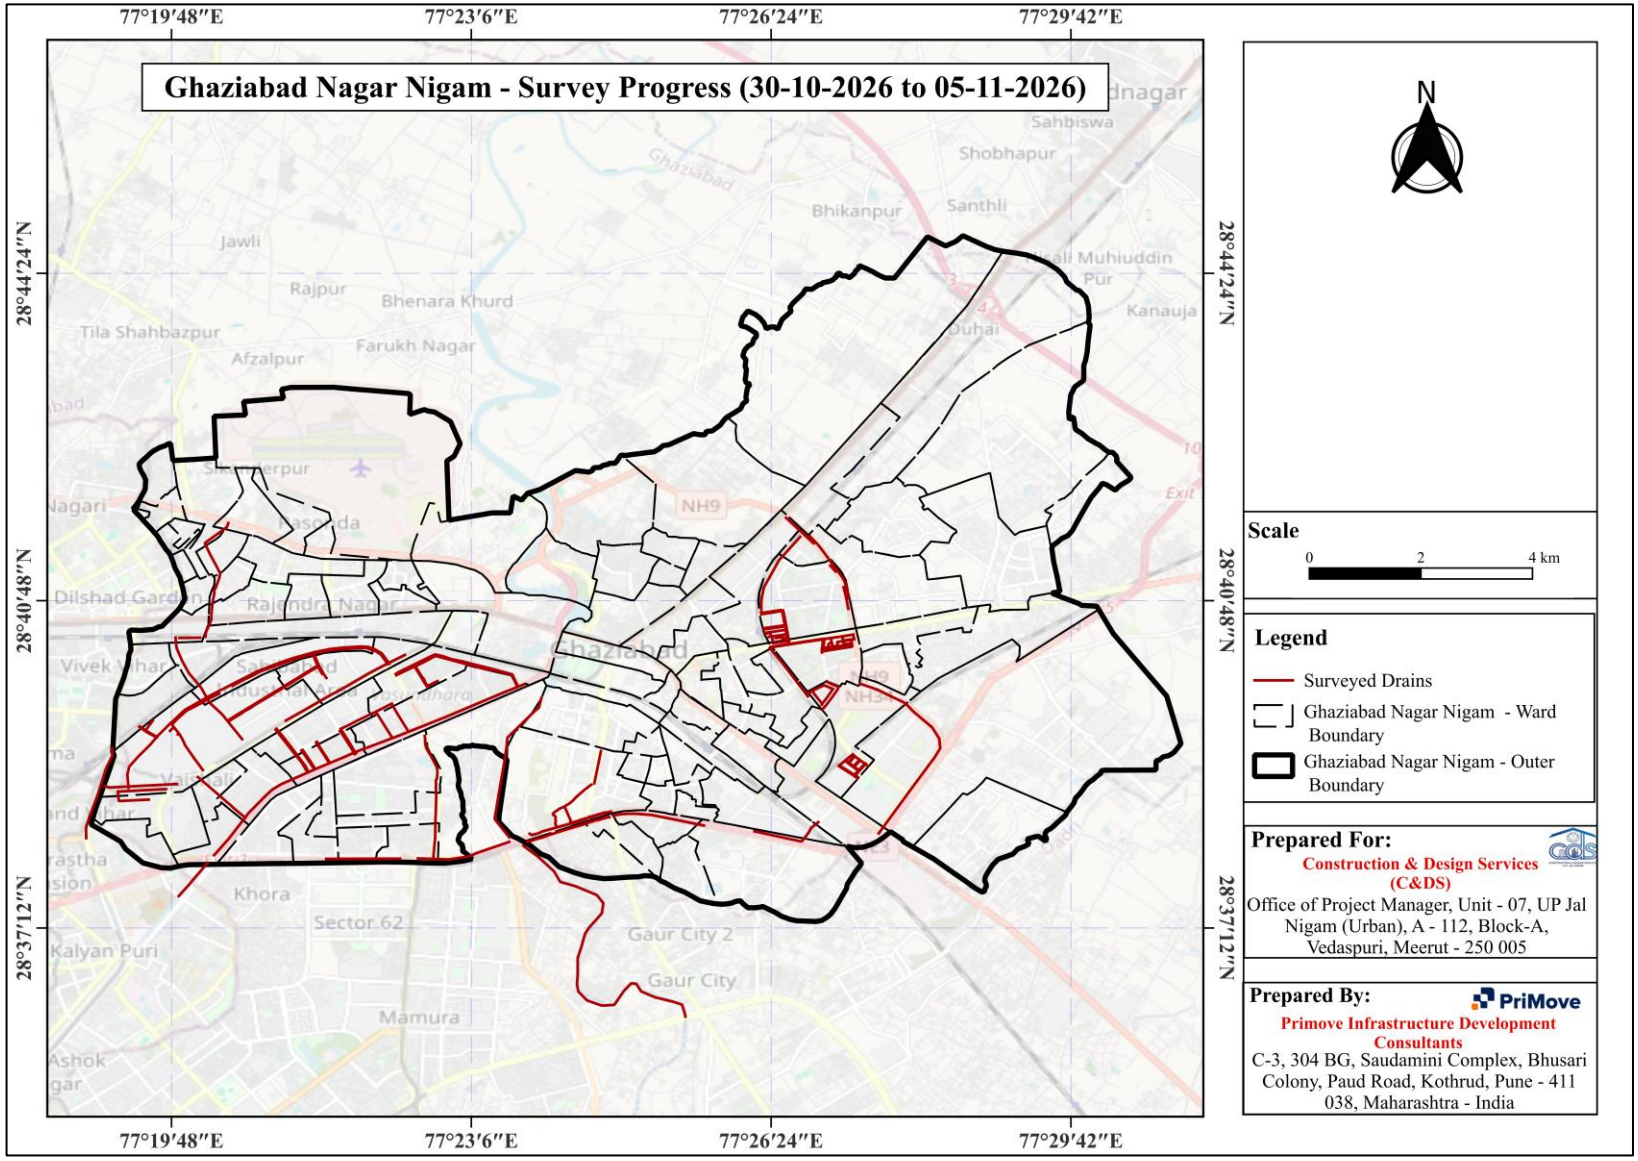

8. DGPS Static Points

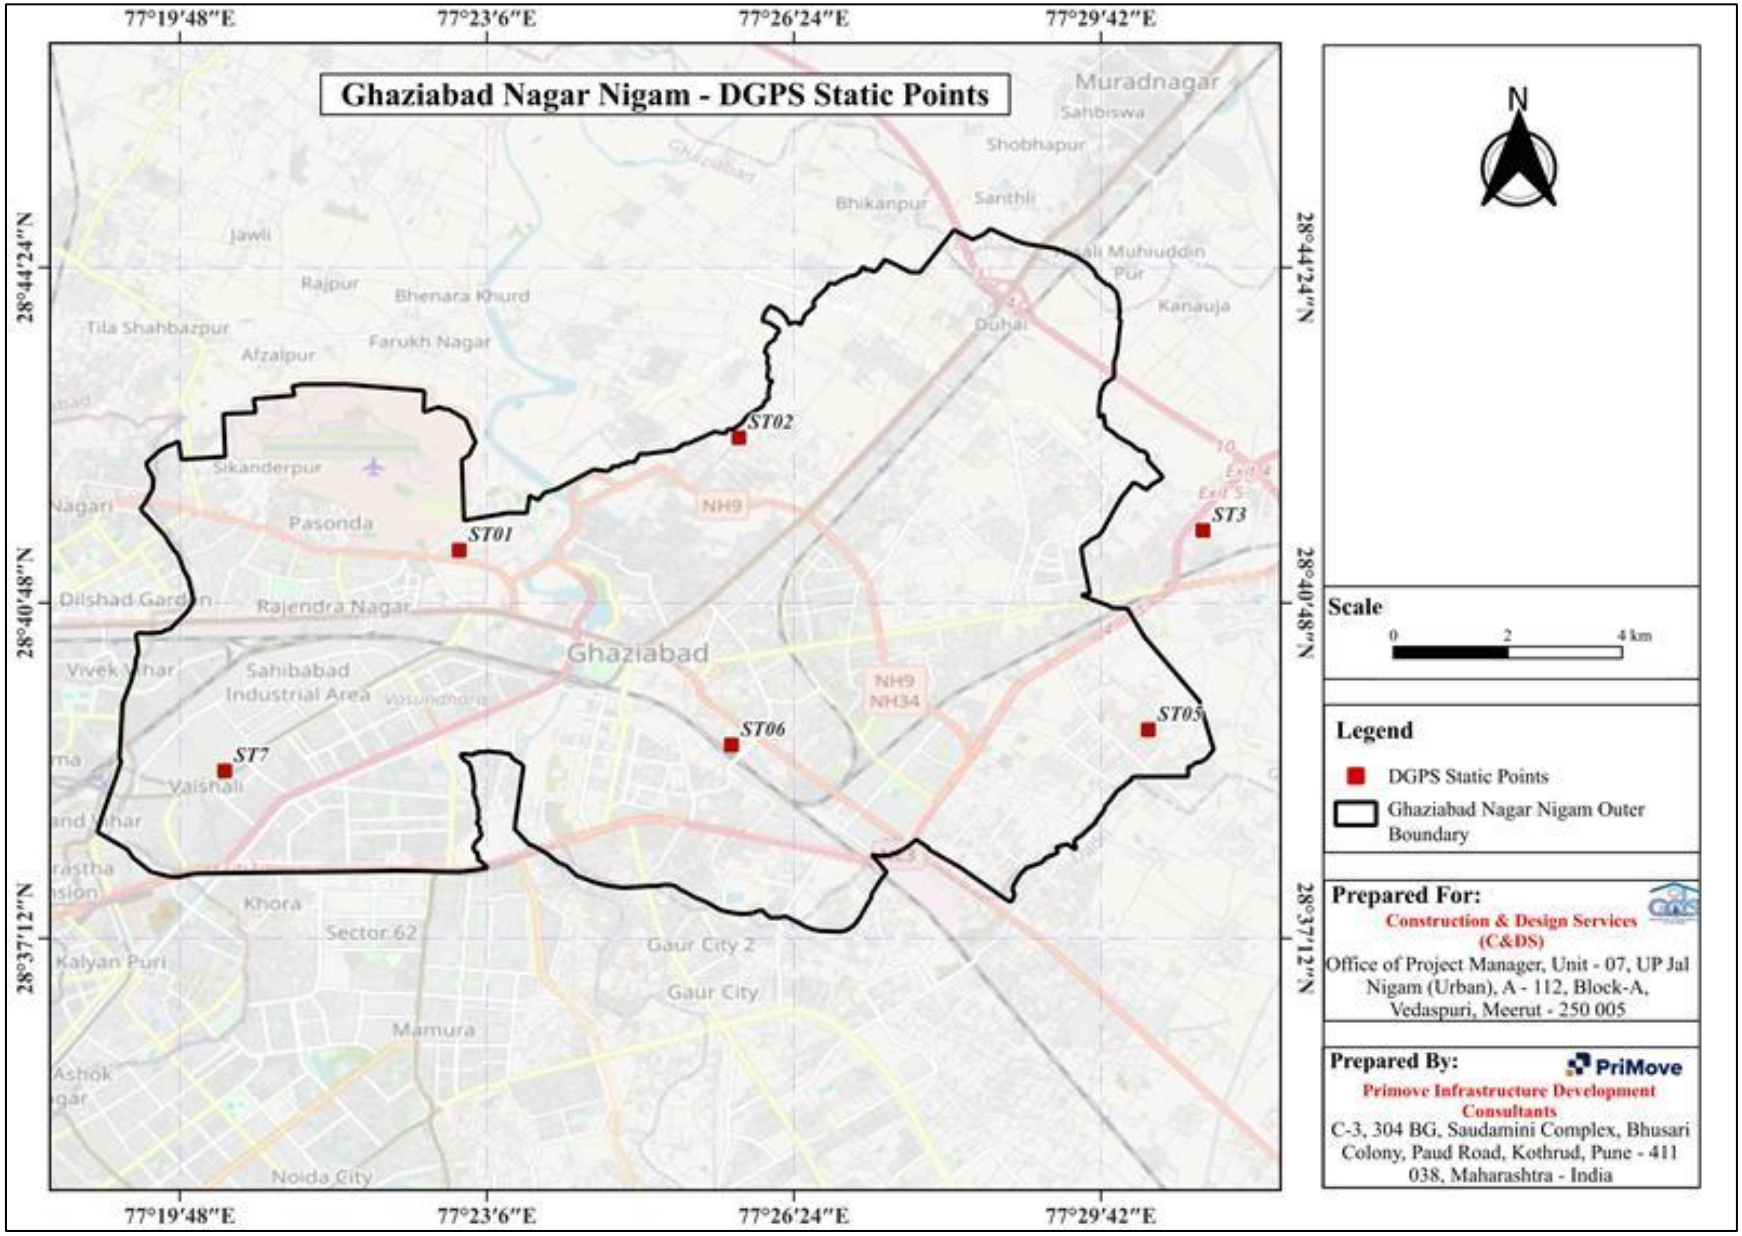

9. Photographs

Survey Photographs from 30/10/2026 – 05/11/2026









Survey Photographs from 30/10/2026 – 05/11/2026









Survey Photographs from 30/10/2026 – 05/11/2026









Submitted by: PriMove Infrastructure Consultants Pvt. Ltd. **Date:** 06/11/2026
