## WEEKLY PROGRESS REPORT-MEERUT

**Reporting Period: 07/10/2026 to 13/09/2026**

**Project Name:** Survey, Collection of Data, Preparation of Integrated Urban Storm Water Drainage Master Plan (IUSWDMP) and other allied works for **Municipal Corporation Meerut**, Uttar Pradesh, India

### 1. Progress Summary

| Activity | Progress / Status |
|---|---|
| **City area** | 143.83 sq. km |
| **Static points** | - Planned - 8 Nos<br>- Completed - 10 Nos (100%)<br>- Duration – 3 days |
| **GCP points** | - Planned - 340 Nos<br>- Completed - 0 Nos (0%) |
| **LiDAR drone survey** | - Data acquisition activities are planned to commence soon. |
| **LiDAR drone survey Area excluded due to restricted area** | - Cantonment Area |
| **DGPS survey** | - DGPS commenced on 13/09/2026<br>- Deployment reported as 1 base and 3 rovers on dated 14/10/2026<br>- Survey team members – 3 Nos<br>- Calibration report submitted on 22/09/2026 |
| **Survey of Primary drains** | - Primary Drains As per OSM Planned – 80 km<br>- Completed Length up to previous week:- 85.59 Km<br>- Completed length during the reporting period – Invert level marking only: 49.45 km<br>- Cumulative length - 85.59 km (100%) |
| **Out Falls identified till date** | - 4 Outfalls identified |
| **Road Survey** | - Road Length as per OSM Planned - 2458 km<br>- Completed Length up to previous week:- 55.4 Km<br>- Completed length during the reporting period – 5 km<br>- Cumulative length – 60.4 km (2.46%) |
| **Secondary /tertiary Drains Covered** | - Completed Length up to previous week:- 46.12 Km<br>- Completed length during the reporting period:– 4.7 km<br>- Cumulative length :- 50.82 km |
| **Inception report** | - Submitted on 16/09/2026 |

### 2. Correspondence and Survey Activities

| Activity | Date / Details |
|---|---|
| LiDAR survey letter submitted by PriMove to PM, C&DS | Will be submitted soon |

| | |
|---|---|
| LiDAR survey – drone details submitted | Will be submitted soon |
| Police permission received from CP | Will be received soon |
| LiDAR drone survey flying started (data acquisition) | Will be commenced soon |
| LiDAR drone survey flying completed (data acquisition) | NA |
| DGPS survey start date | 13/09/2026 |
| DGPS calibration report submitted | 22/09/2026 |
| Number of DGPS teams deployed | 1 base station and 3 rover units |
| Inception report | 16/09/2026 |
| Meeting with PM, C&DS | 31/08/2026, 17/09/2026, 29/09/2026 |
| Survey Site Visit by C&DS officials | 17/09/2026 |

### 3. Drain Survey / Mapping Progress

| Item | Progress / Details |
|---|---|
| Primary drains planned as per OSM | 80 km (tentative; as per OSM) |
| Primary drains completed up to last report | 85.59 km |
| Primary drains completed during reporting period | Invert level marking only– 49.45 km |
| Primary drains cumulative total shown | 85.59 km |
| Road length as per OSM planned | 2458 km |
| Road Survey Completed up to last week | 55.4 km |
| Road Survey Completed in this week | 5 km |
| Cumulative length | 60.4 km |
| Secondary drains completed up to last report | 46.12 km |
| Secondary drains completed during reporting period | 4.7 km |
| Secondary drains cumulative total shown | 50.82 km |
| Secondary / tertiary drain areas reported | Ganga Nagar–Kaseru Baksar–Mawana Road Area, Jagriti Vihar–Garh Road–Devpuri–Shastri Nagar Area, Daurli–Roshanpur–Kanker Khera–Lisari–Ved Vyas Puri–Partapur–Sharda Road Area |

### 4. Primary Drain Reaches Completed

- Abu Nala-1 – Begumpul to Begambagh Primary Drain
- Abu Nala-1 – Panchsheel Colony to Nehru Nagar Primary Drain
- Abu Nala-1 – Mohanpuri to Ahmad Nagar Primary Drain
- Abu Nala-1 – Ganga Nagar to Jai Bheem Nagar Primary Drain
- Odean Nala – Ramgarhi to Prabhat Nagar Primary Drain
- Odean Nala – Garh Road to Chanakyapuri Road Primary Drain
- Odean Nala – Ghosipur to Hasanpur–Mirpur Primary Drain
- Abu Nala-2 – Devpuri to Kanker Khera via Nangla Tashi Primary Drain
- Khadauli Nala – Ved Vyas Puri to Sushant City Primary Drain

- Khadauli Nala – Partapur to Shatabdi Nagar Primary Drain

**Drain Length Covered under Alignment Survey and Invert Level Verification**

- Invert level survey of the primary drains commenced on 06/10/2026, starting with Odean Nala, where a 2.1 km stretch was covered in the initial phase.
- Alignment survey has been completed before 07/10/2026 and it has covered a stretch of 85.59 km in total, and invert level verification for the same is in progress.
- From 07/10/2026 onwards, the invert level survey of the primary drains mentioned above was carried out along Odean Nala, Abu Nala-2 and Khadauli Nala.
- A total of 49.45 km of invert level marking was completed during the reporting period.

## 5. Survey Progress as on 13/10/2026

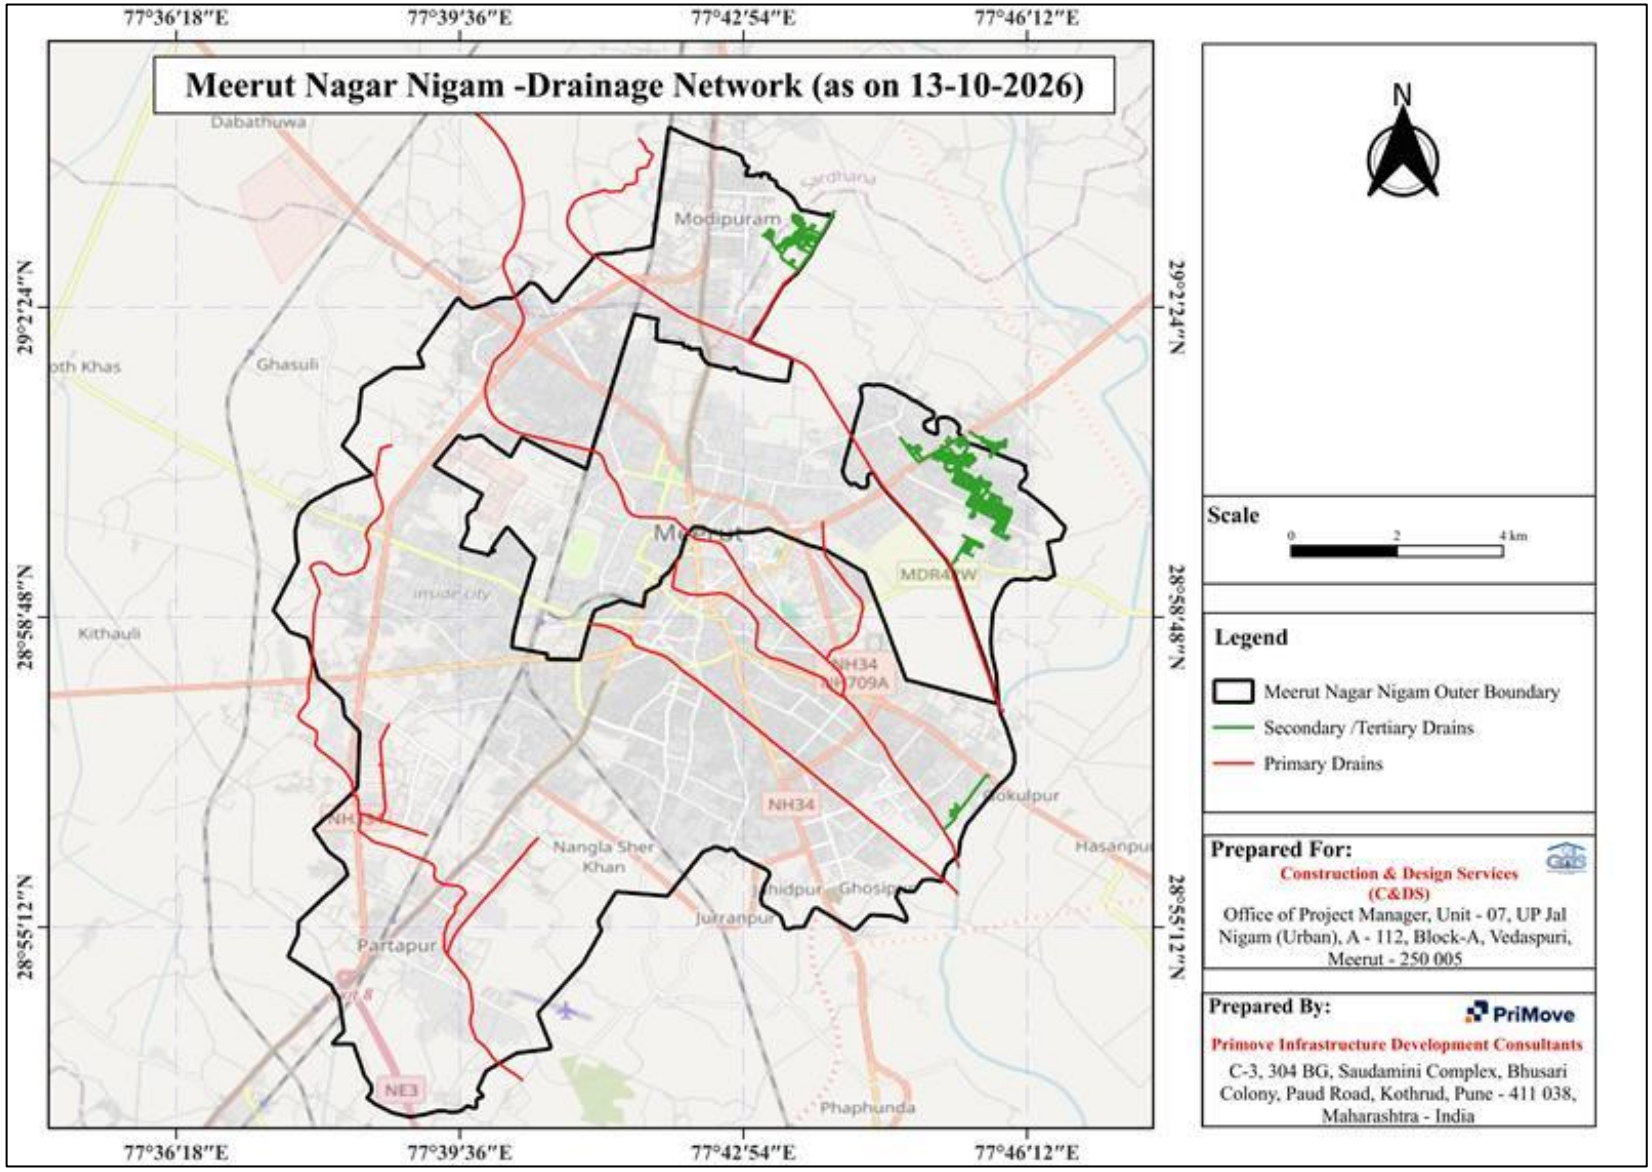



*Figure 1- Survey Progress of Meerut Nagar Nigam as on 13-10-2026*

## 6. DGPS Static Points

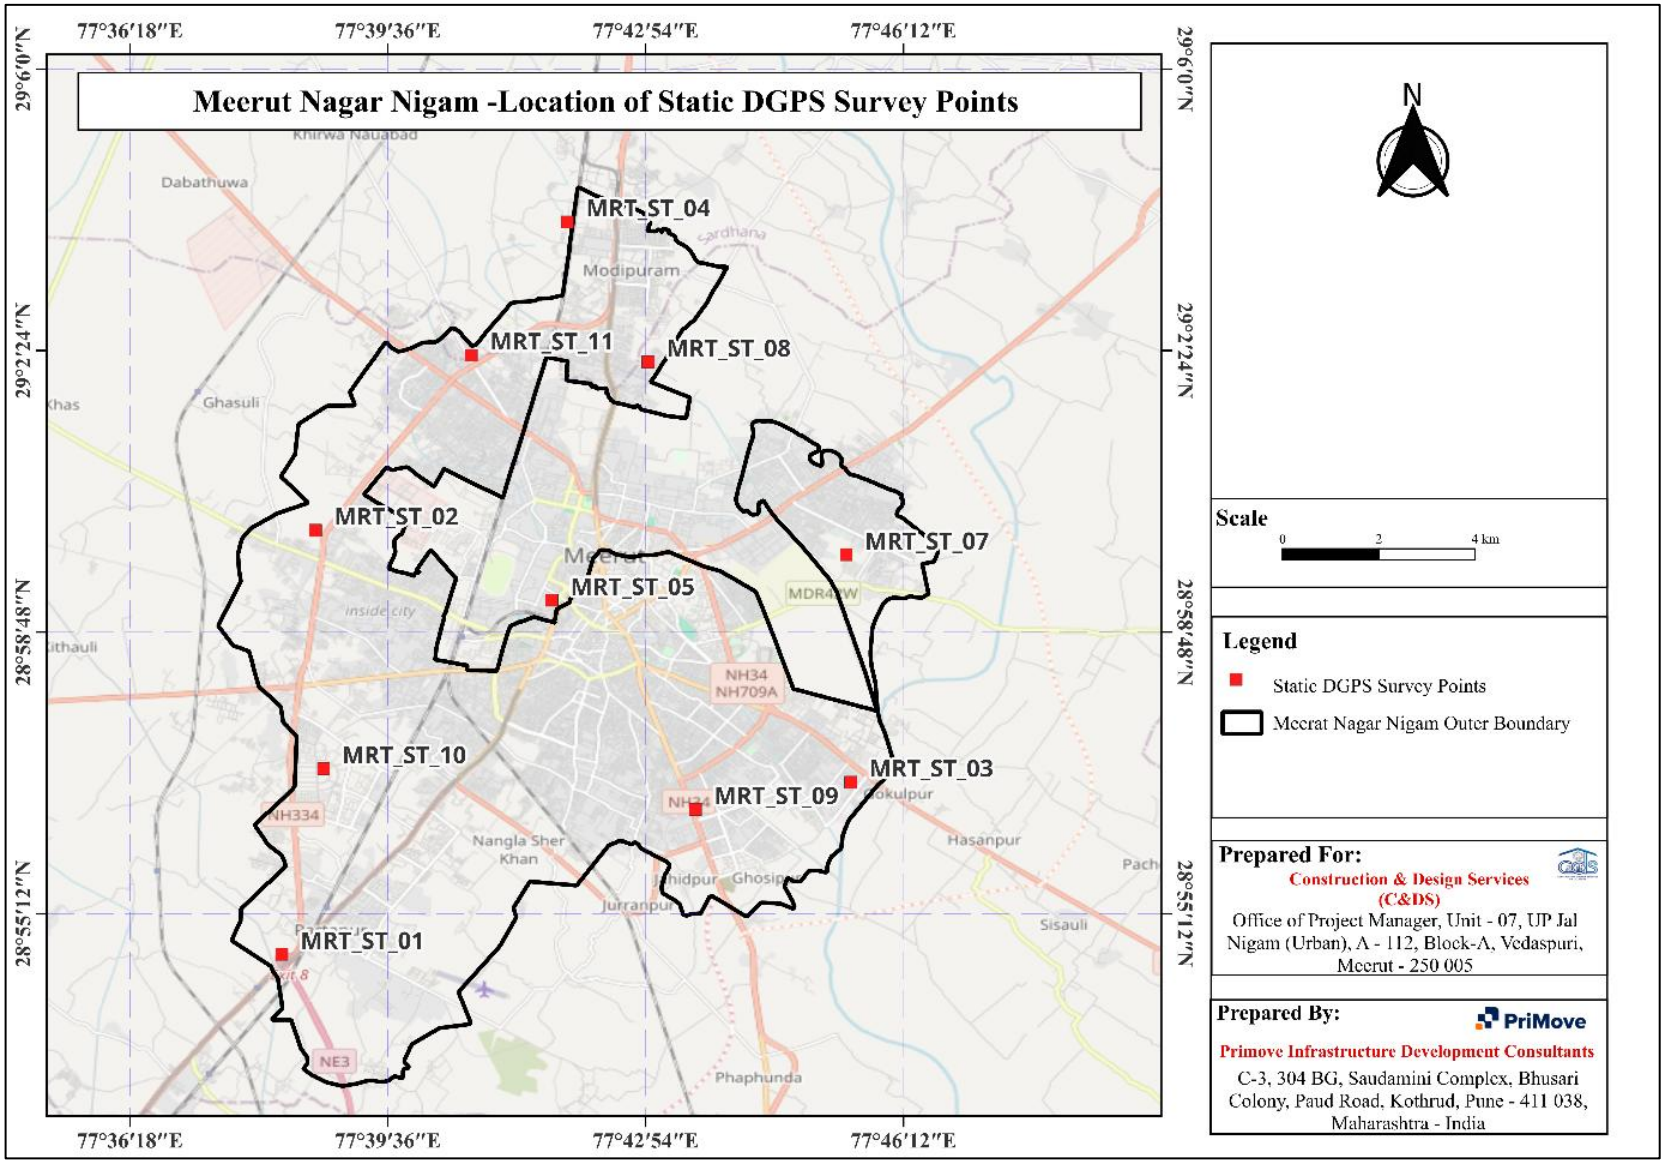



*Figure 2- Location of Static DGPS Survey Control Points within Meerut Nagar Nigam*

## 5. Road Survey Completed in wards

| Ward No. | Ward Name | Length (km) |
|---|---|---|
| 31 | Shatabdi Nagar | 7.2 |
| 6 | Mohikkampur | 2.7 |
| 19 | Dayanpur | 1.1 |
| 42 | Jain Nagar | 0.51 |
| 49 | Purva Mahavir | 0.48 |
| 69 | Sarai Ladas | 0.38 |
| 54 | Purva Elahi Baksh | 0.254 |
| 56 | Prahalad Nagar | 0.85 |
| 76 | Shyam Nagar Pashchim | 0.506 |
| 83 | Faqudin Ali Ahmed Nagar Pashchimi – 1st | 0.42 |
| 82 | Fakruddin Ali Ahmed Nagar Pashchimi – 1st | 0.48 |
| 20 | Kaserukera | 1.52 |
| 37 | Ganga Nagar | 16.9 |
| 17 | Abdullapur | 12.2 |
| 7 | Peclna Sofipur | 2.5 |
| 30 | Modipuram | 2.3 |
| 40 | Jakuali | 0.286 |
| 33 | Hydle Colony | 2.8 |
| 79 | Kidvai Nagar | 0.734 |
| Others | Kali Nadi, Extended length of Abu Nala 2 | 6.28 |

## 6. Survey Plan for Next Week

**Primary drains**

- Topographical survey and drain invert level measurements along the Abu Nala-1 extension needs to be done.
- Secondary and tertiary drain surveys at the junctions and connecting points of the primary drainage network.

**Road survey**


Road level survey along the Abu Nala-1 drainage corridor in the identified areas.

## 7. IMD Data Status


A formal request letter has been submitted to the India Meteorological Department (IMD), Delhi Office, for the procurement of rainfall data pertaining to Meerut Nagar Nigam.

## 6. Photographs

<table>
<tr><th colspan="2">Primary/Secondary/Tertiary Drains</th></tr>
<tr><td> 

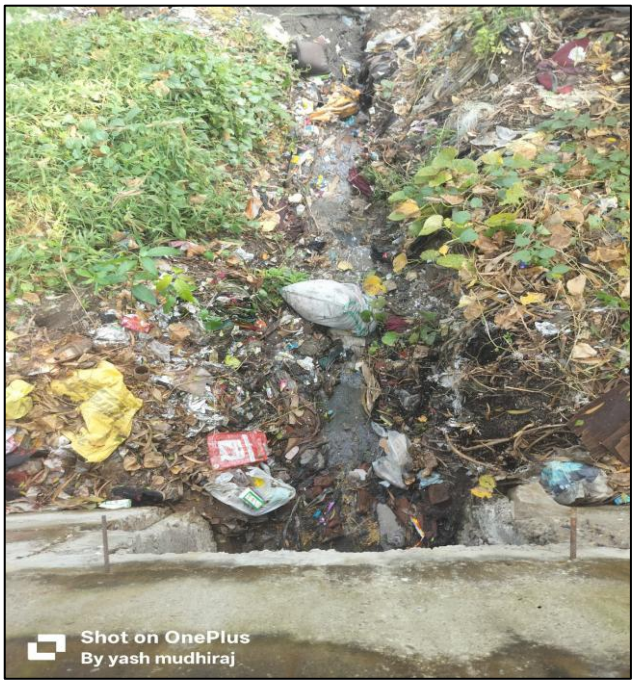Invert level marking</td><td> 

Blockage in Abu Nala-2</td></tr>
<tr><td> 

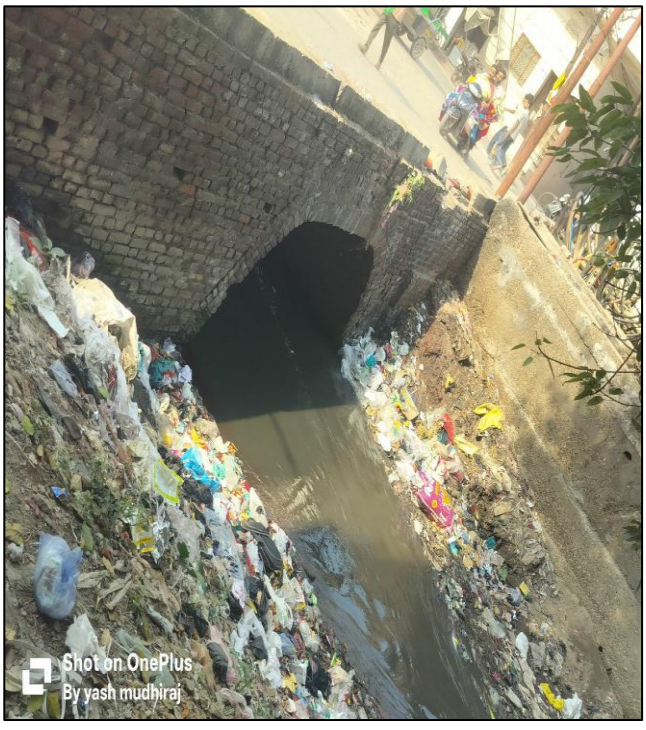Invert level marking</td><td> 

Odeon Nala</td></tr>
</table>

## Primary/Secondary/Tertiary Drains




**Abu Nala - 2**




**Invert level marking in Khadauli Nala**



**Silt deposition in Khadauli Nala**



**Khadauli Nala Feeder Channel**

| Primary/Secondary/Tertiary Drains | |
|---|---|
|  |  |
| **Invert level marking in Khadauli Nala** | **Abu Nala-2** |

**Submitted by:** PriMove Infrastructure Consultants Pvt. Ltd. **Date:** 14/10/2026
