Weekly Progress Review Report – MEERUT

Week: 11/09/2026 to 23/09/2026

1. Survey Overview

Survey Component	Total	Completed till 17th Sep 2026 (number and %)	Completed this week (number and %)	Planned for Coming Week (%)	Teams Mobilized as of today
GCPs for Drone Survey	Not Started	Nil	Not applicable	100%	Not started
Static Points for DGPS Survey	8 Nos	8/8; 100%	Completed	Nil	Not Started
DGPS Survey of Drains	In Progress	40.2 km	81 km covered (13–23 Sept)	100% Primary Drain Mapping	1 DGPS Base 3 Rovers 3 Members
Drone Survey Area	188 sq.km	Awaiting Permission	Awaiting Permission	Tentative as permission for flying is required	Not Stared

2. Survey Progress of First Week (Till 17Th September)

a) **GCPs Marking - Nil**
b) **Static Points for DGPS Survey – 8 Points completed out of 8 with 4 hours of data logging**
c) **DGPS Drain Survey – Covered 40.2 km (Ganga Nagar Area; Later shifted for Primary Nala Survey)**

3. DETAILS OF SURVEY TEAM & DGPS/ROVER EQUIPMENT – MEERUT

DATE	DGPS BASE	ROVER	MEMBERS
8/9/2026	1	3	3
9/9/2026	1	3	3
10/9/2026	1	3	3
11/9/2026	1	3	3
12/9/2026	1	3	3
13/9/2026	1	3	4
14/9/2026	1	3	4
15/9/2026	1	3	4
16/9/2026	2	4	6
17/9/2026	2	4	6

DATE	DGPS BASE	ROVER	MEMBERS
18/9/2026	1	3	3
19/9/2026	1	3	3
20/9/2026	1	3	3
21/9/2026	1	3	3
22/9/2026	1	3	3
23/9/2026	1	3	3
24/9/2026	1	3	3
25/9/2026	1	3	3

4. DGPS Survey of Drains

DGPS-based cross-section survey of the Nagar Nigam drain network commenced on 13 September 2026 and has continued through 23 September 2026, carried out by the field survey teams together with the Meerut base crew. A total of 6538 survey points has been logged to date, covering drain top/bottom edges, bed left/right, bank top left/right, manhole rim levels, culverts, water level and nala top/bed points, referenced to temporary benchmarks (TBM) established from the project base station. (7378 points has been taken till 25th September 2026)

Date	Stretch covered (km)	Remarks
13-09-26	5.5	The drain survey in the Ganganagar area, including Panchvati Colony Park, Global Public School, and nearby locations, was discontinued midway as informed by the Nagar Nigam, due to which surveyor had been reassigned to another location.
14-09-26	9.1	
15-09-26	7.7	
16-09-26	9.9	
17-09-26	8.2	
18-09-26	4.1	Beginning of primary drain survey
19-09-26	6.9	-
20-09-26	-	-
21-09-26	11.14	Some sections could not be accessed during the survey, resulting in distances of more than 200 m between consecutive surveyed points. These inaccessible sections have been identified and marked so that necessary action will be taken in the future.
22-09-26	8	
23-09-26	10.8	
24-09-26	12.35	-
25-09-26	9.02	-
Total	**102.71**	

5. Lidar Survey – Awaiting permission for UAV Survey

6. Reconnaissance survey

A three-day field reconnaissance survey was carried out from 17 to 19 September 2026 by a five-member PriMove team (Vivek M., Prabhamani N., Samanyu P Rai, Anjima T. and Mahalakshmi S.) covering the principal stormwater drainage corridors of Meerut Nagar Nigam – Abu Nala, Odeon Nala (ODN Nala), Khadauli Nala and their interface with the Kali River. The survey identified drainage conditions, hydraulic constraints and waterlogging hotspots to guide the subsequent detailed DGPS/topographic survey. Findings are reported in full in the Reconnaissance Survey chapter of the Inception Report; a summary is provided below.

i) Survey Programme

Day	Date	Area / Corridor	Major Activities
Day 1	17 Sept 2026	Abu Nala 1, Abu Nala 2 & Kali River	Coordination meeting with Project Manager & Assistant Project Manager; reconnaissance of Abu Nala system and downstream Kali River interface.
Day 2	18 Sept 2026	Odeon Nala (ODN) & Kali River	Inspection of ODN Nala, feeder channels, culverts, drain choking/siltation, waterlogging locations & downstream connection to Kali River; observed ongoing DGPS survey.
Day 3	19 Sept 2026	Khadauli Nala / Delhi Road corridor	Inspection of nala near Delhi Road, metro/culvert crossings, secondary-drain connectivity, drainage discontinuity & waterlogging hotspots up to the sports-complex area.

7. Instrument Calibration

The DGPS equipment deployed for the survey has been calibrated and is within the validity period. The calibration certificate has been submitted as supporting documentation for the survey equipment to the concerned Project Manager in charge.

8. Report Status

Report	Status	Comments
Inception Report	Report submitted to Project Manager	Sent on 16th September 2026

9. Static Points



Figure 1: Near Continental India Private Limited (MRT_ST_04)



Figure 2: Near Hanuman Mandir, Samoli (MRT_ST_06)



(a) *(b)*

Figure 3: (a) Near Kali Nadi (MRT_ST_03), (b) Near Delhi - Meerut Expy Flyover, Partapur (MRT_ST_01)



Figure 4: (a) Near Kali Nadi (MRT_ST_03), (b) Near Delhi - Meerut Expy Flyover, Partapur (MRT_ST_01)



Figure 5: Near FAIZ E-AM Inter College, Static DGPS Point (MRT_ST_05)


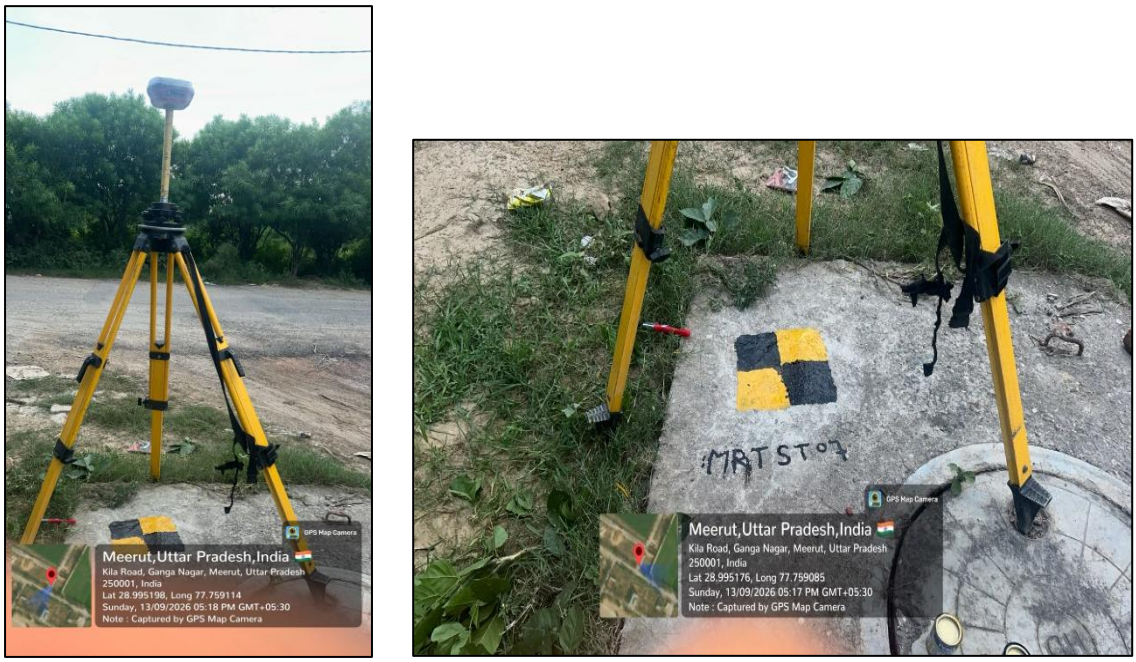


Figure 6: Near IIMT stadium, Static DGPS Point (MRT_ST_05)




Figure 7: Near Anand Niketan, Green City, Daurali (MRT_ST_08)

10. Site Survey Photographs of Second Week (Till 23rd September)

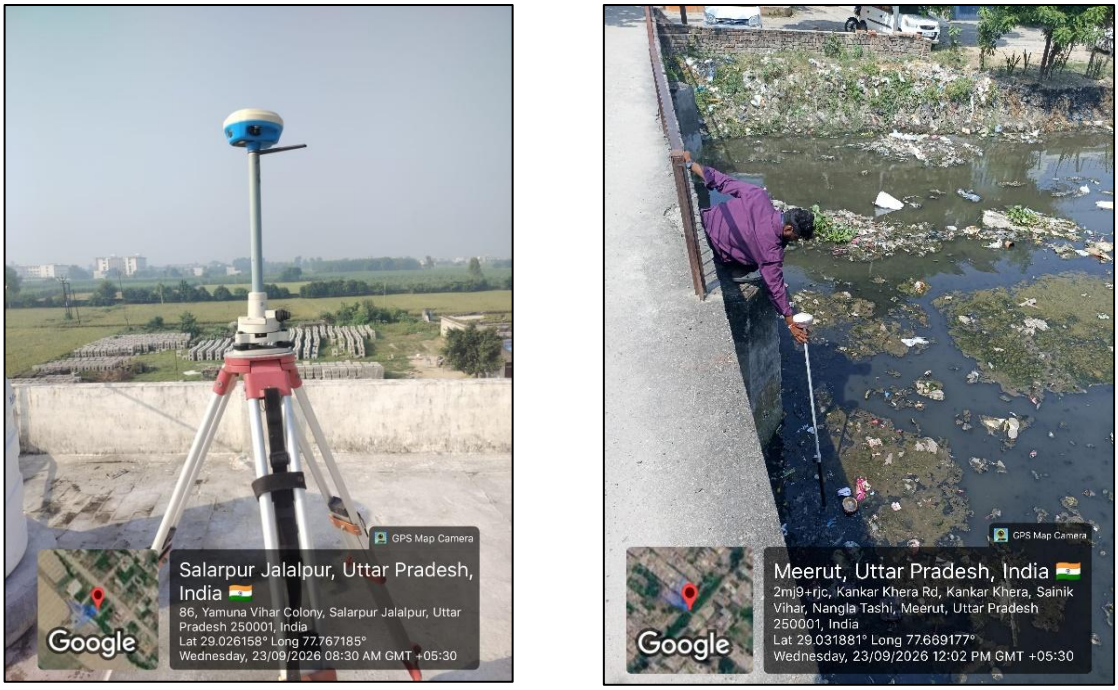



GPS Map Camera
Meerut,UP,India
Devpuri, Devpuri, Meerut, UP 250002, India
Lat 28.976380, Long 77.692493
Wednesday, 23/09/2026 09:45 AM GMT+05:30
Note : Captured by GPS Map Camera


GPS Map Camera
Meerut,UP,India
Nagla Tashi, Sardhana, Meerut, UP 250110, India
Lat 29.054390, Long 77.671508
Wednesday, 23/09/2026 04:01 PM GMT+05:30
Note : Captured by GPS Map Camera

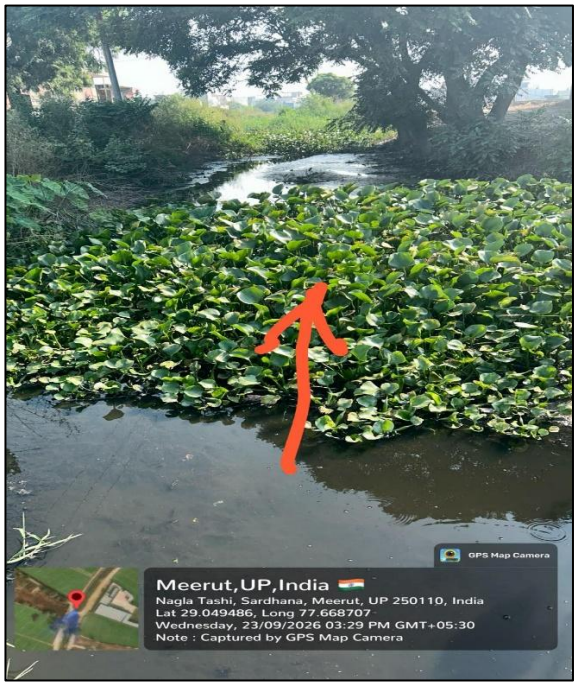
GPS Map Camera
Meerut,UP,India
Nagla Tashi, Sardhana, Meerut, UP 250110, India
Lat 29.049486, Long 77.668707
Wednesday, 23/09/2026 03:29 PM GMT+05:30
Note : Captured by GPS Map Camera


GPS Map Camera
Google
Meerut, Uttar Pradesh, India
Xjwr+gwr, Meerut, Uttar Pradesh 250005, India
Lat 28.996757° Long 77.6417°
Wednesday, 23/09/2026 02:21 PM GMT +05:30


GPS Map Camera
Meerut, Uttar Pradesh, India
65, Near Kaushik Boys Inter College, Army Colony, Meerut, Uttar Pradesh 250001, India
Lat 29.015294° Long 77.672557°
Wednesday, 23/09/2026 10:11 AM GMT +05:30
Google

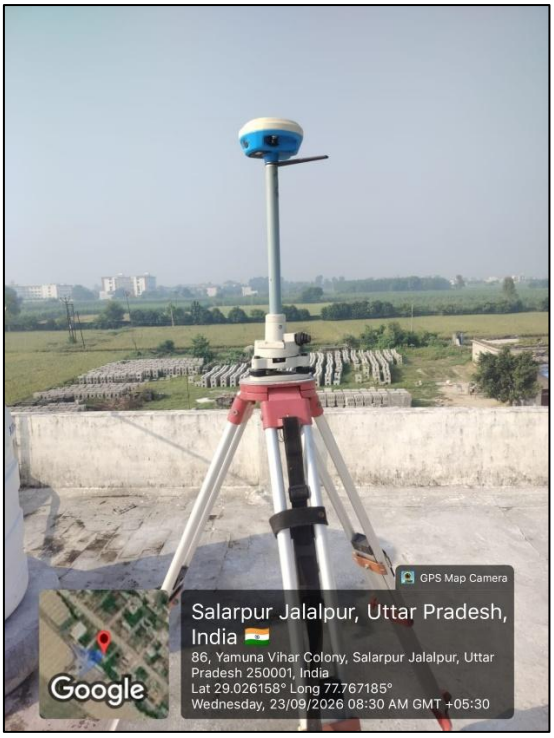
GPS Map Camera
Salarpur Jalalpur, Uttar Pradesh, India
86, Yamuna Vihar Colony, Salarpur Jalalpur, Uttar Pradesh 250001, India
Lat 29.026158° Long 77.767185°
Wednesday, 23/09/2026 08:30 AM GMT +05:30
Google


GPS Map Camera
Meerut, Uttar Pradesh, India
5b, Meerut, Uttar Pradesh 250001, India
Lat 29.023765° Long 77.665092°
Wednesday, 23/09/2026 11:08 AM GMT +05:30
Google

11. Photographic Documentation of Field Reconnaissance



Figure 8: Coordination meeting with the Project Manager & Assistant Project Manager (Day 1)



Figure 9: PriMove survey team with the field surveyors, Meerut



Figure 10: Abu Nala – recorded starting point (28.9986°N, 77.6987°E) | Kali River receiving-water interface (28.9265°N, 77.7563°E)



Figure 11: Waterlogging near Lisari Gate (28.9706°N, 77.7035°E) | Nala passing below metro station, Delhi Road (28.9325°N, 77.6608°E)



Figure 12: Drain discontinuity, Delhi Road (28.9490°N, 77.6753°E) | ~200 m road waterlogging near sports complex (28.9552°N, 77.6807°E)

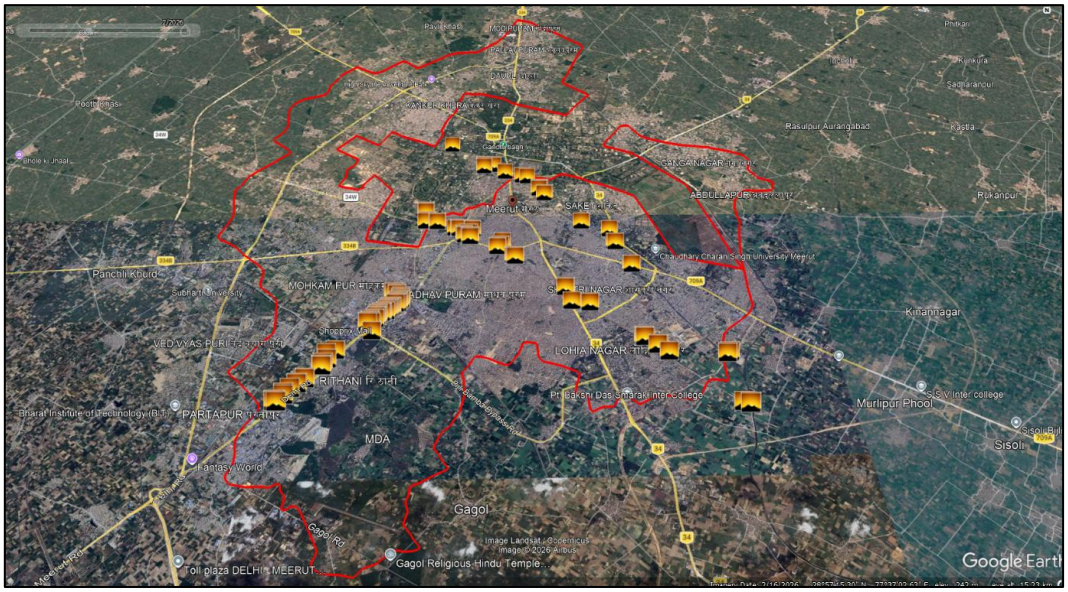


Figure 13: Extent of reconnaissance survey coverage across Meerut Nagar Nigam
