Ref. No.: Pri/ /2026 Date: 16/10/2026

To,
The Project Manager,
Construction & Design Services (C&DS),
Office of Project Manager, Unit– 7,
A-212, Vedvyaspuri Colony, Near Subharti University
Meerut, Uttar Pradesh. (Email -cds.unit7@gmail.com)

Subject: Submission of Weekly Progress Report for Meerut City for the period of 12/10/2026 to 15/10/2026.

Reference:
1. Letter of Acceptance (LOA) Letter No. 2473/G.M.(Ni-9)/e-Tender/2026, dated 10/08/2026 issued by C&DS, U.P. Jal Nigam.
2. Our Acknowledgement Letter no. Pri/1183/2026, dated.18.08.2026

Respected Sir,

With reference to the above-mentioned subject and the meeting held on 18th September 2026, we hereby submit the Weekly Progress Report for the period from 12th to 15th October 2026 for your kind information.

Thanking you,





Sunil Warade
Assistant General Manager

Encl : Weekly Progress Report

Primove Infrastructure Development Consultants Pvt. Ltd.
www.primoveindia.com
C-3, 304 B, Saudamini Complex, Bhusari Colony, Paud Road, Pune 411 038 India
Tel: +91202528 0200 I 01 E: info@primoveindia.com
CIN: U74140PN1999PTC013664

WEEKLY PROGRESS REPORT-MEERUT

Reporting Period: 12/10/2026 to 15/10/2026

Project Name: Survey, Collection of Data, Preparation of Integrated Urban Storm Water Drainage Master Plan (IUSWDMP) and other allied works for **Municipal Corporation Meerut**, Uttar Pradesh, India

1. Progress Summary

Activity	Progress / Status
City area as per RFP	141.94 sq. km
City area as per KML	143.83 sq. km
Static points	- Planned - 8 Nos - Completed - 10 Nos (100%) - Duration – 3 days
GCP points	- Planned - 340 Nos - Completed - 0 Nos (0%) - GCP points will be finalized and provided upon the receipt of LiDAR survey permission and confirmation of the survey area.
LiDAR survey	- To be carried out by helicopter mounted LiDAR. Agency finalization under process.
LiDAR survey Area excluded due to restricted area	- Cantonment Area
DGPS survey	- DGPS commenced on 13/09/2026 - Deployment reported as 1 base and 3 rovers on dated 14/10/2026 - Survey team members – 3 Nos - Calibration report submitted on 22/09/2026
Survey of Primary drains	- Primary Drains As per OSM Planned – 80 km - Completed Length up to previous week:- 85.59 Km (Alignment survey only) - Completed length during the reporting period :– 69.53km (Invert level marking only) - Cumulative length - 85.59 km (100%)
Out Falls identified till date	- 4 Outfalls identified
Road Survey	- Road Length as per OSM Planned - 2458 km - Completed Length up to previous week:- 60.4 Km - Completed length during the reporting period – Nil - Cumulative length – 60.4 km (2.46%)
Secondary /tertiary Drains Covered	- Completed Length up to previous week:- 50.82 Km - Completed length during the reporting period:– Nil - Cumulative length :- 50.82 km
Inception report	- Submitted on 16/09/2026

2. Correspondence and Survey Activities

Activity	Date / Details
LiDAR survey letter submitted by PriMove to PM, C&DS	Will be submitted soon
LiDAR survey – drone details submitted	Will be submitted soon
Police permission received from CP	Will be received soon
LiDAR drone survey flying started (data acquisition)	To be carried out by helicopter mounted LiDAR. Agency finalization under process.
LiDAR drone survey flying completed (data acquisition)	NA
DGPS survey start date	13/09/2026
DGPS calibration report submitted	22/09/2026
Number of DGPS teams deployed	1 base station and 3 rover units
Inception report	16/09/2026
Meeting with PM, C&DS	31/08/2026, 17/09/2026, 29/09/2026
Survey Site Visit by C&DS officials	17/09/2026

3. Drain Survey / Mapping Progress

Item	Progress / Details
Primary drains planned as per OSM	80 km (tentative; as per OSM)
Primary drains completed up to last report	Alignment Survey only - 85.59 km
Primary drains completed during reporting period	Invert level marking only– 69.53 km
Primary drains cumulative total shown	85.59 km
Road length as per OSM planned	2458 km
Road Survey Completed up to last week	60.4 km
Road Survey Completed in this week	Nil
Cumulative length	60.4 km
Secondary drains completed up to last report	46.12 km
Secondary drains completed during reporting period	4.7 km
Secondary drains cumulative total shown	50.82 km
Secondary / tertiary drain areas reported	Ganga Nagar–Kaseru Baksar–Mawana Road Area, Jagriti Vihar–Garh Road–Devpuri–Shastri Nagar Area, Daurli–Roshanpur–Kanker Khera–Lisari–Ved Vyas Puri–Partapur–Sharda Road Area

4. Primary Drain Reaches Completed

- Abu Nala-1 – Begumpul to Begambagh Primary Drain
- Abu Nala-1 – Panchsheel Colony to Nehru Nagar Primary Drain
- Abu Nala-1 – Mohanpuri to Ahmad Nagar Primary Drain
- Abu Nala-1 – Ganga Nagar to Jai Bheem Nagar Primary Drain
- Odean Nala – Ramgarhi to Prabhat Nagar Primary Drain
- Odean Nala – Garh Road to Chanakyapuri Road Primary Drain

- Odean Nala – Ghosipur to Hasanpur–Mirpur Primary Drain
- Abu Nala-2 – Devpuri to Kanker Khera via Nangla Tashi Primary Drain
- Khadauli Nala – Ved Vyas Puri to Sushant City Primary Drain
- Khadauli Nala – Partapur to Shatabdi Nagar Primary Drain

Drain Length Covered under Alignment Survey and Invert Level Verification

- Invert level survey of the primary drains commenced on 06/10/2026, starting with Odean Nala, where a 2.1 km stretch was covered in the initial phase.
- Alignment survey has been completed before 07/10/2026 and it has covered a stretch of 85.59 km in total, and invert level verification for the same is in progress.
- From 07/10/2026 onwards, the invert level survey of the primary drains mentioned above was carried out along Odean Nala, Abu Nala-2 and Khadauli Nala.
- From 12/10/2026 to 15/10/2026, the invert level survey was carried out along Abu Nala-2, Khadauli Nala and Abu Nala-1.
- A total of 69.53km of invert level marking was completed during the reporting period.

5. Survey Progress as on 15/10/2026

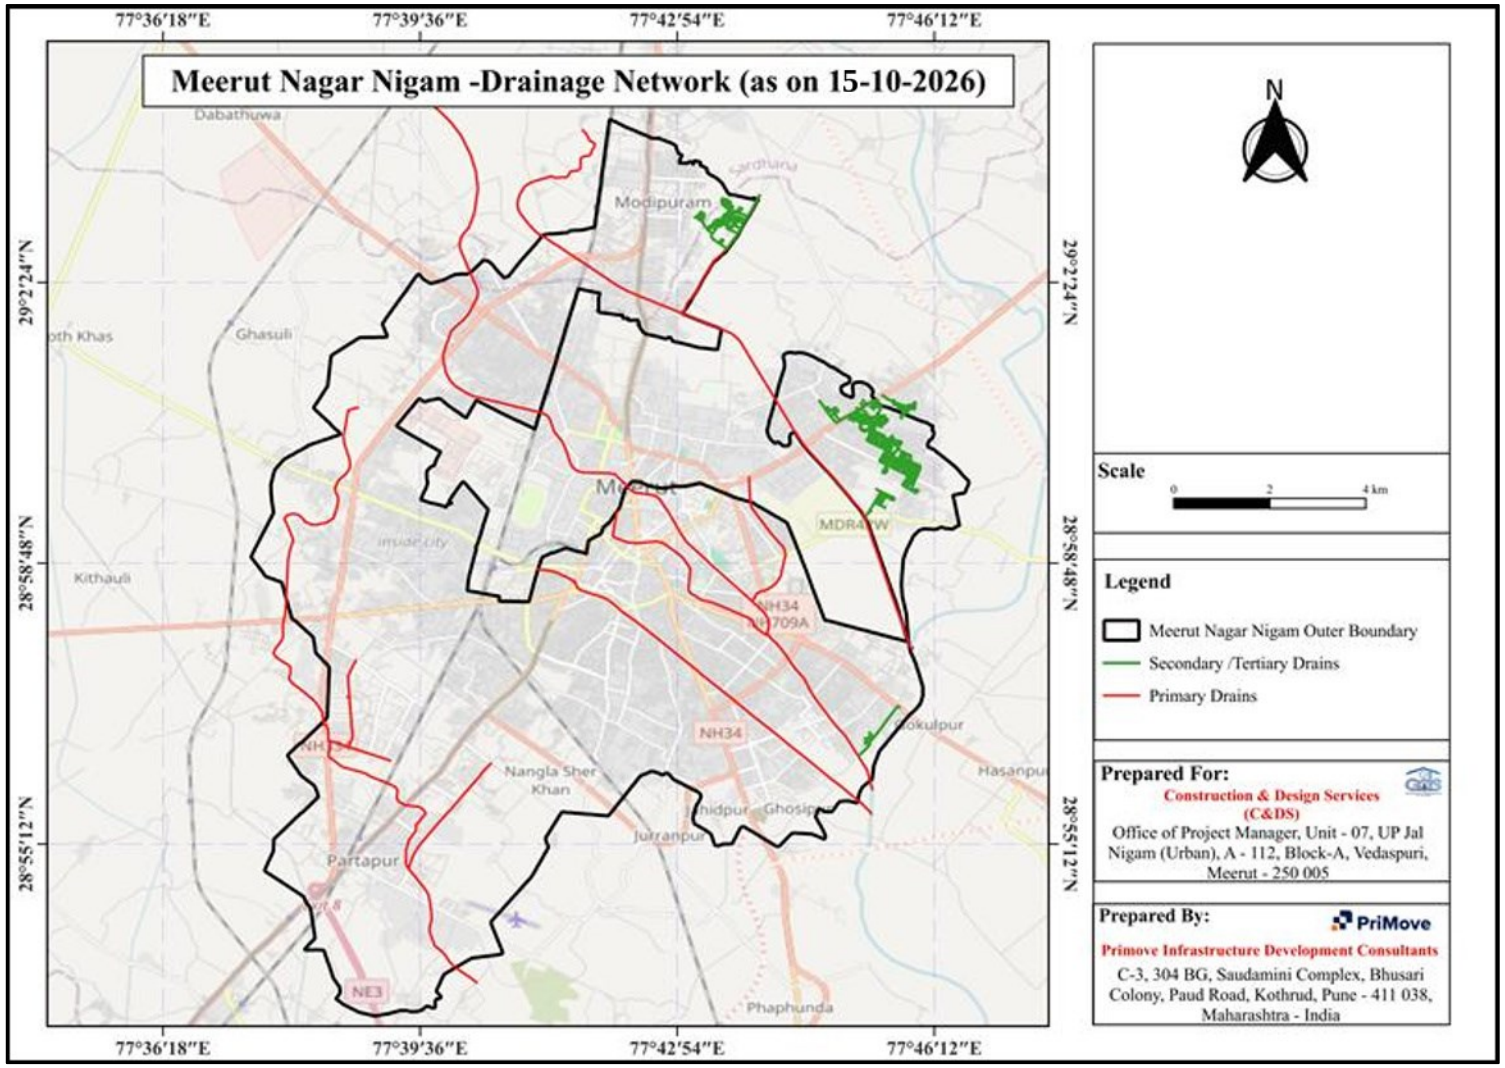


Figure 1- Survey Progress of Meerut Nagar Nigam as on 15-10-2026

6. DGPS Static Points

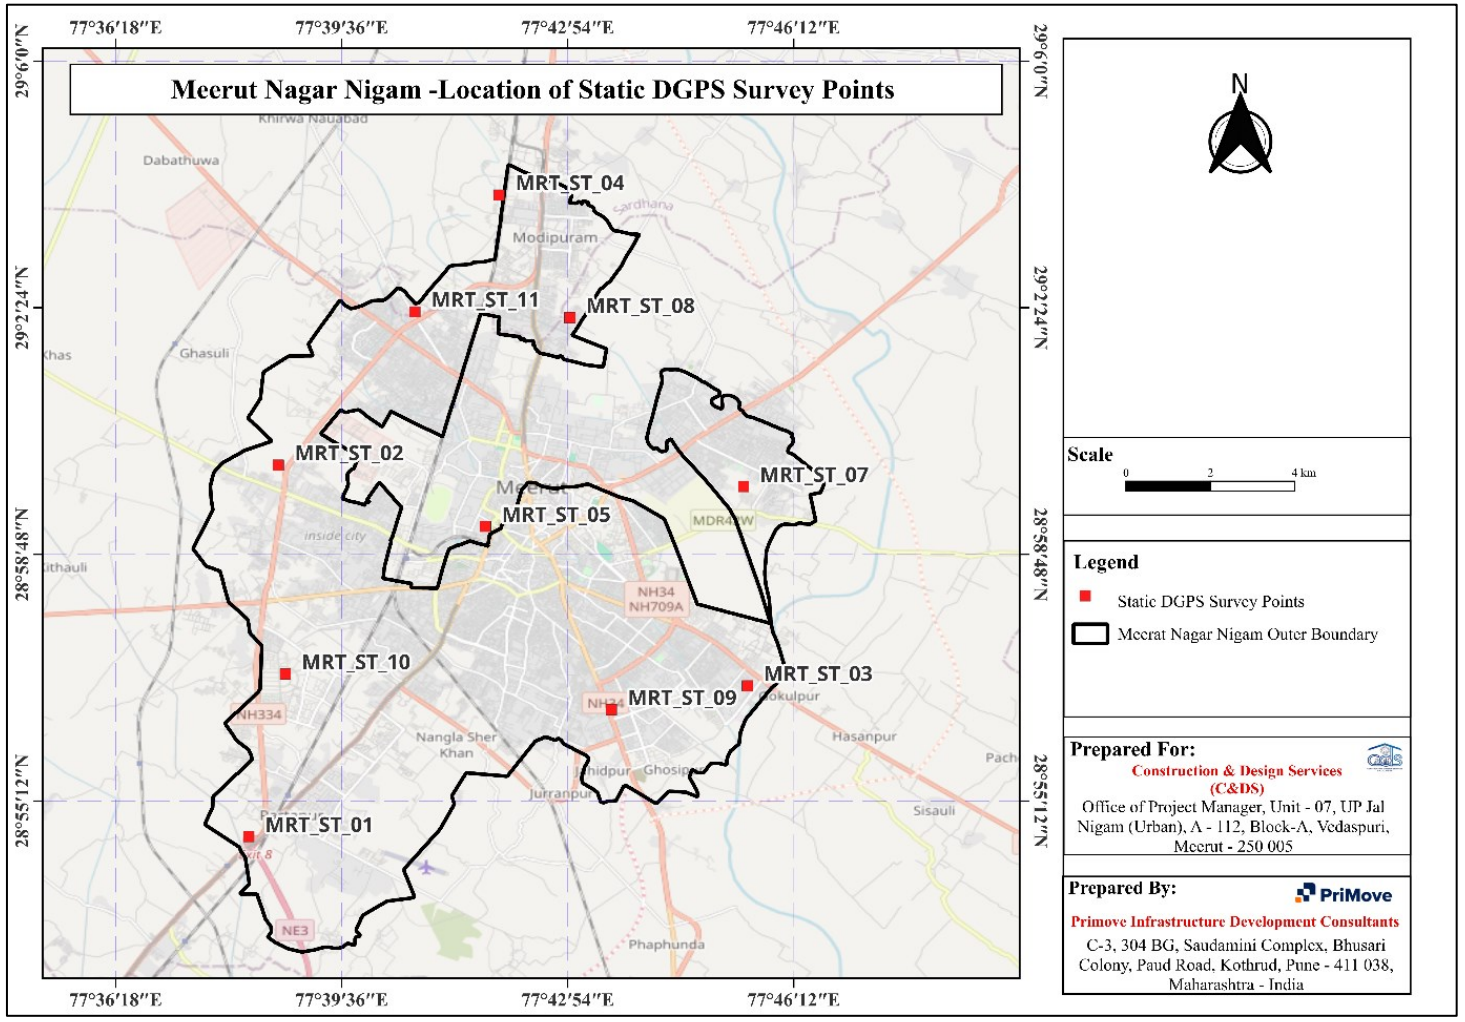


Figure 2- Location of Static DGPS Survey Control Points within Meerut Nagar Nigam

5. Road Survey Completed in wards

Ward No.	Ward Name	Length (km)
31	Shatabdi Nagar	7.2
6	Mohikkampur	2.7
19	Dayanpur	1.1
42	Jain Nagar	0.51
49	Purva Mahavir	0.48
69	Sarai Ladas	0.38
54	Purva Elahi Baksh	0.254
56	Prahalad Nagar	0.85
76	Shyam Nagar Pashchim	0.506
83	Faqudin Ali Ahmed Nagar Pashchimi – 1st	0.42
82	Fakruddin Ali Ahmed Nagar Pashchimi – 1st	0.48
20	Kaserukera	1.52
37	Ganga Nagar	16.9
17	Abdullapur	12.2
7	Peclna Sofipur	2.5
30	Modipuram	2.3
40	Jakuali	0.286
33	Hydle Colony	2.8
79	Kidvai Nagar	0.734
Others	Kali Nadi, Extended length of Abu Nala 2	6.28

6. Survey Plan for Next Week

Primary drains

- Topographical survey and drain invert level measurements along the Abu Nala-1 extension needs to be done.
- Secondary and tertiary drain surveys at the junctions and connecting points of the primary drainage network.

Road survey

Road level survey along the Abu Nala-1 drainage corridor in the identified areas.

7. IMD Data Status

A formal request letter has been submitted to the India Meteorological Department (IMD), Delhi Office, for the procurement of rainfall data pertaining to Meerut Nagar Nigam.

Item	Progress / Details
Submission of request letter to IMD for IDF Curve data	28/09/2026
Payment done for IDF data	15/10/2026
Expected date for receiving IDF data	10 to 15 days

6. Photographs

<table>
<tr><th colspan="2">Primary/Secondary/Tertiary Drains</th></tr>
<tr><td> 

Invert level marking</td><td> 

Blockage in Abu Nala-2</td></tr>
<tr><td> 

Invert level marking</td><td> 

Odeon Nala</td></tr>
</table>

Primary/Secondary/Tertiary Drains



Abu Nala - 2



Invert level marking in Khadauli Nala



Silt deposition in Khadauli Nala



Khadauli Nala Feeder Channel

Primary/Secondary/Tertiary Drains



Invert level marking in Khadauli Nala



Abu Nala-2



Invert level marking in Khadauli Nala



Invert level marking in Khadauli Nala

Primary/Secondary/Tirtiary Drains



Secondary Drain marking



Secondary drain markig

Submitted by: PriMove Infrastructure Consultants Pvt. Ltd. **Date:** 16/10/2026
