Ref. No.: Pri/ /2026 Date: 23/10/2026

To,
The Project Manager,
Construction & Design Services (C&DS),
Office of Project Manager, Unit– 7,
A-212, Vedvyaspuri Colony, Near Subharti University
Meerut, Uttar Pradesh. (Email -cds.unit7@gmail.com)

Subject: Submission of Weekly Progress Report for Meerut City for the period of 16/10/2026 to 22/10/2026.

Reference: 1. Letter of Acceptance (LOA) Letter No. 2473/G.M.(Ni-9)/e-Tender/2026, dated 10/08/2026 issued by C&DS, U.P. Jal Nigam.
2. Our Acknowledgement Letter no. Pri/1183/2026, dated.18.08.2026

Respected Sir,

With reference to the above-mentioned subject and the meeting held on 18th September 2026, we hereby submit the Weekly Progress Report for the period from 16th to 22nd October 2026 for your kind information.

Thanking you,

PRIMOVE Infrastructure Development Consultants Pvt. Ltd. PUNE

Sunil Warade
Assistant General Manager

Encl: Weekly Progress Report

WEEKLY PROGRESS REPORT - MEERUT

Reporting Period: 16/10/2026 to 22/10/2026

Project Name: Survey, Collection of Data, Preparation of Integrated Urban Storm Water Drainage Master Plan (IUSWDMP) and other allied works for **Municipal Corporation Meerut**, Uttar Pradesh, India

1. Progress Summary

Activity	Progress / Status
City area as per RFP	141.94 sq. km
City area as per KML	143.83 sq. km
Static points	- Planned - 8 Nos - Completed - 10 Nos (100%) - Duration – 3 days
LiDAR survey	- To be carried out by helicopter mounted LiDAR. Agency finalization under process.
DGPS survey	- DGPS commenced on 13/09/2026 - Deployment reported as 1 base and 2 rovers - Calibration report submitted on 22/09/2026
Survey of Primary drains	- Primary Drains As per OSM Planned – 80 km - Completed Length up to previous week: - 69.53 km - Completed length during the reporting period: – Nil (Surveyor was unavailable due to medical reason) - Cumulative length: - 69.53 km
Out Falls identified till date	- 4 Outfalls identified
Road Survey	- Road Length as per OSM Planned - 2458 km - Completed Length up to previous week: - 60.4 Km - Completed length during the reporting period – 21.72 km - Cumulative length – 82.12 km
Secondary /tertiary Drains Covered	- Completed Length up to previous week: - 50.82 Km - Completed length during the reporting period: – 14.15 - Cumulative length: - 64.97 km
Inception report	- Submitted on 16/09/2026

2. Correspondence and Survey Activities

Activity	Date / Details
LiDAR survey flying started (data acquisition)	To be carried out by helicopter mounted LiDAR. Agency finalization under process.
DGPS survey start date	13/09/2026

DGPS calibration report submitted	22/09/2026
Number of DGPS teams deployed	1 base station and 2 rover units
Inception report	16/09/2026
Meeting with PM, C&DS	31/08/2026, 17/09/2026, 29/09/2026
Survey Site Visit by C&DS officials	17/09/2026

3. Drain Survey / Mapping Progress

Item	Progress / Details
Primary drains planned as per OSM	80 km (tentative; as per OSM)
Primary drains completed up to last report	69.53 km
Primary drains completed during reporting period	Nil
Primary drains cumulative total shown	69.53 km
Road length as per OSM planned	2458 km
Road Survey Completed up to last week	60.4 km
Road Survey Completed this week	21.72 km
Cumulative length	82.12 km
Secondary / tertiary drains completed up to last report	50.82 km
Secondary / tertiary drains completed during reporting period	14.15 km
Secondary drains cumulative total shown	64.97 km
Secondary / tertiary drain areas reported	Ganga Nagar–Kaseru Baksar–Mawana Road Area, Jagriti Vihar–Garh Road–Devpuri–Shastri Nagar Area, Daurli–Roshanpur–Kanker Khera–Lisari–Ved Vyas Puri–Partapur–Sharda Road Area, Meenakshi Puram Road, Rakshapuram Main Road, Street No.1 to 6 near Amhera Road.

4. Primary Drain Reaches Completed

- Abu Nala-1 – Begumpul to Begambagh Primary Drain
- Abu Nala-1 – Panchsheel Colony to Nehru Nagar Primary Drain
- Abu Nala-1 – Mohanpuri to Ahmad Nagar Primary Drain
- Abu Nala-1 – Ganga Nagar to Jai Bheem Nagar Primary Drain
- Odean Nala – Ramgarhi to Prabhat Nagar Primary Drain
- Odean Nala – Garh Road to Chanakyapuri Road Primary Drain
- Odean Nala – Ghosipur to Hasanpur–Mirpur Primary Drain
- Abu Nala-2 – Devpuri to Kanker Khera via Nangla Tashi Primary Drain
- Khadauli Nala – Ved Vyas Puri to Sushant City Primary Drain
- Khadauli Nala – Partapur to Shatabdi Nagar Primary Drain
- City Nala – East side of the Abu Nala-2

5. Survey Progress as on 22/10/2026

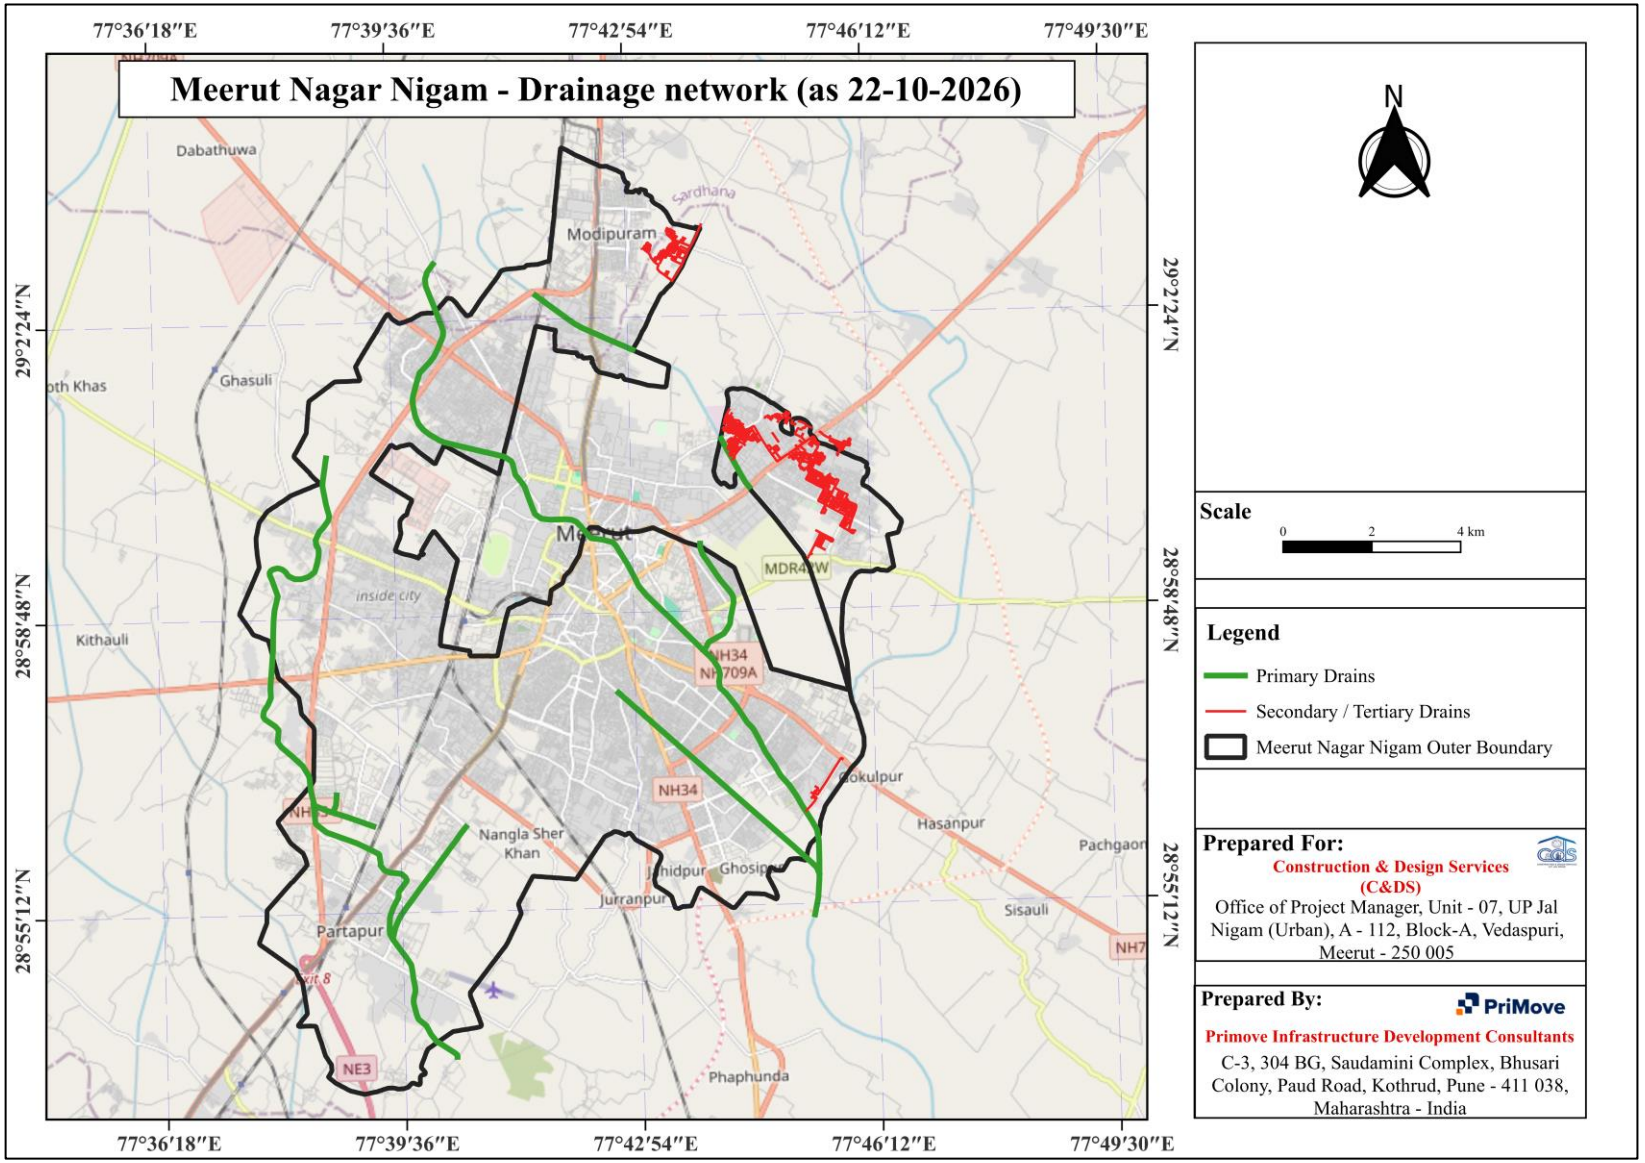


Figure 1- Survey Progress of Meerut Nagar Nigam as on 22-10-2026

6. DGPS Static Points

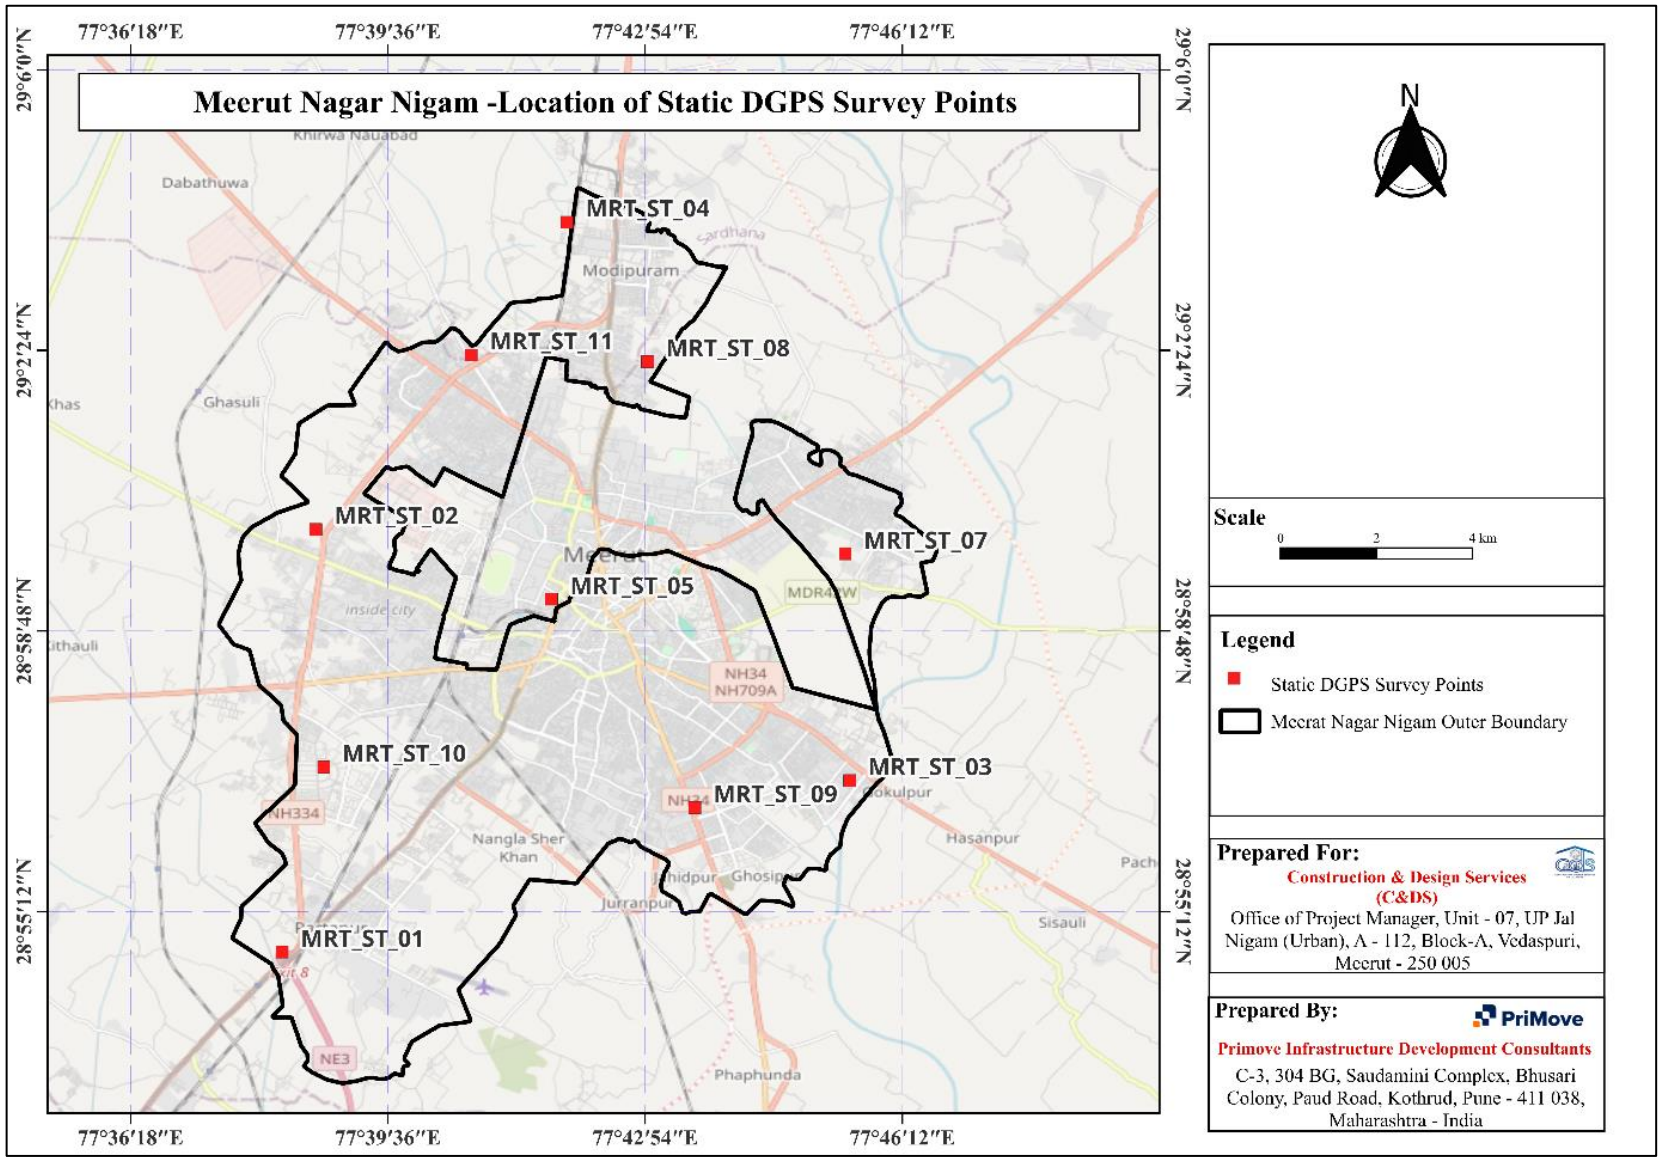


Figure 2- Location of Static DGPS Survey Control Points within Meerut Nagar Nigam

5. Road Survey Completed in wards

Ward No.	Ward Name	Length (km)
3	Islam Nagar	0.21
4	Laxmanpuri	0.67
6	Shiv Hari Mandir	2.39
7	Mehandi Mohalla	1.46
13	Jawahar Nagar	0.11
14	Prem Pryag Colony	0.40
16	Indra Colony	0.41
17	Janakpuri, Sports Colony	11.74
18	Mukarrab Husain, Dwarikapuri	6.06
19	Bazar	0.79
20	Ansal Colony	22.18
26	Kaseru Baksar	0.05
30	Subhash nagar	1.46
31	Modipuram	1.98
33	Hydle Colony	2.64
37	Humanion Nagar	15.72
42	Badrishpuram	0.09
45	Shivpuri	0.86
49	Anoopnagar Fazalpur	0.08
54	Ward 54	0.05
56	Uday Singh	0.74
59	Hanumanpuri	0.23
60	Jai Devi Nagar	0.01
64	Shastri Nagar (K-1,2,3,4,5)	0.00
76	Bel Pathar Colony	0.85
79	Veeru chah	0.58
82	Idgah Colony	0.28
83	Ashiyana Colony	0.42
86	Zakir Hussain Colony Uttari	0.10

6. Survey Plan for Next Week

Primary drains

- City Nala 2 Invert Level is planned to be completed with additional arrangements.
- Catchment contributing to secondary drains which connects to Abu Nala 2 in the upstream section has been targeted to be completed. Target area is demarcated and shared to survey team.

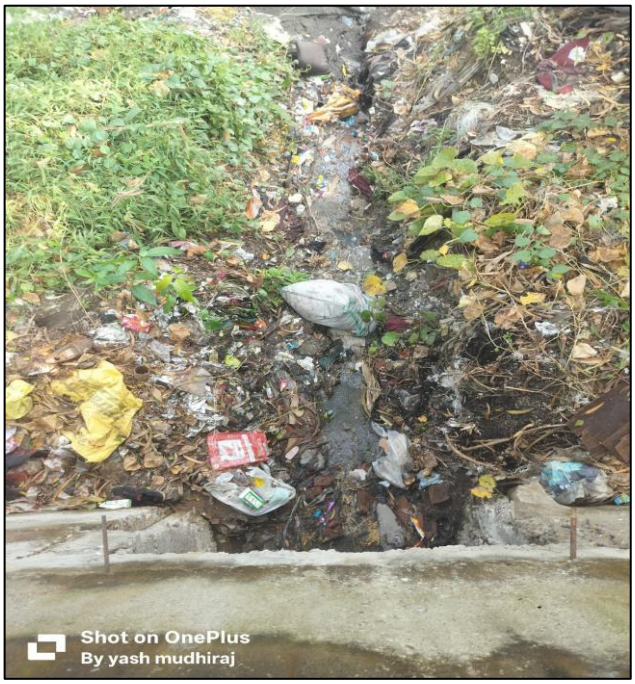
7. IMD Data Status

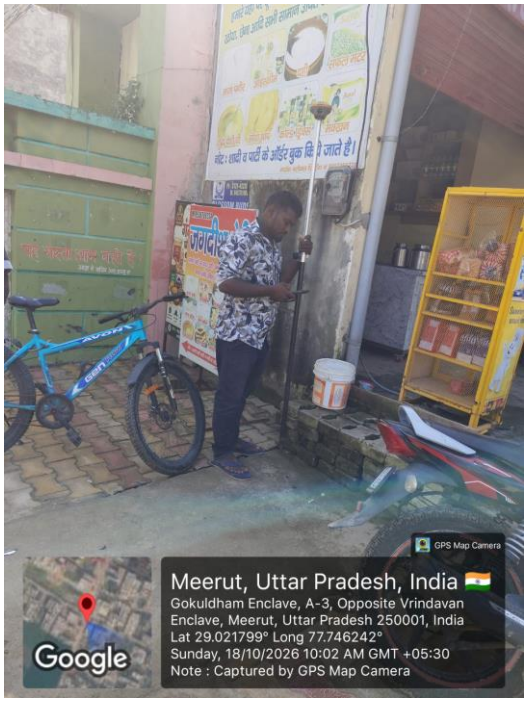
A formal request letter has been submitted to the India Meteorological Department (IMD), Delhi Office, for the procurement of rainfall data pertaining to Meerut Nagar Nigam.

Item	Progress / Details
Submission of request letter to IMD for IDF Curve data	28/09/2026
Payment done for IDF data	15/10/2026
Expected date for receiving IDF data	10 to 15 days

6. Photographs

<table>
<tr><th colspan="2">Primary/Secondary/Tertiary Drains</th></tr>
<tr><td> 

Flow Direction marking</td><td> 

Blockage in Abu Nala-2</td></tr>
<tr><td> 

Rim level marking</td><td> 

Odeon Nala</td></tr>
</table>

Primary/Secondary/Tertiary Drains



Abu Nala - 2



Invert level marking in Khadauli Nala



Silt deposition in Khadauli Nala



Khadauli Nala Feeder Channel

Primary/Secondary/Tertiary Drains



Invert level marking in Khadauli Nala



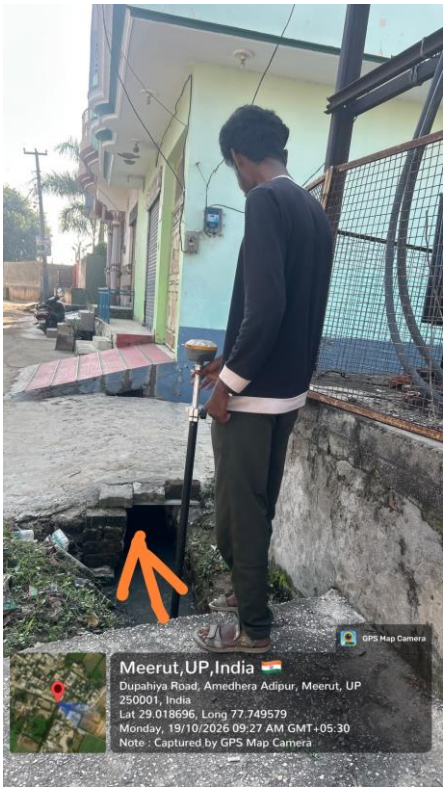
Abu Nala-2



Invert level marking in Khadauli Nala



Invert level marking in Khadauli Nala

Primary/Secondary/Tirtiary Drains	
	
Secondary Drain marking	**Secondary drain markig**

Submitted by: PriMove Infrastructure Consultants Pvt. Ltd. **Date:** 23/10/2026
