Ref. No.: Pri/ /2026 Date: 30/10/2026

To,
The Project Manager,
Construction & Design Services (C&DS),
Office of Project Manager, Unit– 7,
A-212, Vedvyaspuri Colony, Near Subharti University
Meerut, Uttar Pradesh. (Email -cds.unit7@gmail.com)

Subject: Submission of Weekly Progress Report for Meerut City for the period of 23/10/2026 to 29/10/2026.

Reference:
1. Letter of Acceptance (LOA) Letter No. 2473/G.M.(Ni-9)/e-Tender/2026, dated 10/08/2026 issued by C&DS, U.P. Jal Nigam.
2. Our Acknowledgement Letter no. Pri/1183/2026, dated.18.08.2026

Respected Sir,

With reference to the above-mentioned subject and the meeting held on 18th September 2026, we hereby submit the Weekly Progress Report for the period from 23rd to 29th October 2026 for your kind information.

Thanking you,



Sunil Warade
Assistant General Manager

Encl: Weekly Progress Report

Primove Infrastructure Development Consultants Pvt. Ltd.
www.primoveindia.com
C-3, 304 B, Saudamini Complex, Bhusari Colony, Paud Road, Pune 411 038 India
Tel: +91202528 0200 I 01 E: info@primoveindia.com
CIN: U74140PN1999PTC013664

WEEKLY PROGRESS REPORT - MEERUT

Reporting Period: 23/10/2026 to 29/10/2026

Project Name: Survey, Collection of Data, Preparation of Integrated Urban Storm Water Drainage Master Plan (IUSWDMP) and other allied works for **Municipal Corporation Meerut**, Uttar Pradesh, India

1. Progress Summary

Activity	Progress / Status
City area as per RFP	141.94 sq. km
City area as per KML	143.83 sq. km
Static points	- Planned - 10 Nos - Completed - 10 Nos (100%) - Duration – 3 days
LiDAR survey	- To be carried out by helicopter mounted LiDAR. Agency finalization under process.
DGPS survey	- DGPS commenced on 13/09/2026 - Deployment reported as 1 base and 6 rovers - Calibration report submitted on 22/09/2026
Survey of Primary drains	- Primary Drains As per OSM Planned – 80 km - Completed Length up to previous week: - 69.53 km - Completed length during the reporting period: – Nil - Cumulative length: - 69.53 km
Out Falls identified till date	- 6 Outfalls identified
Road Survey	- Road Length as per OSM Planned - 2458 km - Completed Length up to previous week: - 82.12 Km - Completed length during the reporting period – 30.50 km - Cumulative length – 112.62 km
Secondary /Tertiary Drains Covered	- Completed Length up to previous week: - 64.97 Km - Completed length during the reporting period: – 46.21 Km - Cumulative length: - 111.18 km
Days when rainfall occurred	- 29/10/2026 (Work resumed after rain)
Inception report	- Submitted on 16/09/2026

2 Correspondence and Survey Activities

Activity	Date / Details
LiDAR survey flying started (data acquisition)	To be carried out by helicopter mounted LiDAR. Agency finalization under process.
DGPS survey start date	13/09/2026
DGPS calibration report submitted	22/09/2026
Number of DGPS teams deployed	1 base station and 6 rover units
Inception report	16/09/2026
Meeting with PM, C&DS	31/08/2026, 17/09/2026, 29/09/2026
Survey Site Visit by C&DS officials	17/09/2026

3 Drain Survey / Mapping Progress

Item	Progress / Details
Primary drains planned as per OSM	80 km (tentative; as per OSM)
Primary drains completed up to last report	69.53 km
Primary drains completed during reporting period	Nil
Primary drains cumulative total shown	69.53 km
Road length as per OSM planned	2458 km
Road Survey Completed up to last week	82.12km
Road Survey Completed this week	30.50 km
Cumulative length	112.62 km
Secondary / Tertiary drains completed up to last report	64.97 km
Secondary / Tertiary drains completed during reporting period	46.21 km
Secondary drains cumulative total shown	111.18 km
Secondary / tertiary drain areas reported	Ritani to Brahmpuri Stretch, Gagol Road; Katai Mill; Kashi; Reda Basti; Ahmed Nagar; Achronda; Shatabdi Nagar-4E; Shivpuram; Nai Basti Chauhanpuri, Ganga Nagar–Kaseru Baksar–Mawana Road Area, Jagriti Vihar–Garh Road–Devpuri–Shastri Nagar Area, Daurli–Roshanpur–Kanker Khera–Lisari–Ved Vyas Puri–Partapur–Sharda Road Area, Meenakshi Puram Road, Rakshapuram Main Road, Street No.1 to 6 near Amhera Road.

4 Primary Drain Reaches Completed

- Abu Nala-1 – Begumpul to Begambagh Primary Drain
- Abu Nala-1 – Panchsheel Colony to Nehru Nagar Primary Drain
- Abu Nala-1 – Mohanpuri to Ahmad Nagar Primary Drain
- Abu Nala-1 – Ganga Nagar to Jai Bheem Nagar Primary Drain
- Odean Nala – Ramgarhi to Prabhat Nagar Primary Drain

- Odean Nala – Garh Road to Chanakyapuri Road Primary Drain
- Odean Nala – Ghosipur to Hasanpur–Mirpur Primary Drain
- Abu Nala-2 – Devpuri to Kanker Khera via Nangla Tashi Primary Drain
- Khadauli Nala – Ved Vyas Puri to Sushant City Primary Drain
- Khadauli Nala – Partapur to Shatabdi Nagar Primary Drain
- City Nala – East side of the Abu Nala-2

5 Survey Progress as on 29/10/2026

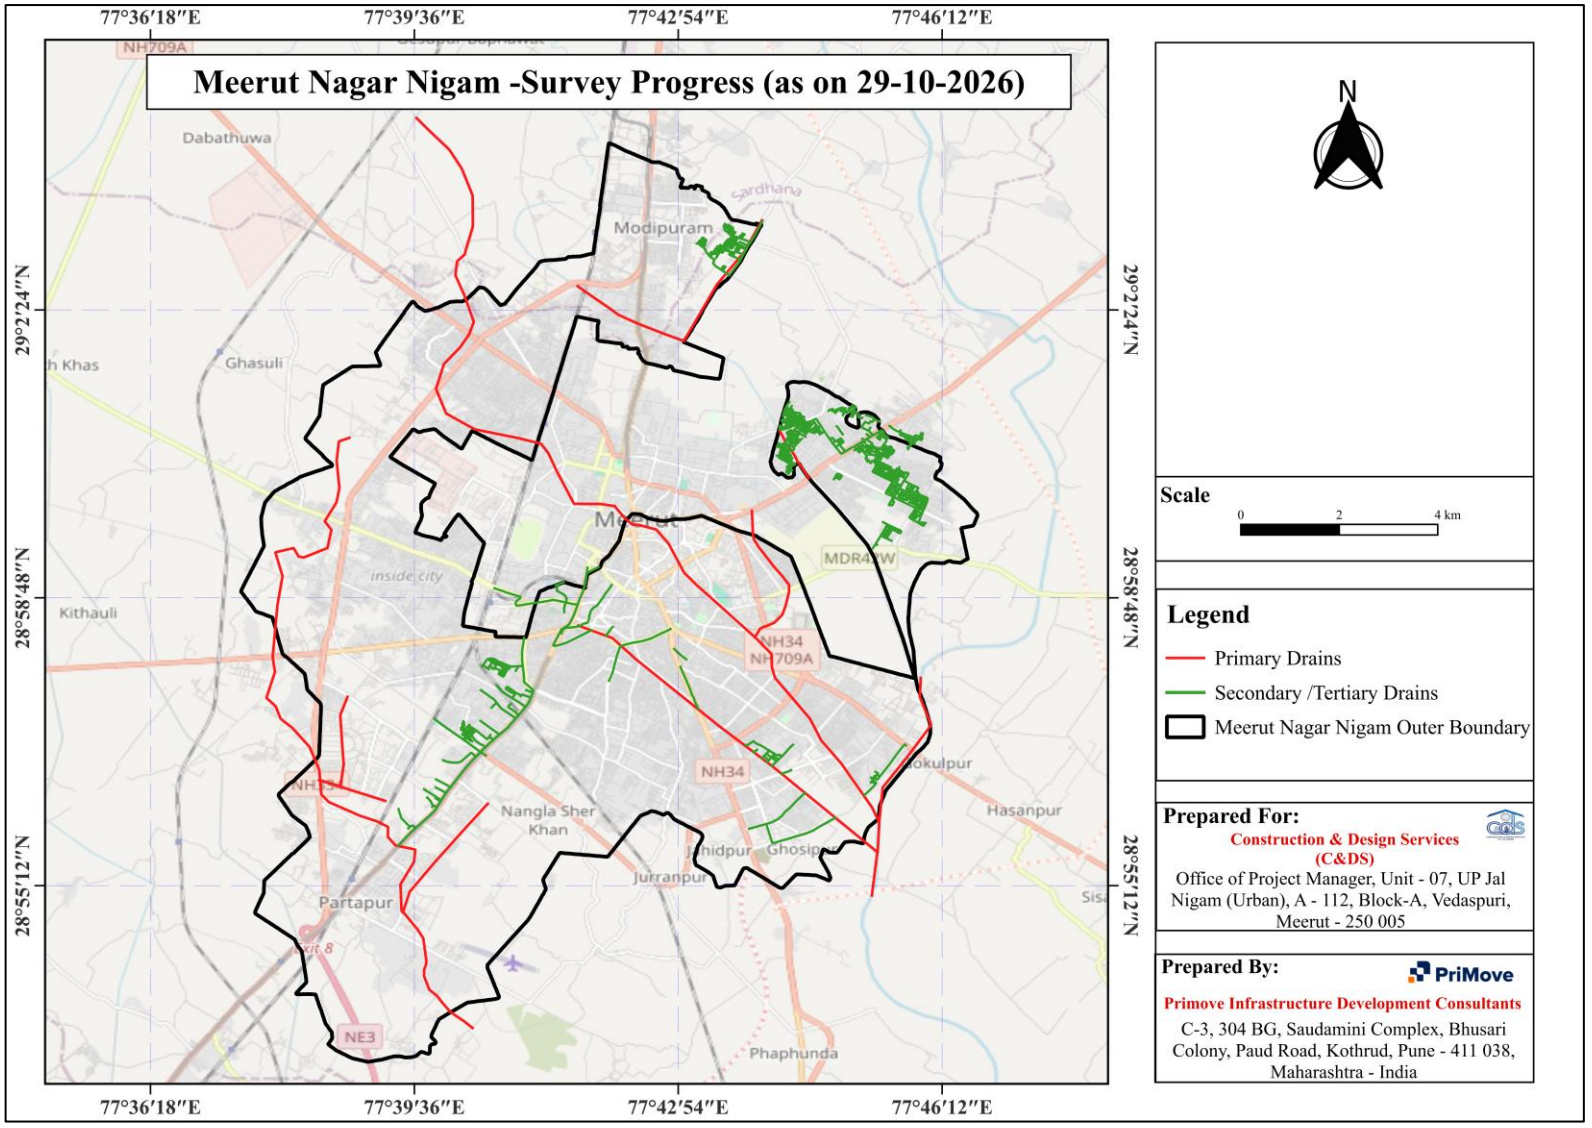


Figure 1- Survey Progress of Meerut Nagar Nigam as on 29-10-2026

6 DGPS Static Points

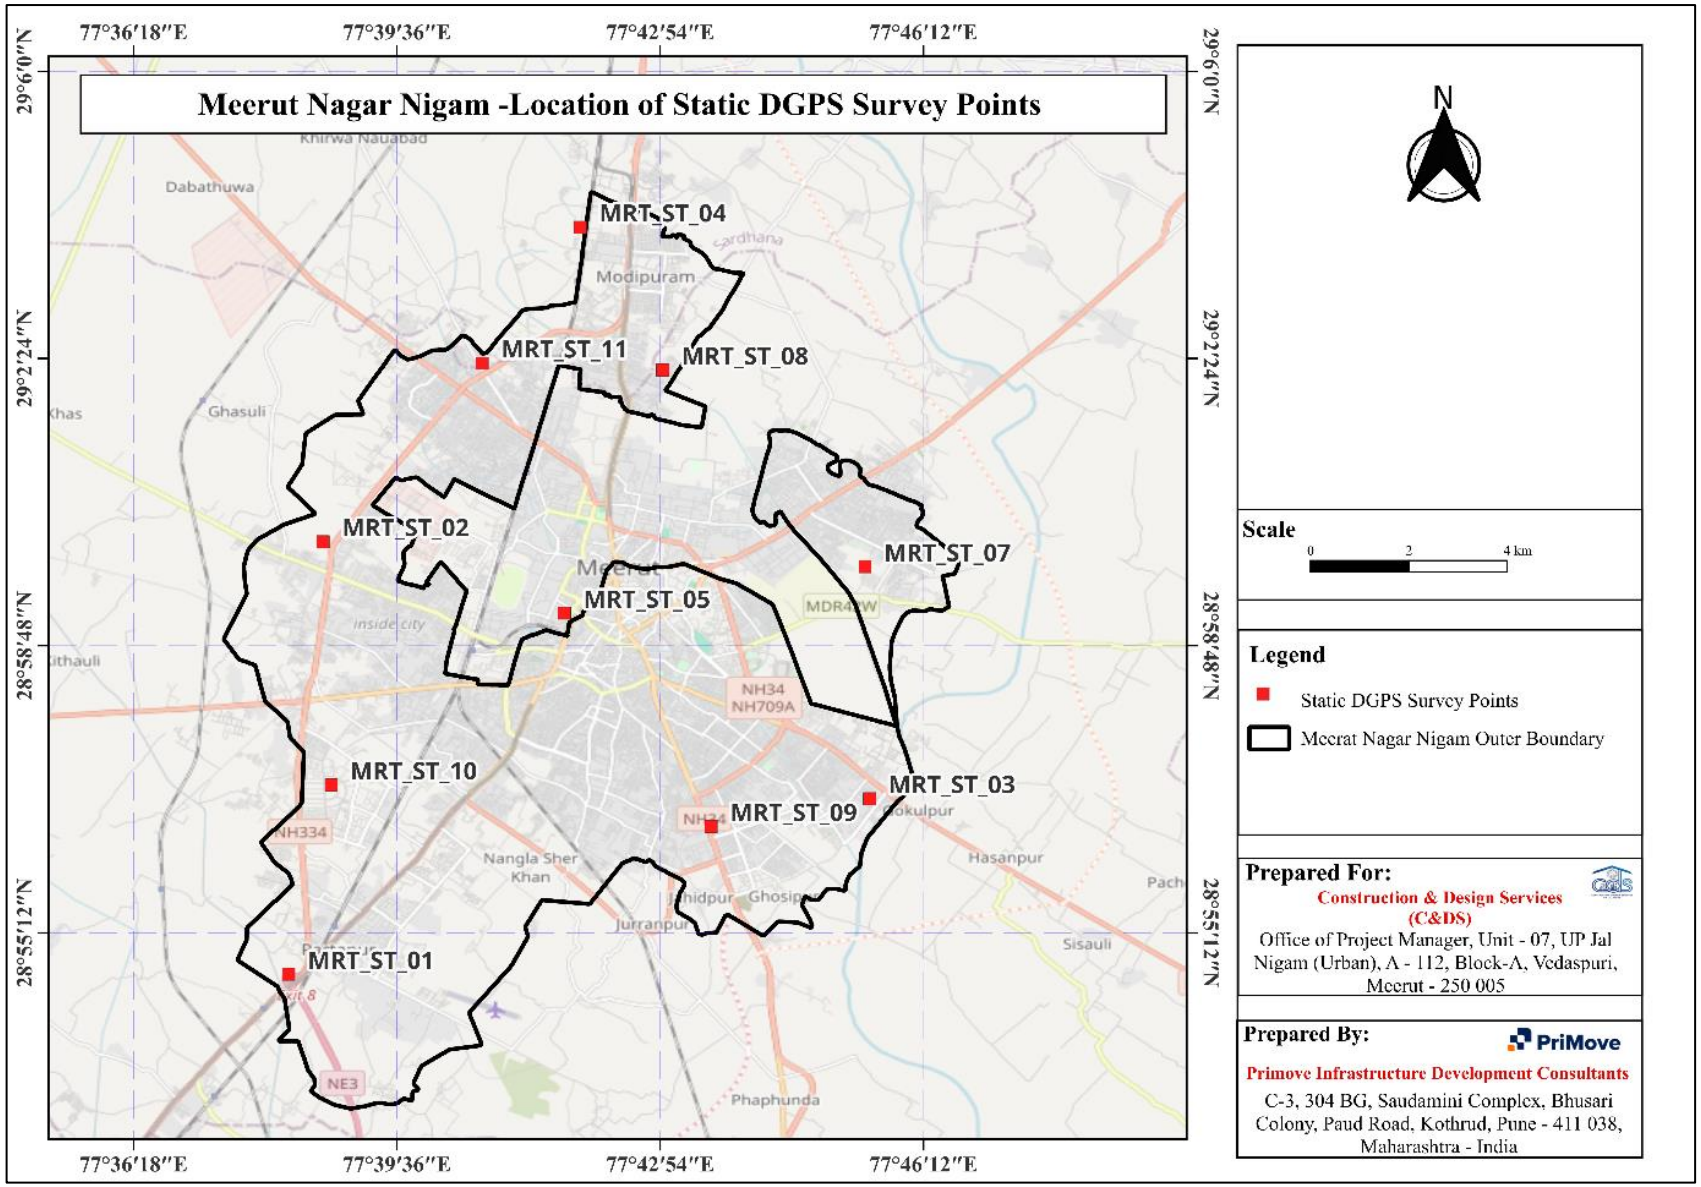


Figure 2- Location of Static DGPS Survey Control Points within Meerut Nagar Nigam

7 Road Survey Completed in wards

Ward No.	Ward Name	Road Length (km)
3	Islam Nagar	1.07
4	Laxmanpuri	2.22
6	Shiv Hari Mandir	12.68
7	Mehandi Mohalla	1.46
11	Gagol Road	1.16
13	Jawahar Nagar	0.12
14	Prem Pryag Colony	0.4
16	Indra Colony	0.41
17	Janakpuri, Sports Colony	11.76
18	Mukarrab Husain, Dwarikapuri	6.08
19	Bazar	0.79
20	Ansal Colony	26.89
24	subhashpuri	0.45
26	Kaseru Baksar	0.05
28	Muqarrabpur Palhera	0.33
30	Subhash nagar	1.46
31	Modipuram	2.32
33	Hydle Colony	5.43
34	Ghosipur	0.02
35	Prem Vihar	0.5
37	Humanion Nagar	15.75
39	Rampur Pavti	0.81
42	Badrishpuram	1.06
45	Shivpuri	0.86
49	Anoopnagar Fazalpur	0.65
51	Pragati Nagar	0.41
54	Ward 54	0.06
56	Uday Singh	1.58
59	Hanumanpuri	0.22
60	Jai Devi Nagar	0.01
63	Indra Nagar IInd	1.58
70	Lala Ka Bazar	0.28
71	Chatta Anantram	0.28
72	Purwa Peer Baksh	0.34
74	Zaidi Society	0.16
76	Bel Pathar Colony	1.23
79	Veeru chah	1.33
82	Idgah Colony	0.28
83	Ashiyana Colony	0.42
86	Zakir Hussain Colony Uttari	0.11

8 Survey Plan for Next Week

Secondary/Tertiary drains

1. City Nala Stretch – West Side of Abu Nala 2
2. Survey of secondary drains of the Odean Nala is planned to cover.
3. Downstream section of Abu Nala 1 by deploying additional labor for accessibility to drain banks
4. The topographical survey for the secondary and tertiary drains along the Brahmpuri to Ritani stretch will progress with the remaining 3 rovers.

9 IMD Data Status

A formal request letter has been submitted to the India Meteorological Department (IMD), Delhi Office, for the procurement of rainfall data pertaining to Meerut Nagar Nigam. Additionally, a forwarding letter dt. 16/10/2026 has been issued by C&DS to facilitate and expedite the data procurement process.


Item	Progress / Details
Submission of request letter to IMD for IDF Curve data	28/09/2026
Payment done for IDF data	15/10/2026
Expected date for receiving IDF data	15/11/2026

10 Photographs

Primary/Secondary/Tertiary Drains






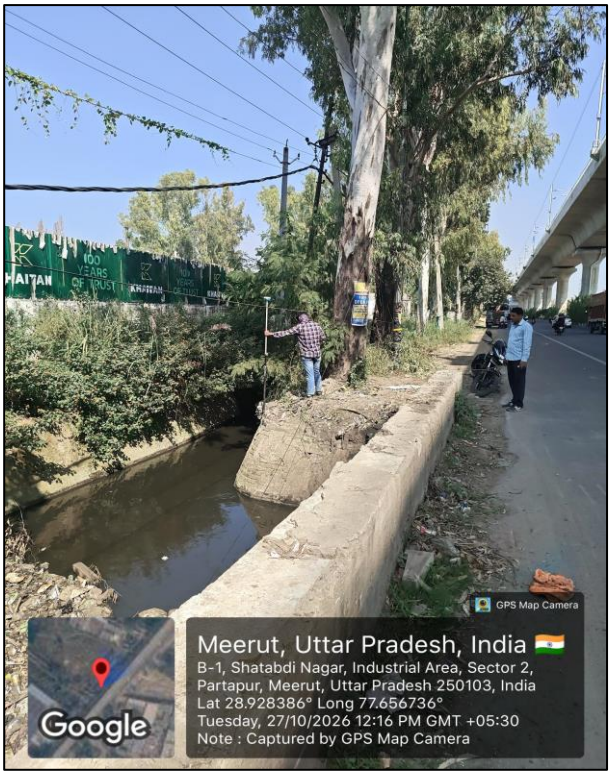



Primary/Secondary/Tertiary Drains



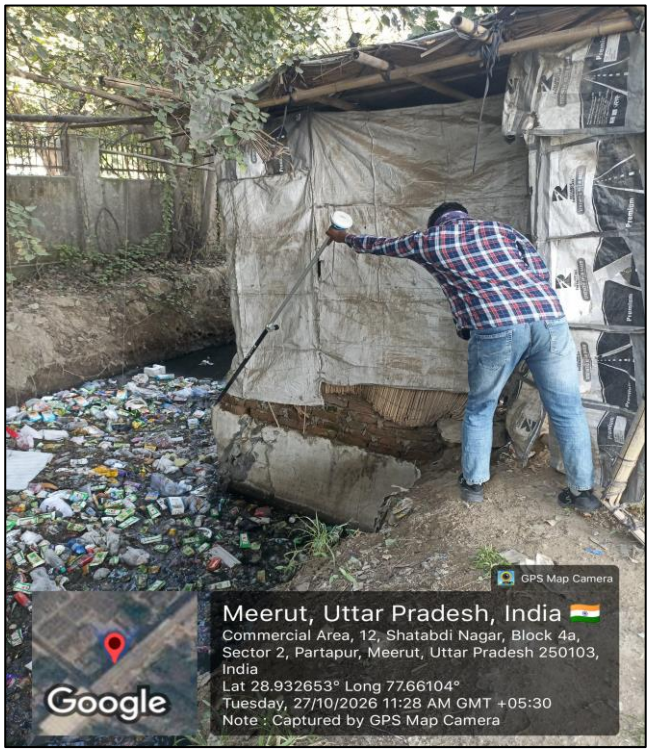





Primary/Secondary/Tertiary Drains









Primary/Secondary/Tertiary Drains	
	

Submitted by: PriMove Infrastructure Consultants Pvt. Ltd. **Date:** 30/10/2026
