Ref. No.: Pri/ /2026 Date: 06/11/2026

To,
The Project Manager,
Construction & Design Services (C&DS),
Office of Project Manager, Unit– 7,
A-212, Vedvyaspuri Colony, Near Subharti University
Meerut, Uttar Pradesh. (Email -cds.unit7@gmail.com)

Subject: Submission of Weekly Progress Report for Meerut City for the period of 30/10/2026 to 05/11/2026.

Reference:
1. Letter of Acceptance (LOA) Letter No. 2473/G.M.(Ni-9)/e-Tender/2026, dated 10/08/2026 issued by C&DS, U.P. Jal Nigam.
2. Our Acknowledgement Letter no. Pri/1183/2026, dated.18.08.2026

Respected Sir,

With reference to the above-mentioned subject and the meeting held on 18th September 2026, we hereby submit the Weekly Progress Report for the period from 30th October to 05th November 2026 for your kind information.

Thanking you,

PRIMOVE Infrastructure Development Consultants Pvt. Ltd. PUNE

Sunil Warade
Assistant General Manager

Encl: Weekly Progress Report

WEEKLY PROGRESS REPORT - MEERUT

Reporting Period: 30/10/2026 to 05/11/2026

Project Name: Survey, Collection of Data, Preparation of Integrated Urban Storm Water Drainage Master Plan (IUSWDMP) and other allied works for **Municipal Corporation Meerut**, Uttar Pradesh, India

1. Progress Summary

Activity	Progress / Status
City area as per RFP	141.94 sq. km
City area as per KML	143.83 sq. km
Static points	- Planned - 10 Nos - Completed - 10 Nos (100%) - Duration – 3 days
LiDAR survey	- To be carried out by helicopter mounted LiDAR. Agency finalization under process.
DGPS survey	- DGPS commenced on 13/09/2026 - Deployment reported as 1 base and 6 rovers for 30th and 31st October and rest of the days 1 base and 4 rovers - Calibration report submitted on 22/09/2026
Survey of Primary drains	- Completed Length up to previous week: - 69.53 km (with invert) of total 85.59 km (with alignment only) - Completed length during the reporting period – 5.13 km - Survey awaited as; 1. Require permission from Cantonment area, 2. Inaccessible banks of Abu Nala 1 approx. 5km U/S outfall location at Kali Nadi - Cumulative length: - 74.66 km (with invert) of total 85.59 km (with alignment only)
Out Falls identified till date	- 4 Outfalls identified
Road Survey	- Road Length as per OSM Planned - 2458 km - Completed Length up to previous week: - 112.62 Km - Completed length during the reporting period – 49.98 km - Cumulative length – 162.6 km
Secondary /Tertiary Drains Covered	- Completed Length up to previous week: - 111.18 Km - Completed length during the reporting period: – 117.54 Km - Cumulative length: - 228.72 km
Days when rainfall occurred	- Nil
Inception report	- Submitted on 16/09/2026

Correspondence and Survey Activities

Activity	Date / Details
LiDAR survey flying started (data acquisition)	To be carried out by helicopter mounted LiDAR. Agency finalization under process.
DGPS survey start date	13/09/2026
DGPS calibration report submitted	22/09/2026
Number of DGPS teams deployed	1 base and 6 rovers for 30th and 31st October and rest of the days 1 base and 4 rovers.
Inception report	16/09/2026
Meeting with PM, C&DS	31/08/2026, 17/09/2026, 29/09/2026
Survey Site Visit by C&DS officials	17/09/2026

2 Drain Survey / Mapping Progress

Item	Progress / Details
Primary drains planned as per OSM	80 km (tentative; as per OSM)
Primary drains completed up to last report	69.53 km
Primary drains completed during reporting period	5.13 km
Primary drains cumulative total shown	74.66 km
Road length as per OSM planned	2458 km
Road Survey Completed up to last week	112.62 km
Road Survey Completed this week	49.98 km
Cumulative length of road survey completed	162.6 km
Secondary / Tertiary drains completed up to last report	111.18 km
Secondary / Tertiary drains completed during reporting period	117.54 km
Secondary drains cumulative total shown	228.72 km
Secondary / tertiary drain areas reported	Ritani to Brahmpuri Stretch, Rohta Road Area; Navin Mandi Area; Garh Road Area; Baghpat Road Connecting Area; Delhi Road–Hapur Road Connecting Area, Gali Number 8, Daksh Prajapati Maarg, Pal Chowk Link Rd, Gali Number 2, Street Number 3, Kalindi Rd, Gupta Colony Rd, Lisari Rd, Shivam Nagar Rd, Budhana-Hapur Rd, RTO Rd, Gautam Buddha Marg, Somdutt Vihar Rd, Kaliyagarhi Rd.

3 Primary Drain Reaches Completed

- Abu Nala-1 – Begumpul to Begambagh Primary Drain
- Abu Nala-1 – Panchsheel Colony to Nehru Nagar Primary Drain
- Abu Nala-1 – Mohanpuri to Ahmad Nagar Primary Drain
- Abu Nala-1 – Ganga Nagar to Jai Bheem Nagar Primary Drain
- Odean Nala – Ramgarhi to Prabhat Nagar Primary Drain

- Odean Nala – Garh Road to Chanakyapuri Road Primary Drain
- Odean Nala – Ghosipur to Hasanpur–Mirpur Primary Drain
- Abu Nala-2 – Devpuri to Kanker Khera via Nangla Tashi Primary Drain
- Khadauli Nala – Ved Vyas Puri to Sushant City Primary Drain
- Khadauli Nala – Partapur to Shatabdi Nagar Primary Drain
- City Nala – East side of the Abu Nala-2
- City Nala – West side of the Abu Nala-2

4 Survey Progress as on 05/11/2026

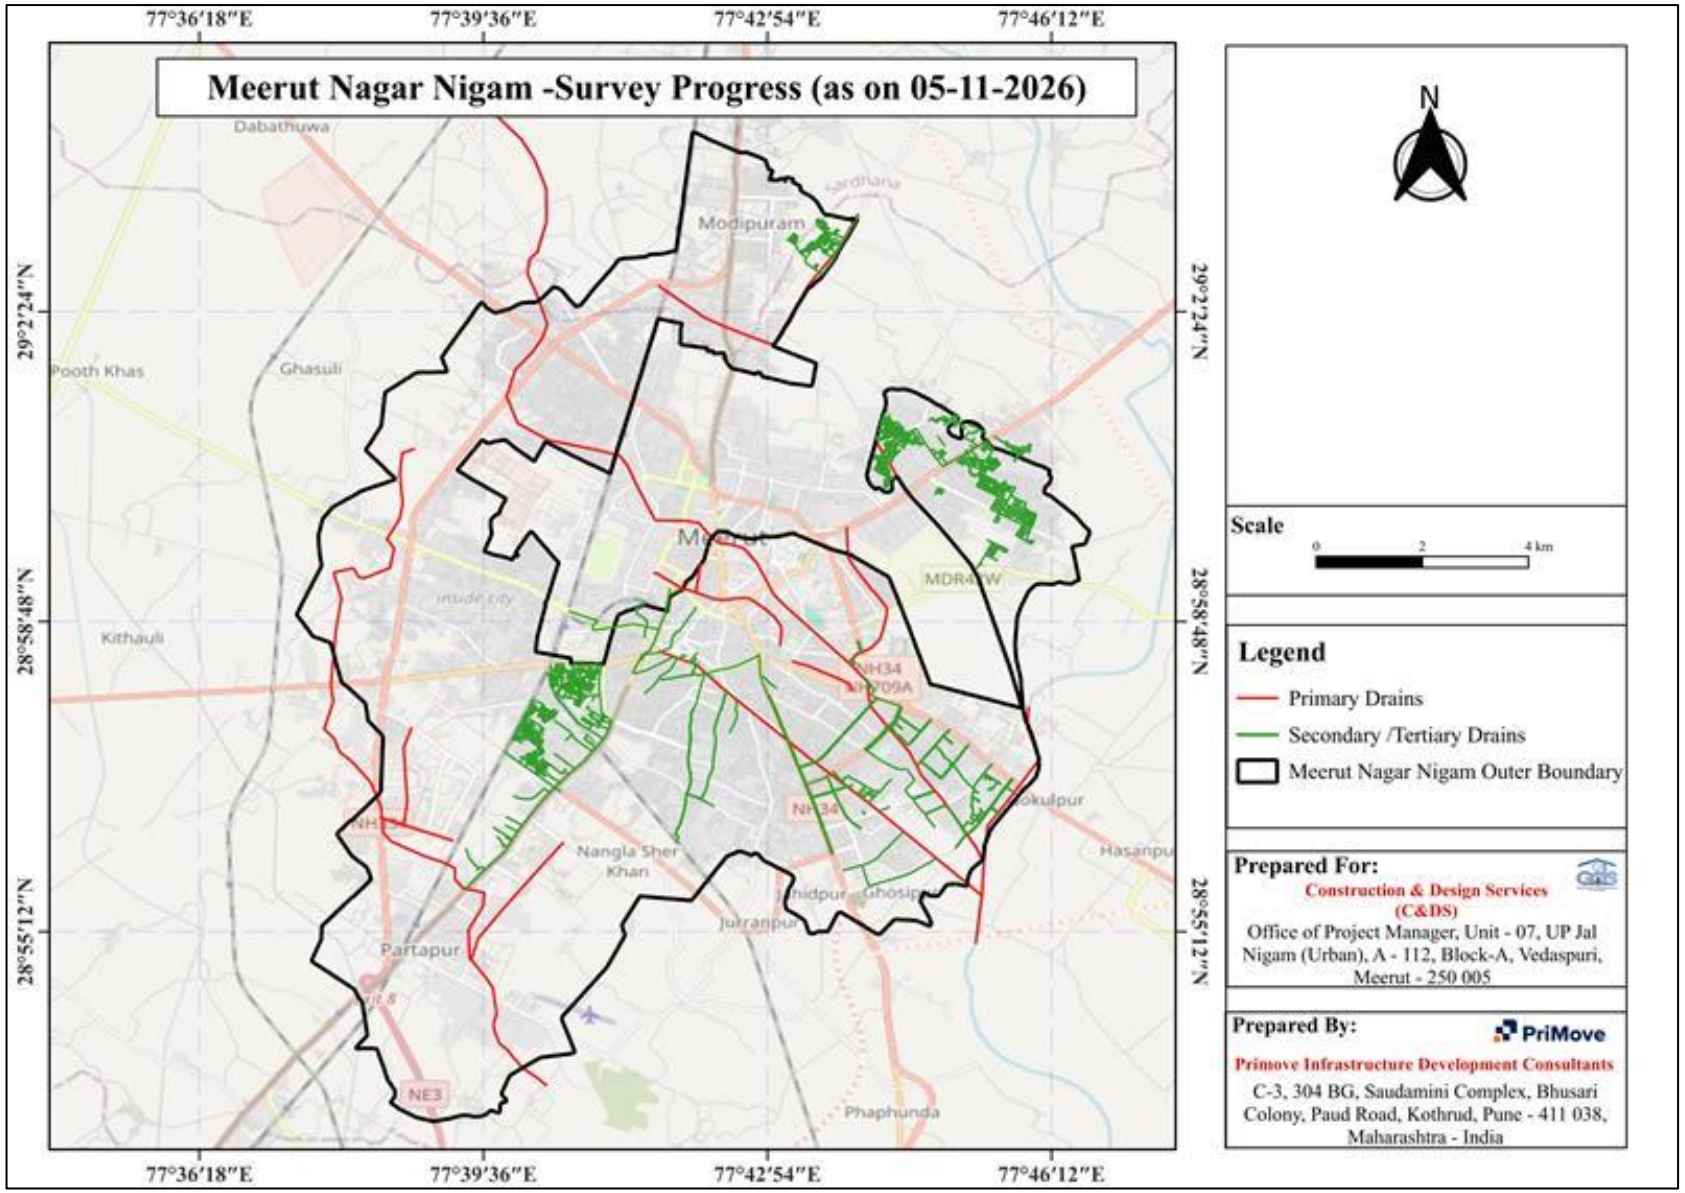


Figure 1- Survey Progress of Meerut Nagar Nigam as on 05-11-2026

5 DGPS Static Points

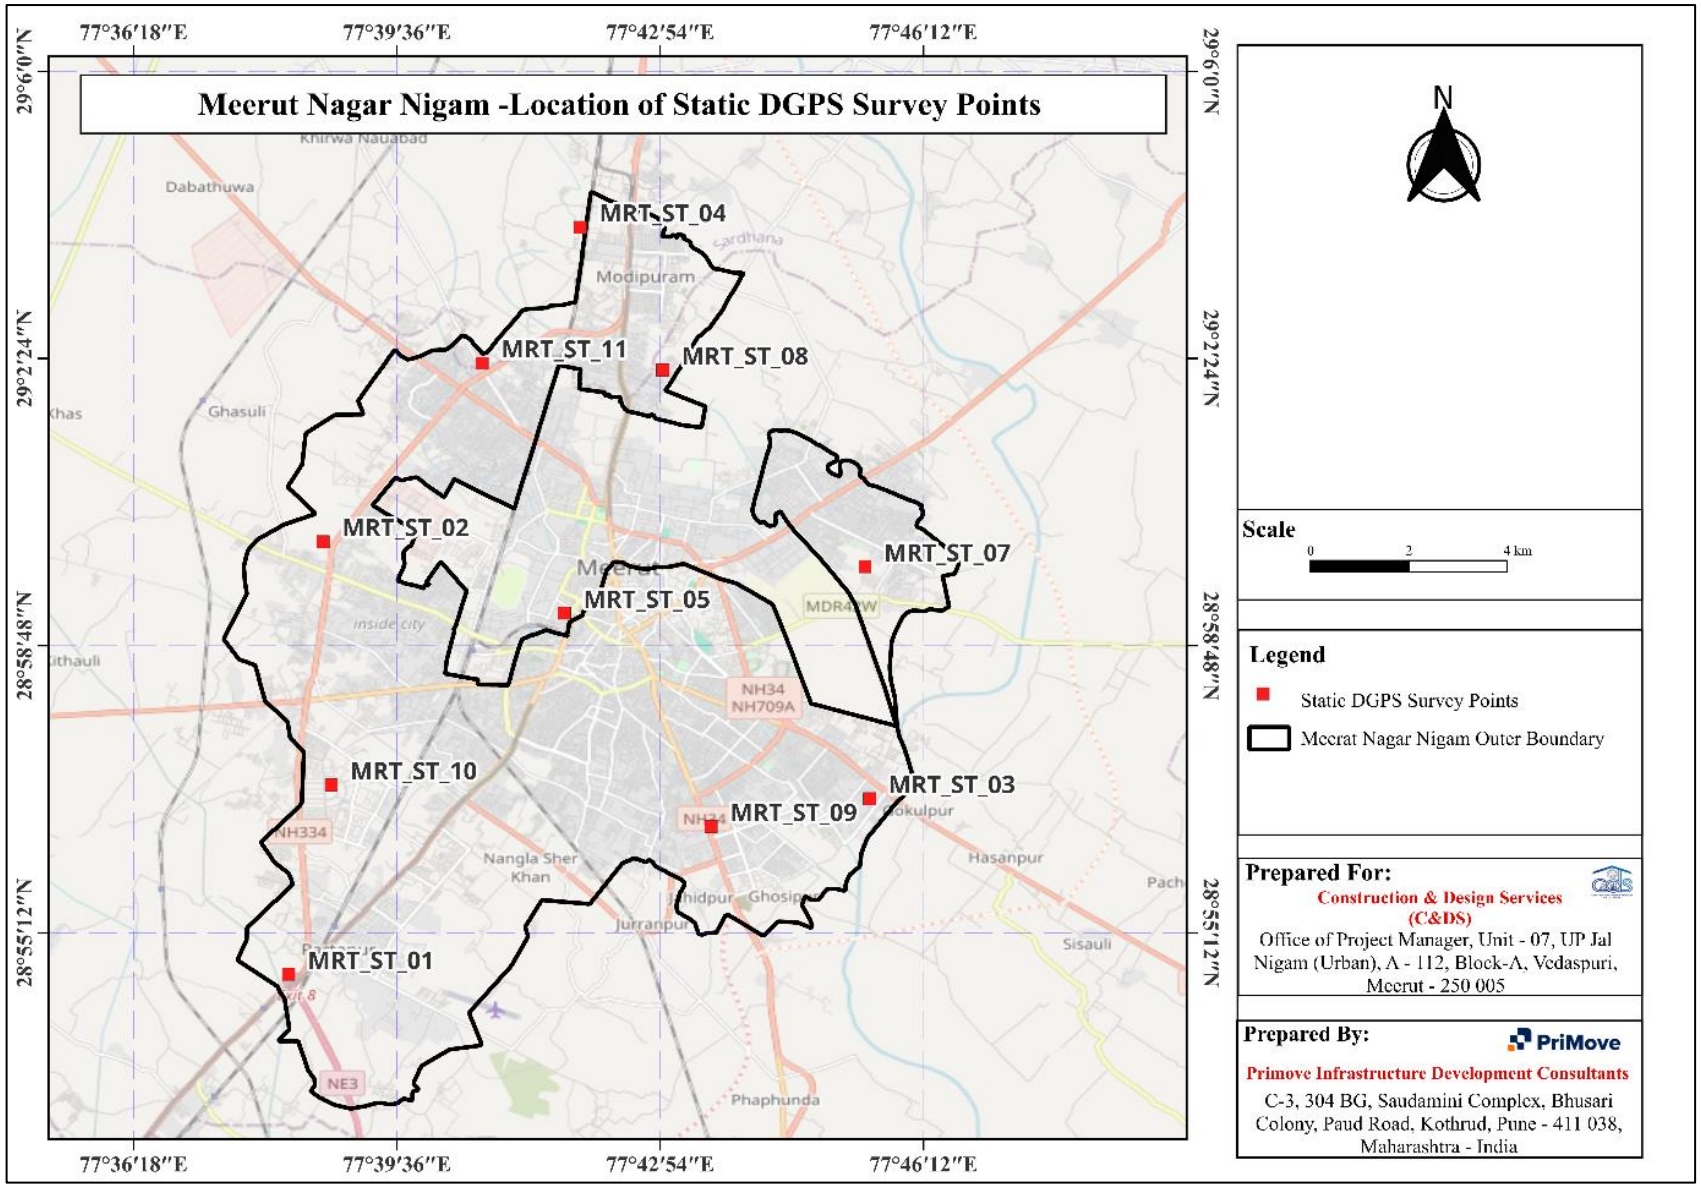


Figure 2- Location of Static DGPS Survey Control Points within Meerut Nagar Nigam

6 Road Survey Completed in wards

Ward No.	Ward Name	Road Length (Km)
1	Ward 1	0.422
3	Islam Nagar	2.109
4	Laxmanpuri	3.584
6	Shiv Hari Mandir	30.741
7	Mehandi Mohalla	1.456
8	Vivek vihar	2.38
11	Gagol Road	3.388
13	Jawahar Nagar	0.113
14	Prem Pryag Colony	1.307
16	Indra Colony	0.97
17	Janakpuri, Sports Colony	11.738
18	Mukarrab Husain, Dwarikapuri	11.404
19	Bazar	0.793
20	Ansal Colony	26.918
24	subhashpuri	0.456
26	Kaseru Baksar	2.005
28	Muqarrabpur Palhera	0.335
30	Subhash nagar	1.464
31	Modipuram	2.325
33	Hydle Colony	7.733
34	Ghosipur	0.531
35	Prem Vihar	3.981
36	Beripura	0.986
37	Humanion Nagar	15.723
39	Rampur Pavti	1.561
42	Badrishpuram	1.063
45	Shivpuri	4.194
48	Budhana Gate	0.774
49	Anoopnagar Fazalpur	0.651
51	Pragati Nagar	12.57
53	Court Compound	1.69
54	Ward 54	0.244
55	limit Besides Mohalla List included.	1.905
56	Uday Singh	1.629
59	Hanumanpuri	0.481
60	Jai Devi Nagar	0.009
61	Nehru Nagar	2.616
62	Shastri Nagar (Sec-,8,9,11,13)	0.194
63	Indra Nagar IInd	6.125
64	Shastri Nagar (K-1,2,3,4,5)	0.003
66	Khair Nagar, Bun Batan	0.008
69	Makbara Abbu	0.062
70	Lala Ka Bazar	0.28
71	Chatta Anantram	0.686
72	Purwa Peer Baksh	0.342

73	Bank Colony Hapur Road	0.74
74	Zaidi Society	0.163
76	Bel Pathar Colony	1.259
79	Veeru chah	1.34
81	Tarapuri	2.214
82	Idgah Colony	0.279
83	Ashiyana Colony	0.421
85	Zakir Hussain Colony	1.302
86	Zakir Hussain Colony Uttari	1.225
87	Zakir Hussain Colony Dakshir	0.494
88	Shyam Nagar Purwi	0.556
90	Guljar Ibraheem	1.174

7 Survey Plan for Next Week

Secondary/Tertiary drains

1. The survey of secondary drains of Odean Nala, followed by Abu Nala-2, is planned for the upcoming week.
2. The topographical survey of Brahampuri to Rithani stretch is also included in the planned survey activities.
3. Subject to the arrival and mobilization of the new survey team, the secondary drain survey of Abu Nala-1 is expected to commence.

8 IMD Data Status

A formal request letter has been submitted to the India Meteorological Department (IMD), Delhi Office, for the procurement of rainfall data pertaining to Meerut Nagar Nigam. Additionally, a forwarding letter dt. 16/10/2026 has been issued by C&DS to facilitate and expedite the data procurement process.


Item	Progress / Details
Submission of request letter to IMD for IDF Curve data	28/09/2026
Payment done for IDF data	15/10/2026
Expected date for receiving IDF data	15/11/2026

9 Photographs


Primary/Secondary/Tertiary Drains	
	
	

Primary/Secondary/Tertiary Drains



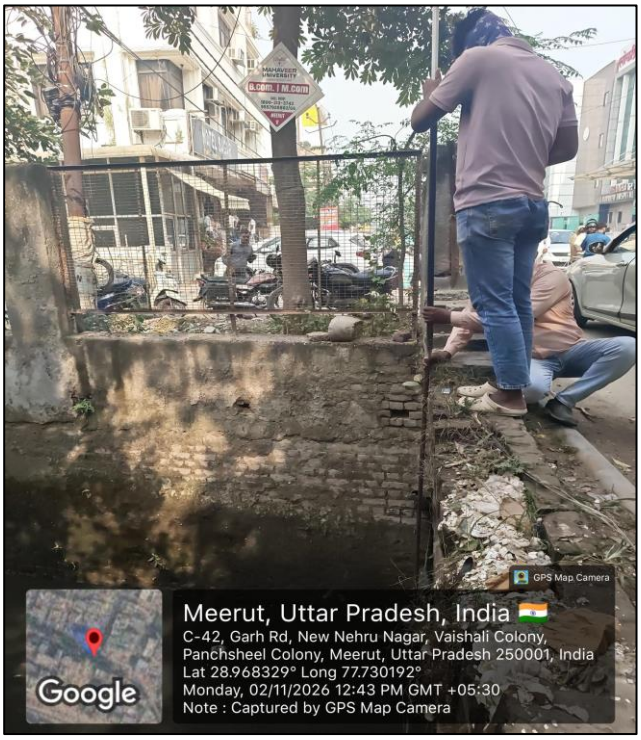




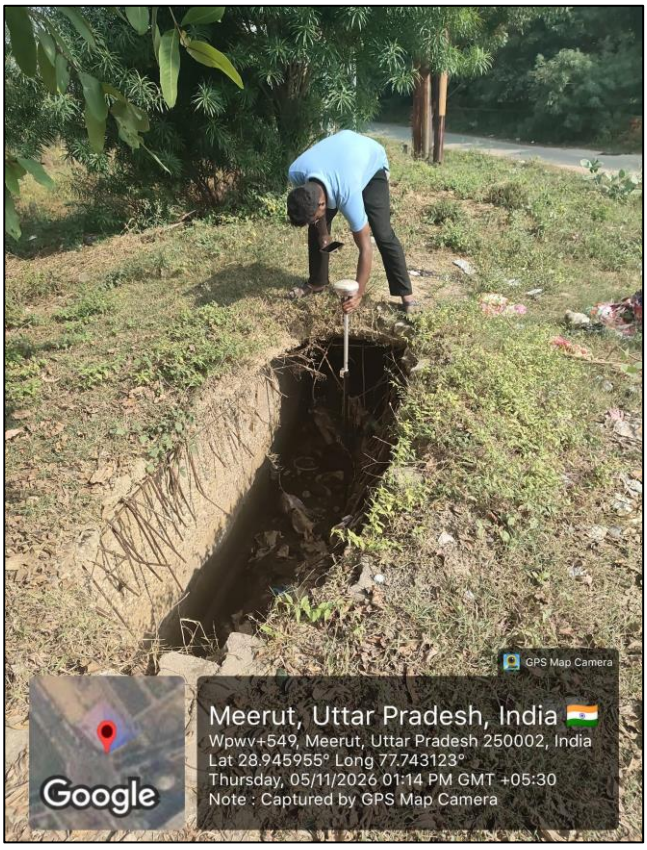

Primary/Secondary/Tertiary Drains



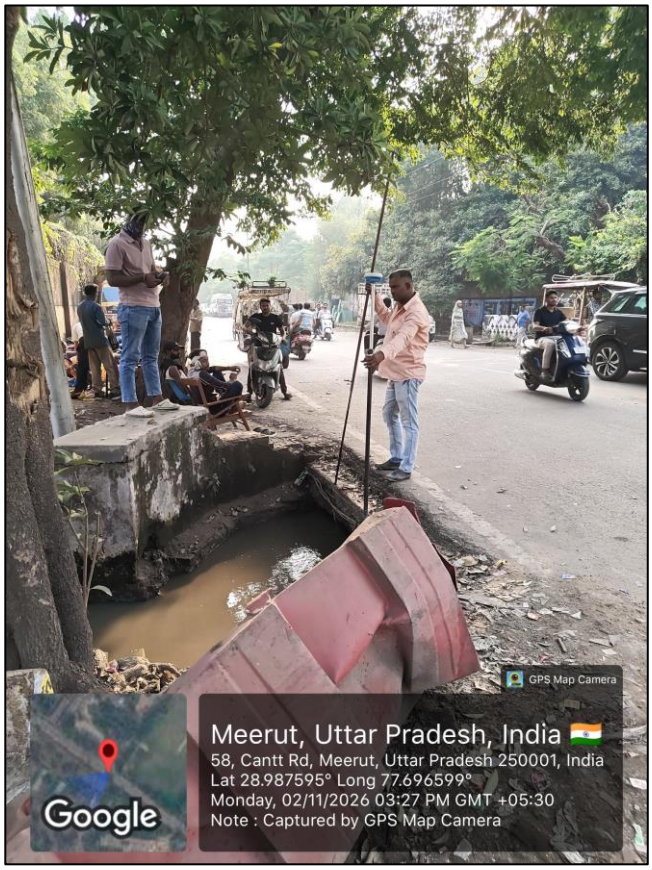





Submitted by: PriMove Infrastructure Consultants Pvt. Ltd. **Date:** 06/11/2026
