Ref. No.: Pri/ /2026 Date: 23/10/2026

To,

The Project Manager,

Construction & Design Services (C&DS),

Office of Project Manager, Unit–18,

House No. 7B/108, Buddhi Vihar Yojana No. 4

Part-2, Delhi Road, Moradabad, Uttar Pradesh.

(Email. pm18mbd@gmail.com)

Subject: Submission of Weekly Progress Report for Moradabad City for the period of 13 to 15 /10/2026.

Reference: 1. Letter of Acceptance (LOA) Letter No. 2473/G.M.(Ni-9)/e-Tender/2026, dated 10/08/2026 issued by C&DS, U.P. Jal Nigam.

2. Our Acknowledgement Letter no. Pri/1183/2026, dated.18.08.2026

Respected Sir,

With reference to the above-mentioned subject and the meeting held on 18th September 2026, we hereby submit the Weekly Progress Report for the period from 16th to 22th October 2026 for your kind information

Thanking you,

PRIMOVE Infrastructure Development Consultants Pvt. Ltd. PUNE

Sunil Warade

Assistant General Manager

Encl : Weekly Progress Report

WEEKLY PROGRESS REPORT-MORADABAD

Reporting Period: 16/10/2026 to 22/10/2026

Project Name: Survey, Collection of Data, Preparation of Integrated Urban Storm Water Drainage Master Plan (IUSWDMP) and other allied works for **Municipal Corporation Moradabad**, Uttar Pradesh, India

1. Progress Summary

Activity	Progress / Status
City area as per KML	**64.52** sq. km (Nagar Nigam)
City Area as per RFP	**85.2** sq.km
Static points	- Planned - 10 Nos - Completed - 10 Nos (100%)
GCP points	- Planned - **206** Nos - Completed - **206** Nos (100%) - Completed 100%
LiDAR drone survey	- Permission Received 5/10/2026 - Data acquisition started on 7/10/2026 - Area Covered **100** Sq.km (Data Acquisition Completed- **14 Blocks**) - Data processing Status: Not Started
LiDAR drone survey Area excluded due to restricted area	- Name- Nil - Area - Nil
DGPS survey	- DGPS commenced on **07/09/2026** - Deployment reported as 1 base and 3 rover on dated **22/10/2026** - Survey team– 3 Nos (6 Members) - DGPS Processed data received till **19th Oct**.
Survey of Primary drains	- Primary Drains As per OSM Planned – **140 km** - Completed Length up to previous week:- **113.23** Km - Completed length during the reporting period – **11.2 km**(Actual Invert); - Cumulative length (Alignment) **113.234** km (80%) - Actual Invert (Desilting)- **11.2** Km
Out Falls identified till date	- 5 ; (Subject to Change)
Road Length Survey	- Road Length as per OSM Planned -**1155** km - Completed Length up to previous week: - **113.3** Km - Completed length during the reporting period **17.8** km; - Cumulative length **130.8** km (11.3%)
Secondary /tertiary Drains Covered	- Completed Length up to previous week: - **57.295** Km (Secondary); **23 Km**(Tertiary) - Completed length during the reporting period **5.46** km(Secondary)

	- Completed length during the reporting period **13.84** km(Tertiary) - Cumulative length completed - **99.59** km
Inception report	- Submitted on 16/09/2026

2. Correspondence and Survey Activities

Activity	Date / Details
LiDAR survey letter submitted by PriMove to PM, C&DS	22/09/2026
LiDAR survey – drone details submitted	5/10/2026
Police permission received from CP	5/10/2026
LiDAR drone survey flying started (data acquisition)	07/10/2026
LiDAR drone survey flying completed (data acquisition)	Data Acquisition Completed (100 Sqkm-5 Survey Blocks)
Lidar Data ORI,DTM,DSM	In Progress.
DGPS survey start date	07/09/2026
DGPS calibration report submitted	22/09/2026
Number of DGPS teams deployed	1 base station and 3 rover units
Inception report	16/09/2026
Meeting with PM, C&DS	12/10/2026;21/09/2026;22/10/2026
Survey Site Visit by C&DS officials	7/10/2026 (Drone)
City area and Ward boundary KMZ file based on secondary data submitted to PM office for Verification from Nagar Nigam	10/10/2026
Verification received from Nagar Nigam	Nil
Survey Data submitted to PM office for Verification	Nil
Survey Verification done by PM office	Nil

3. Drain Survey / Mapping Progress

Item	Progress / Details
Primary drains planned as per OSM	140 km (tentative; as per OSM)
Primary drains completed up to last report	113.23 km
Primary drains completed during reporting period	11.2 km (Actual Invert)
Primary drains cumulative total shown	113.2 km
Road length as per OSM planned	1155 km
Road Survey Completed up to last week	113.3 km
Road Survey Completed in this week	17.8 km
Cumulative length	130.8 km
Secondary drains completed up to last report	57.28 km
Secondary drains completed during reporting period	5.46 km
Secondary drains cumulative total shown	62.75 km
Secondary / tertiary drain areas reported	Ward 16
Tertiary Drains completed during reporting period	13.84 Km
Tertiary Drains Cumulative	36.84 Km

4. Primary Drain Reaches Surveyed

- Sambhal Road
- Bijnor–Moradabad Road
- Atal Path
- Rampur Road
- Eidgah Road
- GMD Road and Bhagwan Maharshi Valmiki Road
- Lakri–Fazalpur Road
- Delhi Road and Majhola Road
- Buddhi Vihar Phase 2 Road
- Drain along the north-western side of Moradabad Railway Station
- Ekta Colony

5. Road Survey ongoing in wards

- Ward No : -16, Ward Name Budhi Vihar - Avas Vikas Area

6. Survey Plan for Next Week

- **Primary drains/DGPS**
  - Ward 16.
  - To action on the desilting plan with the authorities; Continue the DGPS survey.
  - Remaining Primary drains and Outfalls as per SOP

7. IMD Data Status

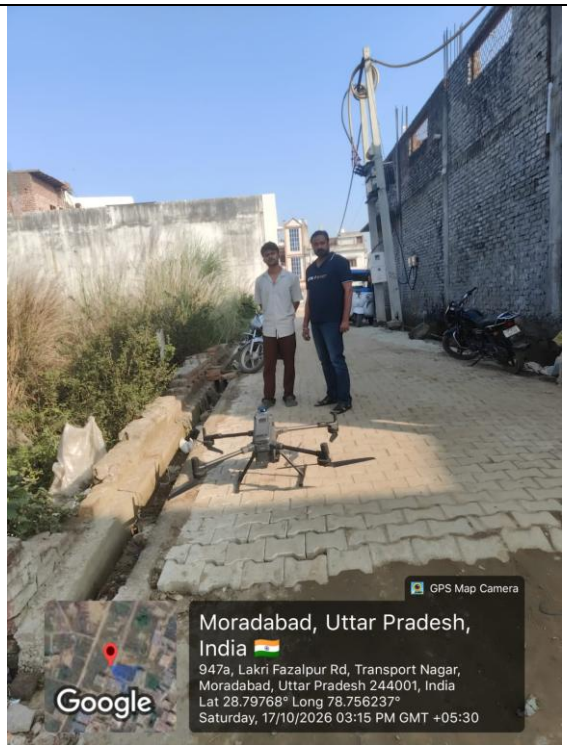
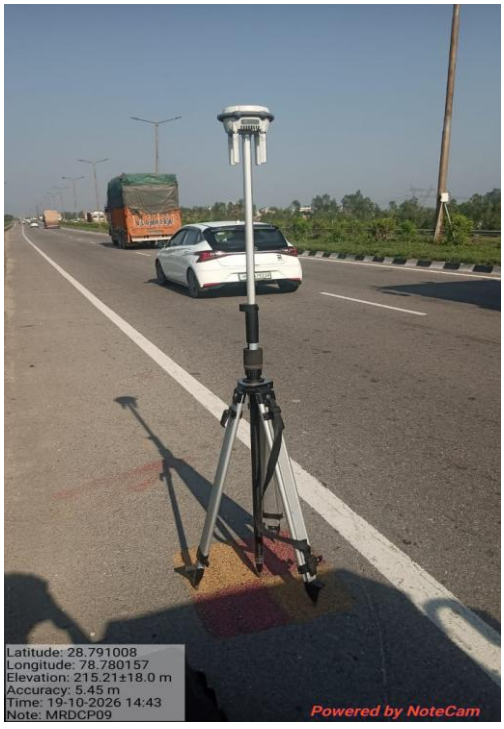
A formal request letter has been submitted to the India Meteorological Department (IMD), Delhi Office, for the procurement of rainfall data pertaining to Moradabad.

Item	Progress / Details
Submission of request letter to IMD for IDF Curve data	Submitted on 28/09/2026
Payment for IDF data	Completed on 15/10/2026
Expected date for receiving IDF data	10 to 15 days

Issues Faced

On 16 October 2026, no drone survey activities were carried out due to adverse weather conditions.

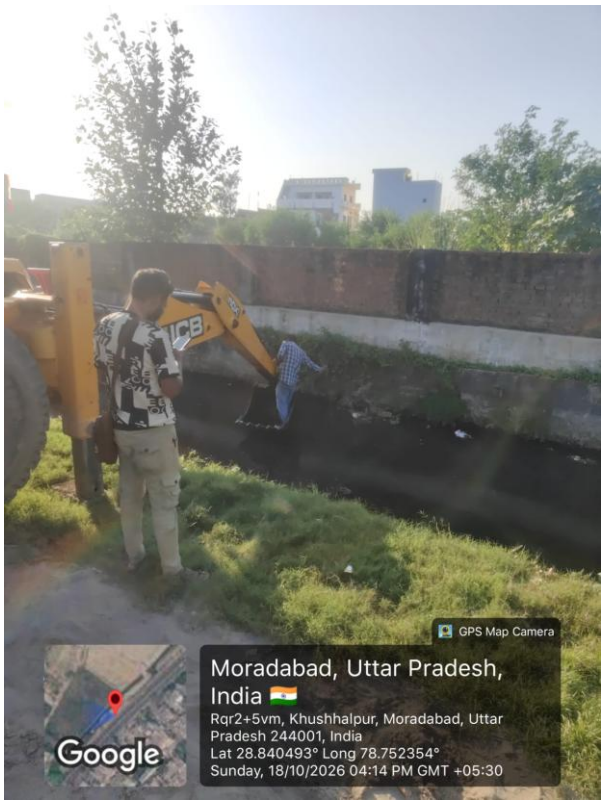
Photographs and Maps

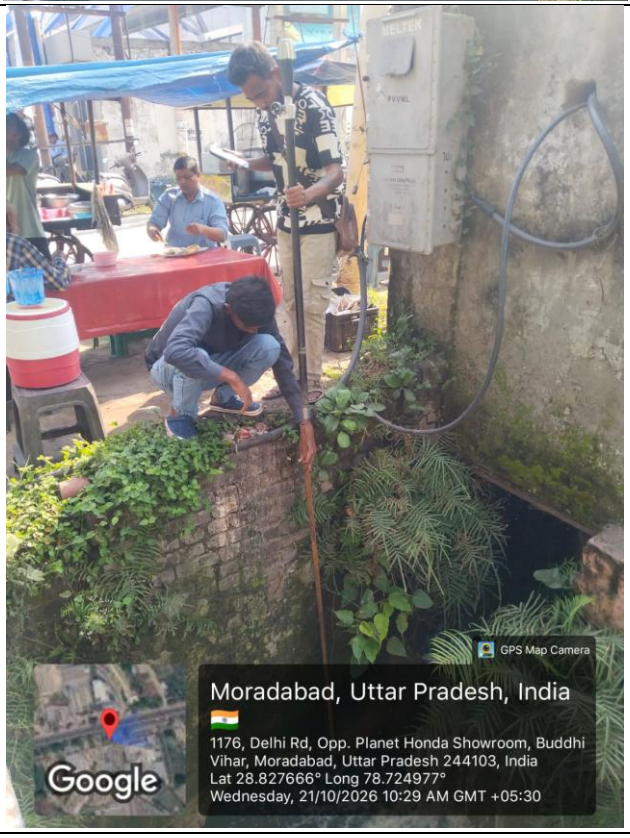
Drone Survey	Drone Survey
	
	

Drains	Drains
	
	

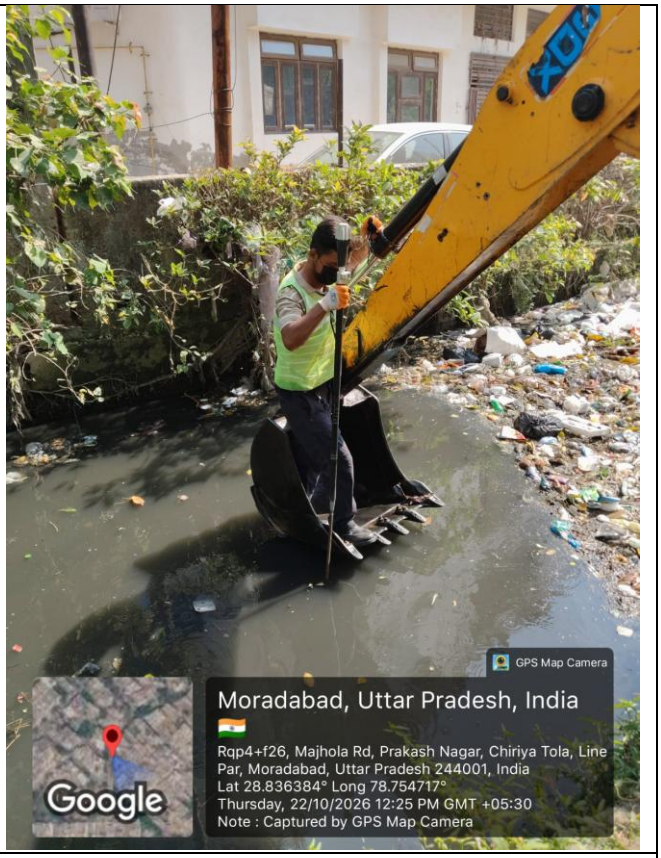

GPS Map Camera
Moradabad, Uttar Pradesh, India
Ae-26, Kanth Rd, Ram Ganga Vihar Phase 1, Moradabad, Uttar Pradesh 244105, India
Lat 28.866335° Long 78.747933°
Sunday, 18/10/2026 10:37 AM GMT +05:30
Google


GPS Map Camera
Moradabad, Uttar Pradesh, India
Vp8x+395, Kanth Rd, Near P.c Jewellers, Adarsh Colony, Moradabad, Uttar Pradesh 244105, India
Lat 28.865147° Long 78.748672°
Sunday, 18/10/2026 10:29 AM GMT +05:30
Google

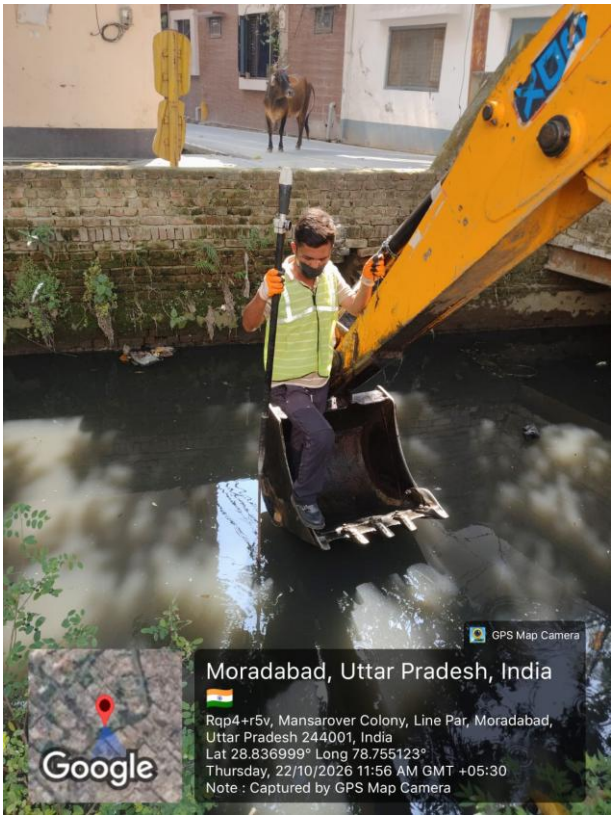

GPS Map Camera
Moradabad, Uttar Pradesh, India
Rqr2+5vm, Khushhalpur, Moradabad, Uttar Pradesh 244001, India
Lat 28.840493° Long 78.752354°
Sunday, 18/10/2026 04:14 PM GMT +05:30
Google


GPS Map Camera
Moradabad, Uttar Pradesh, India
1176, Delhi Rd, Opp. Planet Honda Showroom, Buddhi Vihar, Moradabad, Uttar Pradesh 244103, India
Lat 28.827666° Long 78.724977°
Wednesday, 21/10/2026 10:29 AM GMT +05:30
Google


GPS Map Camera
Moradabad, Uttar Pradesh, India
56 Hotel 24, Delhi Rd, Vikas Colony, Buddhi Vihar, Moradabad, Uttar Pradesh 244103, India
Lat 28.83032° Long 78.738264°
Wednesday, 21/10/2026 01:27 PM GMT +05:30
Note : Captured by GPS Map Camera
Google


GPS Map Camera
Moradabad, Uttar Pradesh, India
Rqp4+f26, Majhola Rd, Prakash Nagar, Chiriya Tola, Line Par, Moradabad, Uttar Pradesh 244001, India
Lat 28.836384° Long 78.754717°
Thursday, 22/10/2026 12:25 PM GMT +05:30
Note : Captured by GPS Map Camera
Google


GPS Map Camera
Moradabad, Uttar Pradesh, India
Rphp+rqv, Majhola, Moradabad, Uttar Pradesh 244103, India
Lat 28.830028° Long 78.737539°
Wednesday, 21/10/2026 01:17 PM GMT +05:30
Note : Captured by GPS Map Camera
Google


GPS Map Camera
Moradabad, Uttar Pradesh, India
Rqp4+r5v, Mansarover Colony, Line Par, Moradabad, Uttar Pradesh 244001, India
Lat 28.836999° Long 78.755123°
Thursday, 22/10/2026 11:56 AM GMT +05:30
Note : Captured by GPS Map Camera
Google

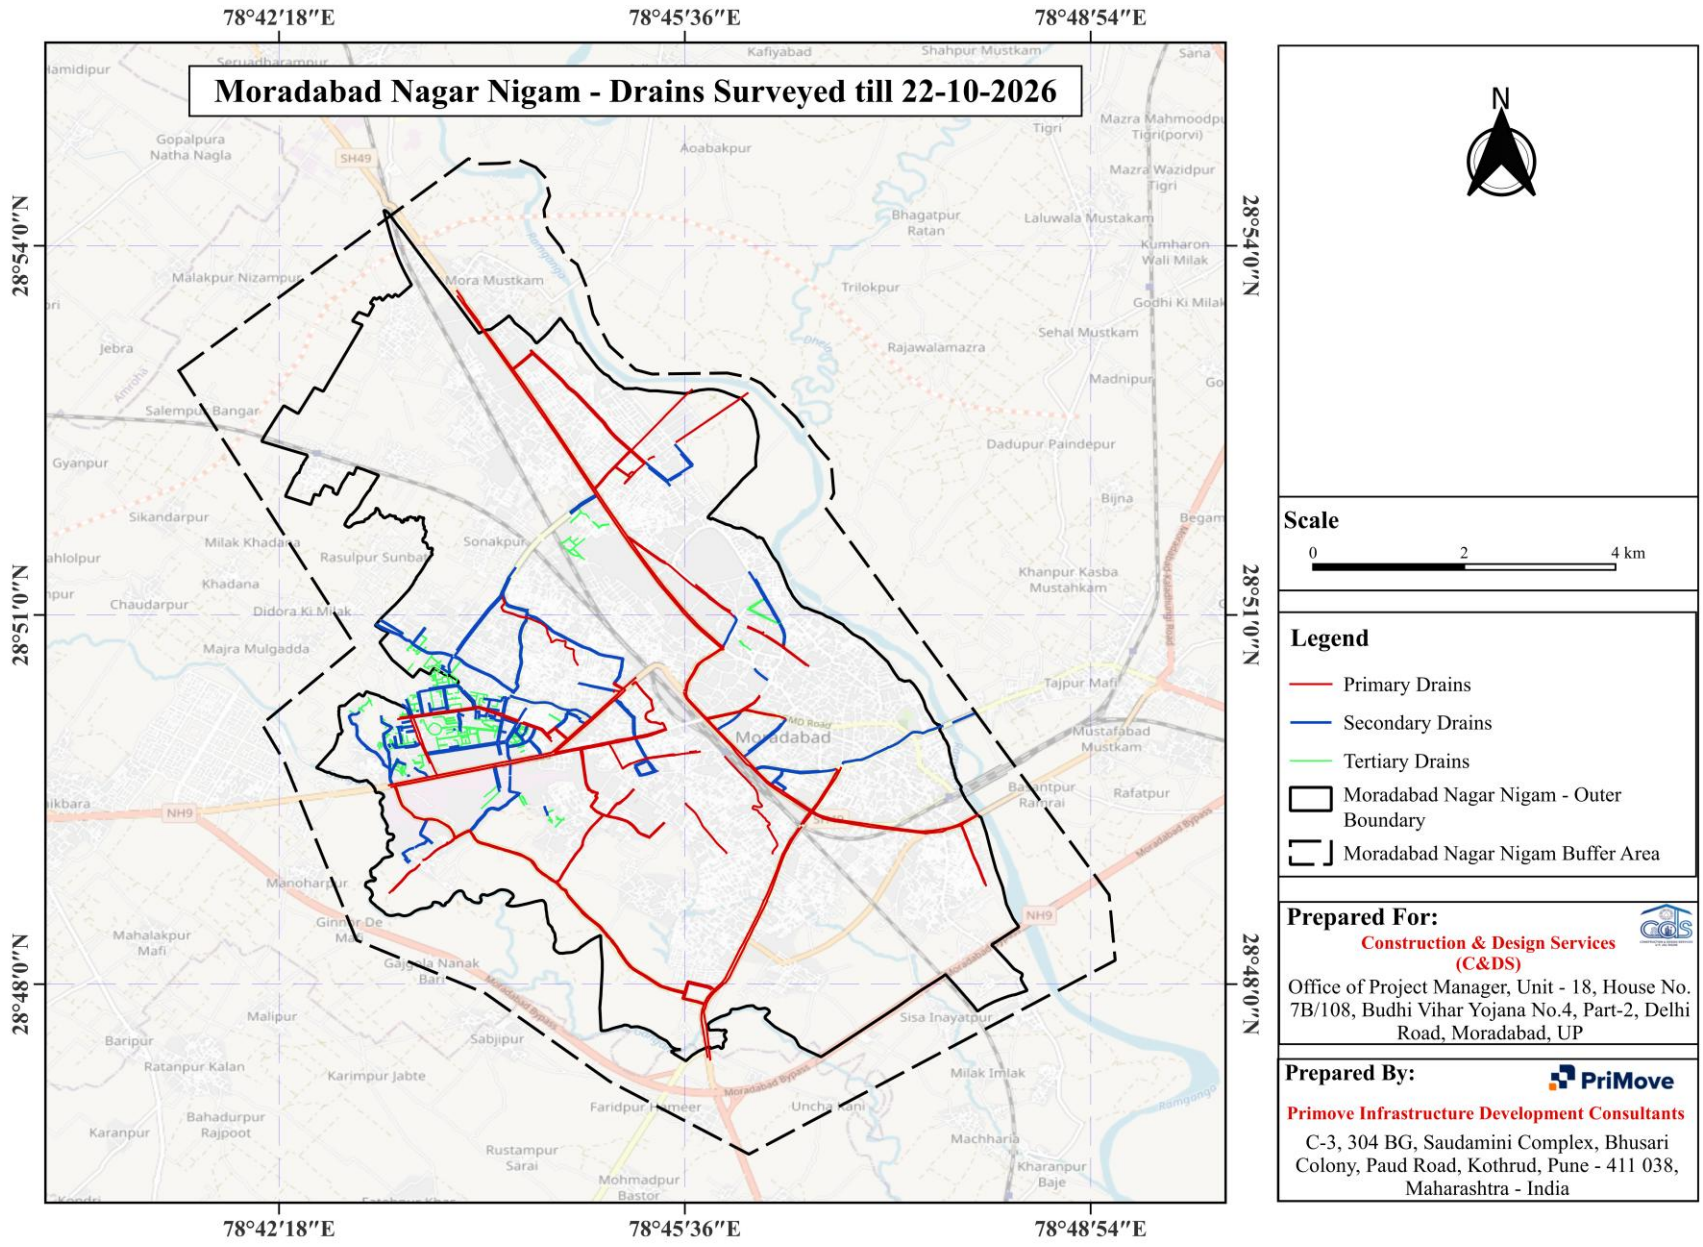


Figure : Drains Marked Till Reporting Phase

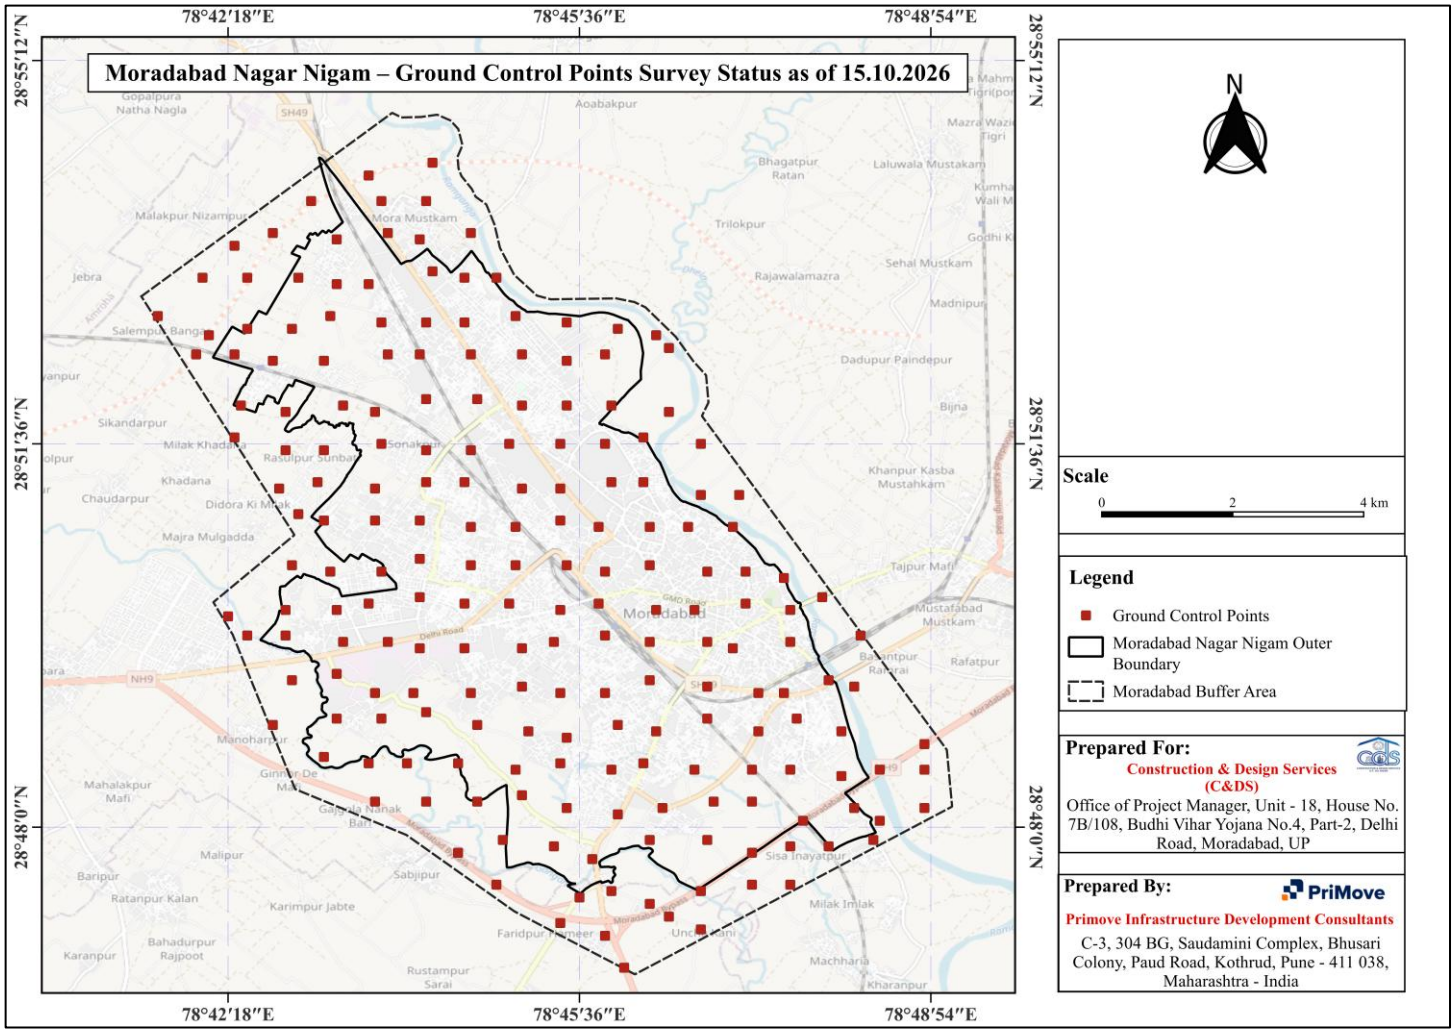


Figure : GCP Maked till Reporting Phase

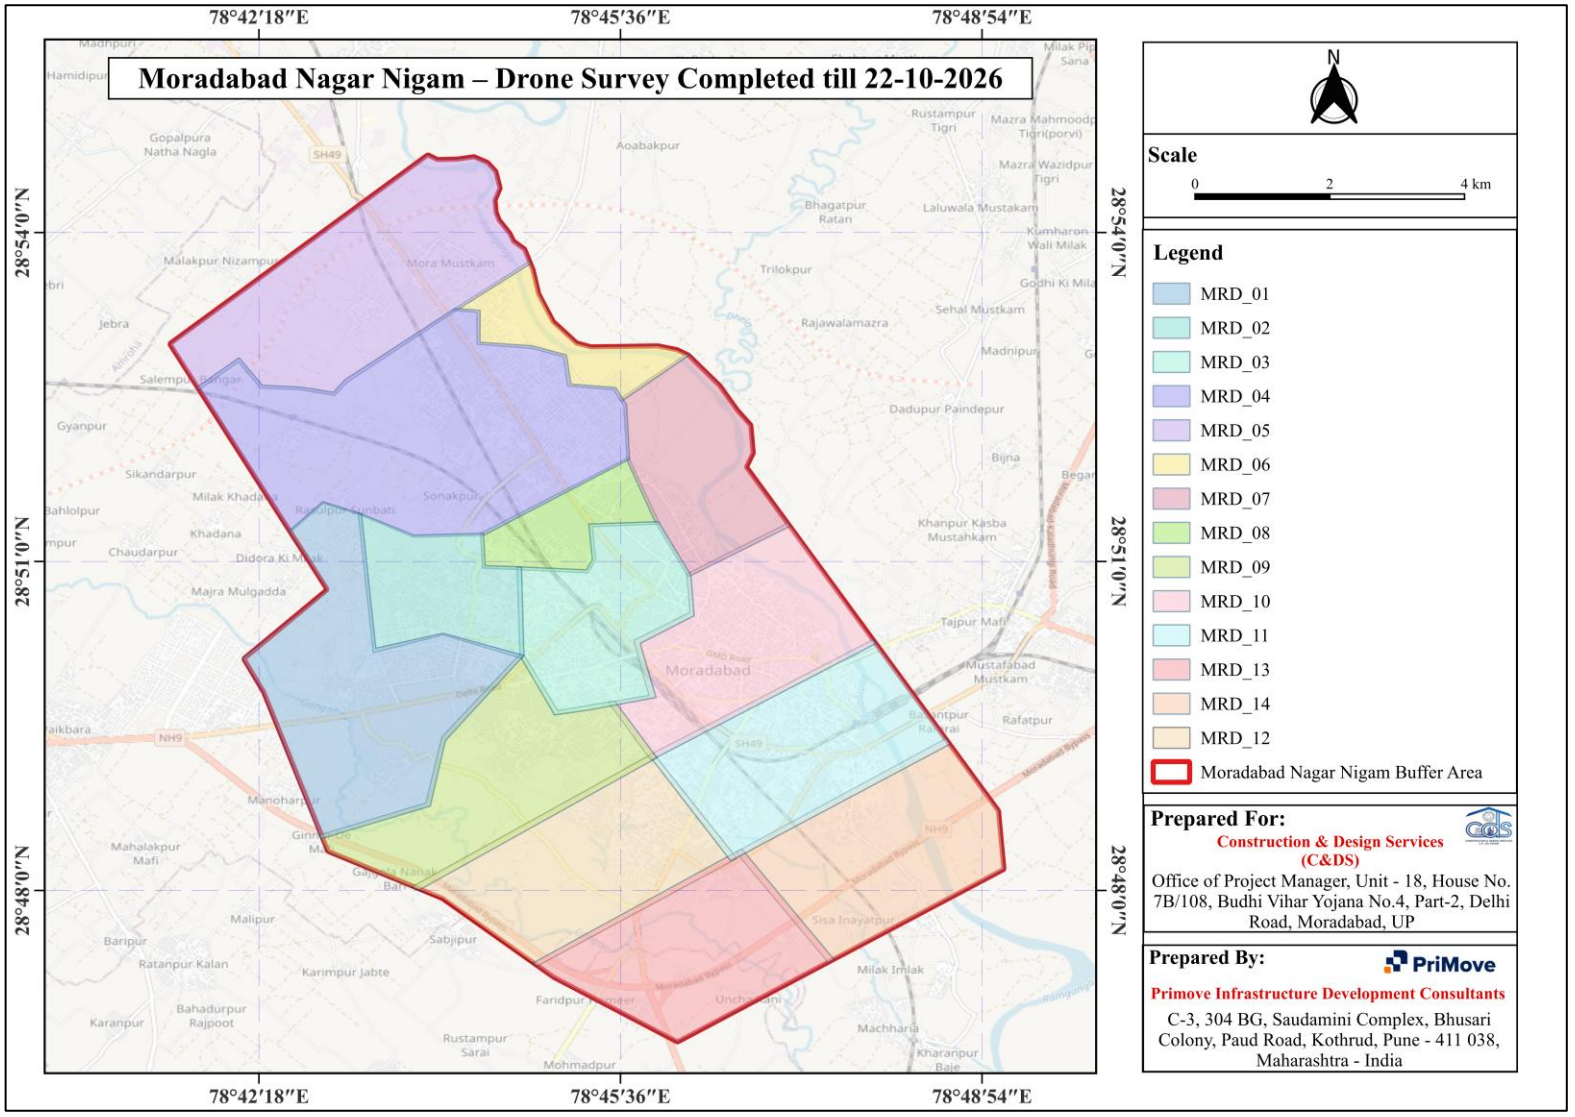


Figure : Drone Area Covered till 22th Oct.

Submitted by: PriMove Infrastructure Consultants Pvt. Ltd. **Date:** 23/10/2026
