Ref. No.: Pri/ /2026 Date: 6/11/2026

To,

The Project Manager,

Construction & Design Services (C&DS),

Office of Project Manager, Unit–18,

House No. 7B/108, Buddhi Vihar Yojana No. 4

Part-2, Delhi Road, Moradabad, Uttar Pradesh.

(Email. pm18mbd@gmail.com)

Subject: Submission of Weekly Progress Report for Moradabad City for the period of 30/10/2026 to 6/11/2026.

Reference: 1. Letter of Acceptance (LOA) Letter No. 2473/G.M.(Ni-9)/e-Tender/2026, dated 10/08/2026 issued by C&DS, U.P. Jal Nigam.

2. Our Acknowledgement Letter no. Pri/1183/2026, dated.18.08.2026

Respected Sir,

With reference to the above-mentioned subject and the meeting held on 18th September 2026, we hereby submit the Weekly Progress Report for the period from 30th October to 6th November 2026 for your kind information

Thanking you,

PRIMOVE Infrastructure Development Consultants Pvt. Ltd. PUNE

Sunil Warade

Assistant General Manager

Encl : Weekly Progress Report

WEEKLY PROGRESS REPORT-MORADABAD

Reporting Period: 30/10/2026 to 6/11/2026

Project Name: Survey, Collection of Data, Preparation of Integrated Urban Storm Water Drainage Master Plan (IUSWDMP) and other allied works for **Municipal Corporation Moradabad**, Uttar Pradesh, India

1. Progress Summary

Activity	Progress / Status
City area as per KML	**64.52** sq. km (Nagar Nigam)
City Area as per RFP	**85.2** sq.km
Static points	- Planned - 10 Nos - Completed - 10 Nos (100%)
GCP points	- Planned - **206** Nos - Completed - **206** Nos (100%) - Completed 100%
LiDAR drone survey	- Permission Received 5/10/2026 - Data acquisition started on 7/10/2026 - Area Covered **100** Sq.km (Data Acquisition Completed- **14 Blocks**) - Data processing Status: In Progress
LiDAR drone survey Area excluded due to restricted area	- Name- Nil - Area - Nil
DGPS survey	- DGPS commenced on **07/09/2026** - Deployment reported as 1 base and 4 rovers on dated **6/11/2026** - Survey team– 4 Nos (8 Members)
Survey of Primary drains	- Primary Drains As per OSM Planned – **140 km** - Completed Length up to previous week:- **113.23** Km - Completed length during the reporting period – **21.95 Km** (Actual Invert); - Alignment during reporting period- - Cumulative length (Alignment) **135.18** km (96%) - Actual Invert (Desilting)- **57.63** Km
Out Falls identified till date	- 5 ; (Subject to Change)
Road Length Survey	- Road Length as per OSM Planned -**1155** km - Completed Length up to previous week: - **149.98** Km - Completed length during the reporting period **15.68** km; - Cumulative length **165.66** km (14.3%)
Secondary /tertiary Drains Covered	- Completed Length up to previous week: - **67.27** Km (Secondary); **51.90 Km**(Tertiary) - Completed length during the reporting period **0** km(Secondary)

	- Completed length during the reporting period **0** km(Tertiary) - Cumulative length completed – **119.17** km
Inception report	- Submitted 16/09/2026; 2/11/2026

2. Correspondence and Survey Activities

Activity	Date / Details
LiDAR survey letter submitted by PriMove to PM, C&DS	22/09/2026
LiDAR survey – drone details submitted	5/10/2026
Police permission received from CP	5/10/2026
LiDAR drone survey flying started (data acquisition)	07/10/2026
LiDAR drone survey flying completed (data acquisition)	Data Acquisition Completed (100 Sqkm-14 Survey Blocks)
Lidar Data ORI,DTM,DSM	In Progress
DGPS survey start date	07/09/2026
DGPS calibration report submitted	22/09/2026
Number of DGPS teams deployed	1 base station and 4 rover units
Inception report	16/09/2026
Meeting with PM, C&DS	**12/10/2026;21/09/2026;22/10/2026;28/10/2026;31/10/2026**
Survey Site Visit by C&DS officials	7/10/2026 (Drone)
City area and Ward boundary KMZ file based on secondary data submitted to PM office for Verification from Nagar Nigam	10/10/2026
Verification received from Nagar Nigam	Nil
Survey Data submitted to PM office for Verification	Nil
Survey Verification done by PM office	Nil

3. Drain Survey / Mapping Progress

Item	Progress / Details
Primary drains planned as per OSM	140 km (tentative; as per OSM)
Primary drains completed up to last report	113.23 km
Primary drains completed during reporting period	21.95 km (Actual Invert)
Primary drains cumulative total shown	135.18 km
Road length as per OSM planned	1155 km
Road Survey Completed up to last week	149.98 km
Road Survey Completed in this week	15.68 km
Cumulative length	165.66 km
Secondary drains completed up to last report	67.27 km
Secondary drains completed during reporting period	0 km
Secondary drains cumulative total shown	67.27 km

Secondary / tertiary drain areas reported	**Ward 16**
Tertiary Drains completed during reporting period	0 Km
Tertiary Drains Cumulative	51.90 Km

4. Primary Drain Reaches Surveyed

- Sambhal Road
- Bijnor–Moradabad Road
- Atal Path
- Neta Colony, Karula
- Rampur Road
- Eidgah Road
- GMD Road and Bhagwan Maharshi Valmiki Road
- Lakri–Fazalpur Road
- Delhi Road and Majhola Road
- Buddhi Vihar Phase 2 Road
- Drain along the north-western side of Moradabad Railway Station
- Ekta Colony
- Sonakpur Vasti

5. Road Survey ongoing in wards

- Ward No: -16, Ward Name Budhi Vihar - Avas Vikas Area, Lakdi Fazalpur, Karula

6. Survey Plan for Next Week

- **Primary drains/DGPS**
  - Completion of the Ward 16; Followed by Ward 9 ,3 and 23.
  - Remaining Primary drains and Outfalls as per SOP with Drain Bottom (**Map Added**)

7. IMD Data Status


A formal request letter has been submitted to the India Meteorological Department (IMD), Delhi Office, for the procurement of rainfall data pertaining to Moradabad.


Item	**Progress / Details**
Submission of request letter to IMD for IDF Curve data	Submitted on 28/09/2026
Payment for IDF data	Completed on 15/10/2026
Expected date for receiving IDF data	15/11/2026



Figure : Meeting with RE Sir, showing progress of survey.


Photographs and Maps

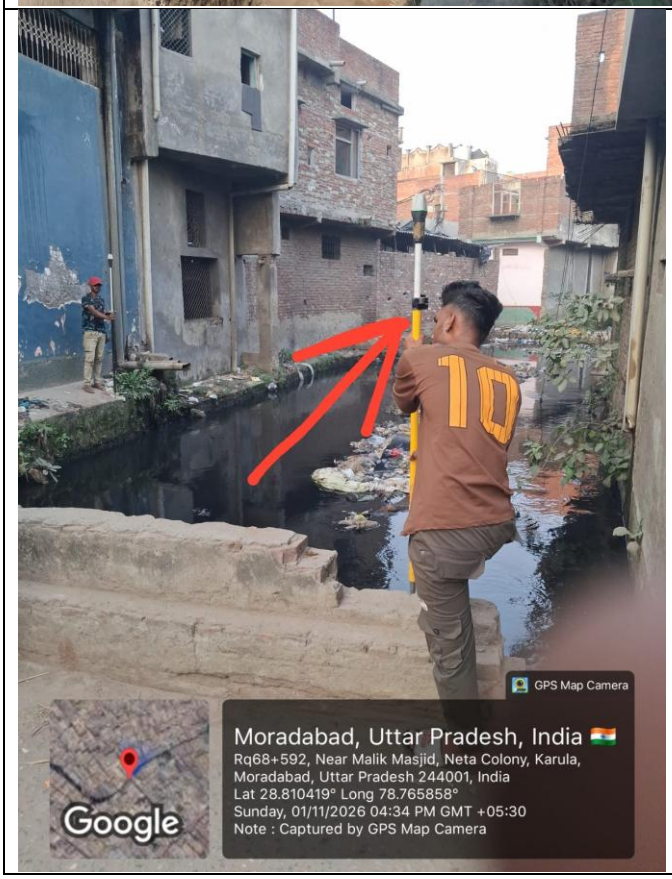Drains	Drains
	
	

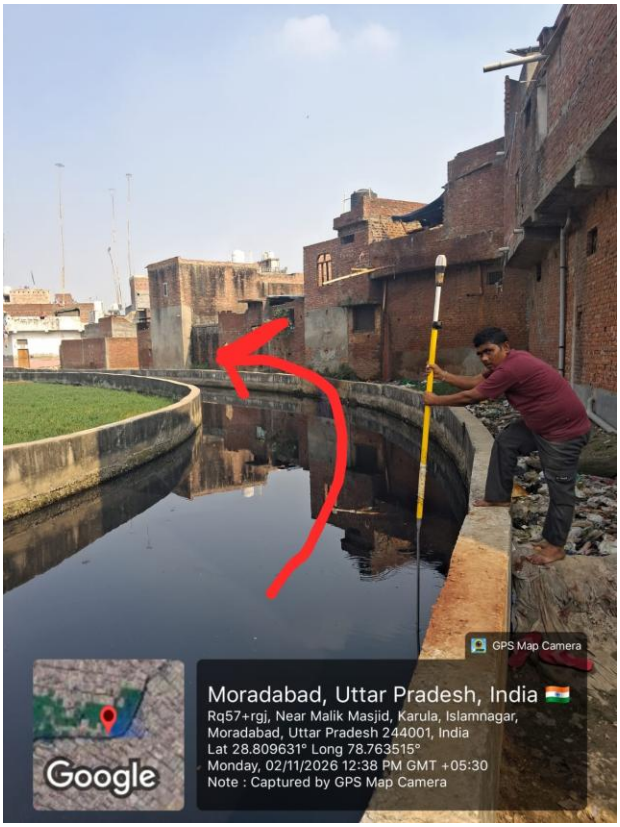
GPS Map Camera
Moradabad, Uttar Pradesh, India
Rq57+rgj, Near Malik Masjid, Karula, Islamnagar, Moradabad, Uttar Pradesh 244001, India
Lat 28.809631° Long 78.763515°
Monday, 02/11/2026 12:38 PM GMT +05:30
Note : Captured by GPS Map Camera
Google



GPS Map Camera
Moradabad, Uttar Pradesh, India
Rq56+pf7, Karula, Moradabad, Uttar Pradesh 244001, India
Lat 28.809618° Long 78.761596°
Monday, 02/11/2026 01:01 PM GMT +05:30
Note : Captured by GPS Map Camera
Google


GPS Map Camera
Moradabad, Uttar Pradesh, India
Surya Nagar, Vikas Nagar, Line Par, Moradabad, Uttar Pradesh 244103, India
Lat 28.824791° Long 78.760082°
Tuesday, 03/11/2026 11:13 AM GMT +05:30
Note : Captured by GPS Map Camera
Google

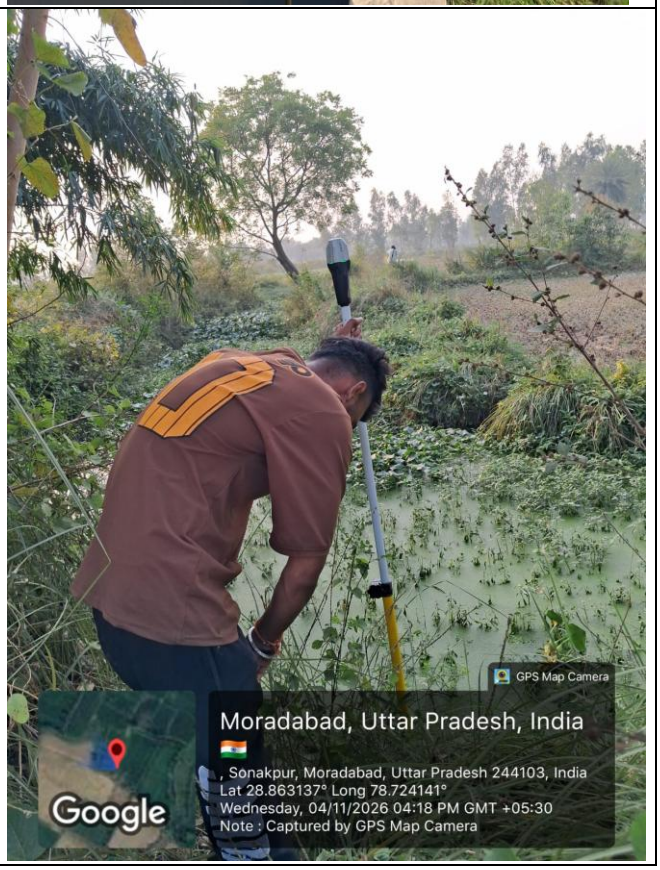
GPS Map Camera
Moradabad, Uttar Pradesh, India
, Sonakpur, Moradabad, Uttar Pradesh 244103, India
Lat 28.863137° Long 78.724141°
Wednesday, 04/11/2026 04:18 PM GMT +05:30
Note : Captured by GPS Map Camera
Google


GPS Map Camera
Rasulpur Sunwati, Uttar Pradesh, India
Vp69+mxv, Rasulpur Sunwati, Uttar Pradesh 244103, India
Lat 28.863048° Long 78.722273°
Wednesday, 04/11/2026 04:47 PM GMT +05:30
Note : Captured by GPS Map Camera
Google


GPS Map Camera
Moradabad, Uttar Pradesh, India
, Uttar Pradesh 244103, India, Moradabad, Uttar Pradesh 244103, India
Lat 28.858318° Long 78.711097°
Thursday, 05/11/2026 01:35 PM GMT +05:30
Note : Captured by GPS Map Camera
Google

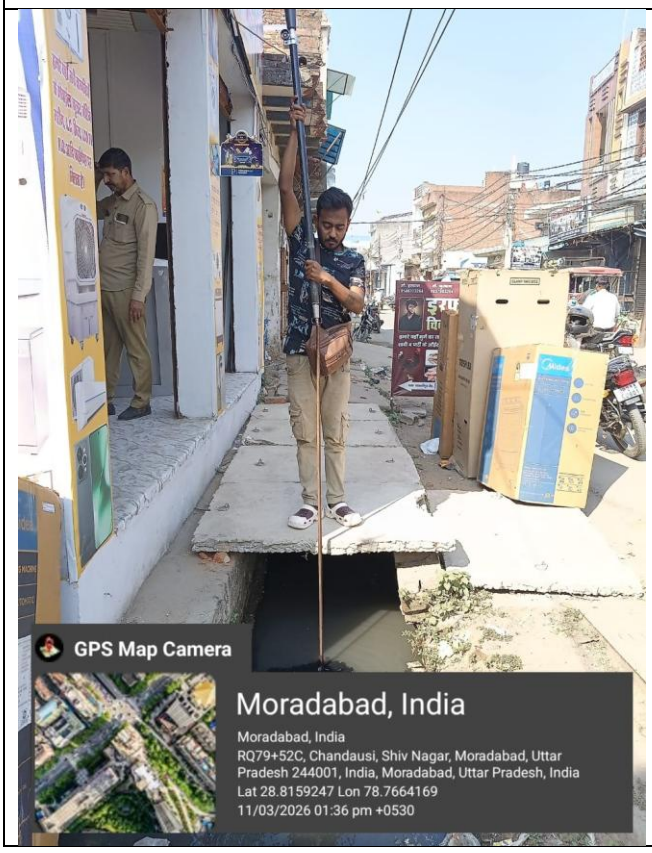
GPS Map Camera
Moradabad, India
Moradabad, India
RQ79+52C, Chandausi, Shiv Nagar, Moradabad, Uttar Pradesh 244001, India, Moradabad, Uttar Pradesh, India
Lat 28.8159247 Lon 78.7664169
11/03/2026 01:36 pm +0530


GPS Map Camera
Moradabad, Uttar Pradesh, India
Vp99+mxh, Vishanpur Bhimather, Moradabad, Uttar Pradesh 244103, India
Lat 28.868835° Long 78.719699°
Thursday, 05/11/2026 04:22 PM GMT +05:30
Note : Captured by GPS Map Camera
Google

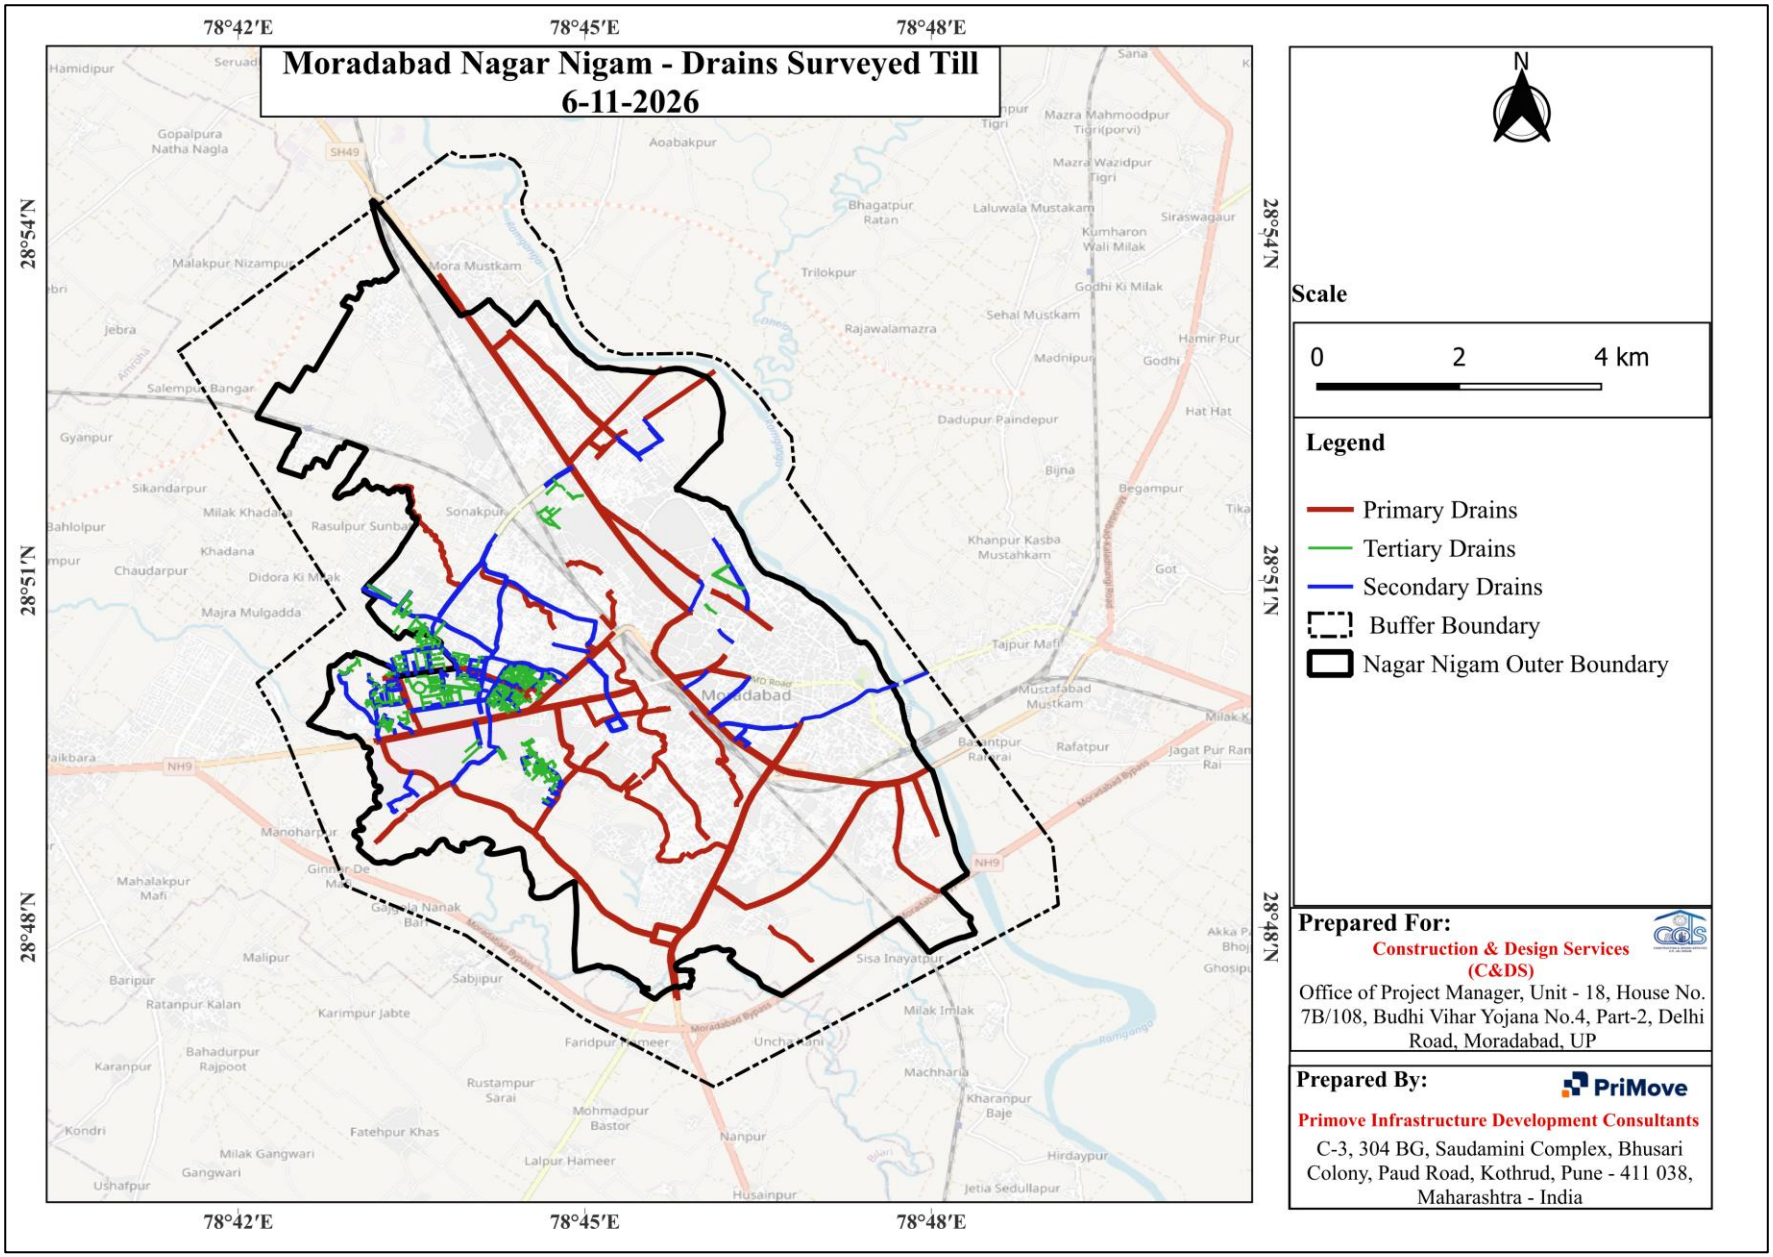

Moradabad Nagar Nigam - Drains Surveyed Till 6-11-2026
78°42′E
78°45′E
78°48′E
28°54′N
28°51′N
28°48′N
N
Scale
0
2
4 km
Legend
Primary Drains
Tertiary Drains
Secondary Drains
Buffer Boundary
Nagar Nigam Outer Boundary
Prepared For:
Construction & Design Services (C&DS)
Office of Project Manager, Unit - 18, House No. 7B/108, Budhi Vihar Yojana No.4, Part-2, Delhi Road, Moradabad, UP
Prepared By:
PriMove
Primove Infrastructure Development Consultants
C-3, 304 BG, Saudamini Complex, Bhusari Colony, Paud Road, Kothrud, Pune - 411 038, Maharashtra - India

Figure : Drains Marked Till Reporting Phase

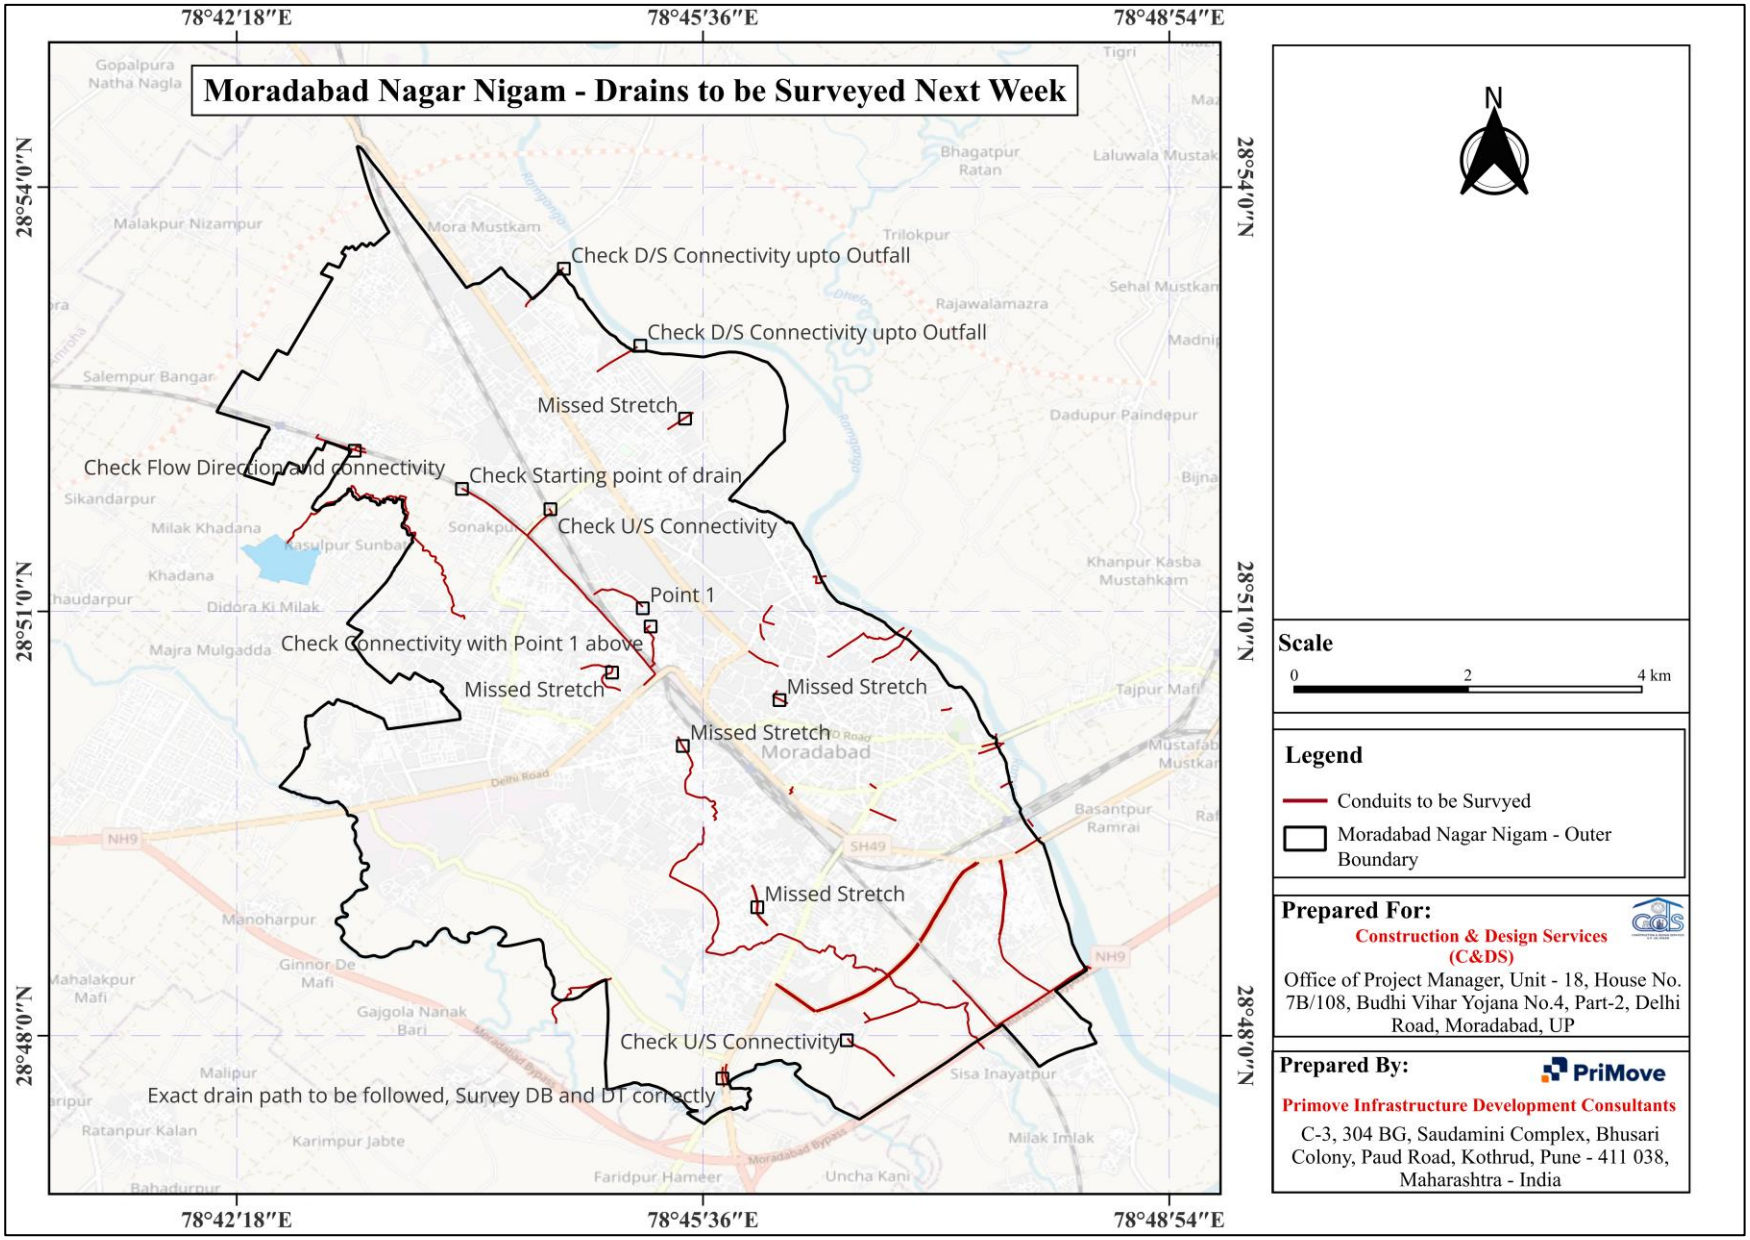


Figure : Drains and Outfalls to be Surveyed next week

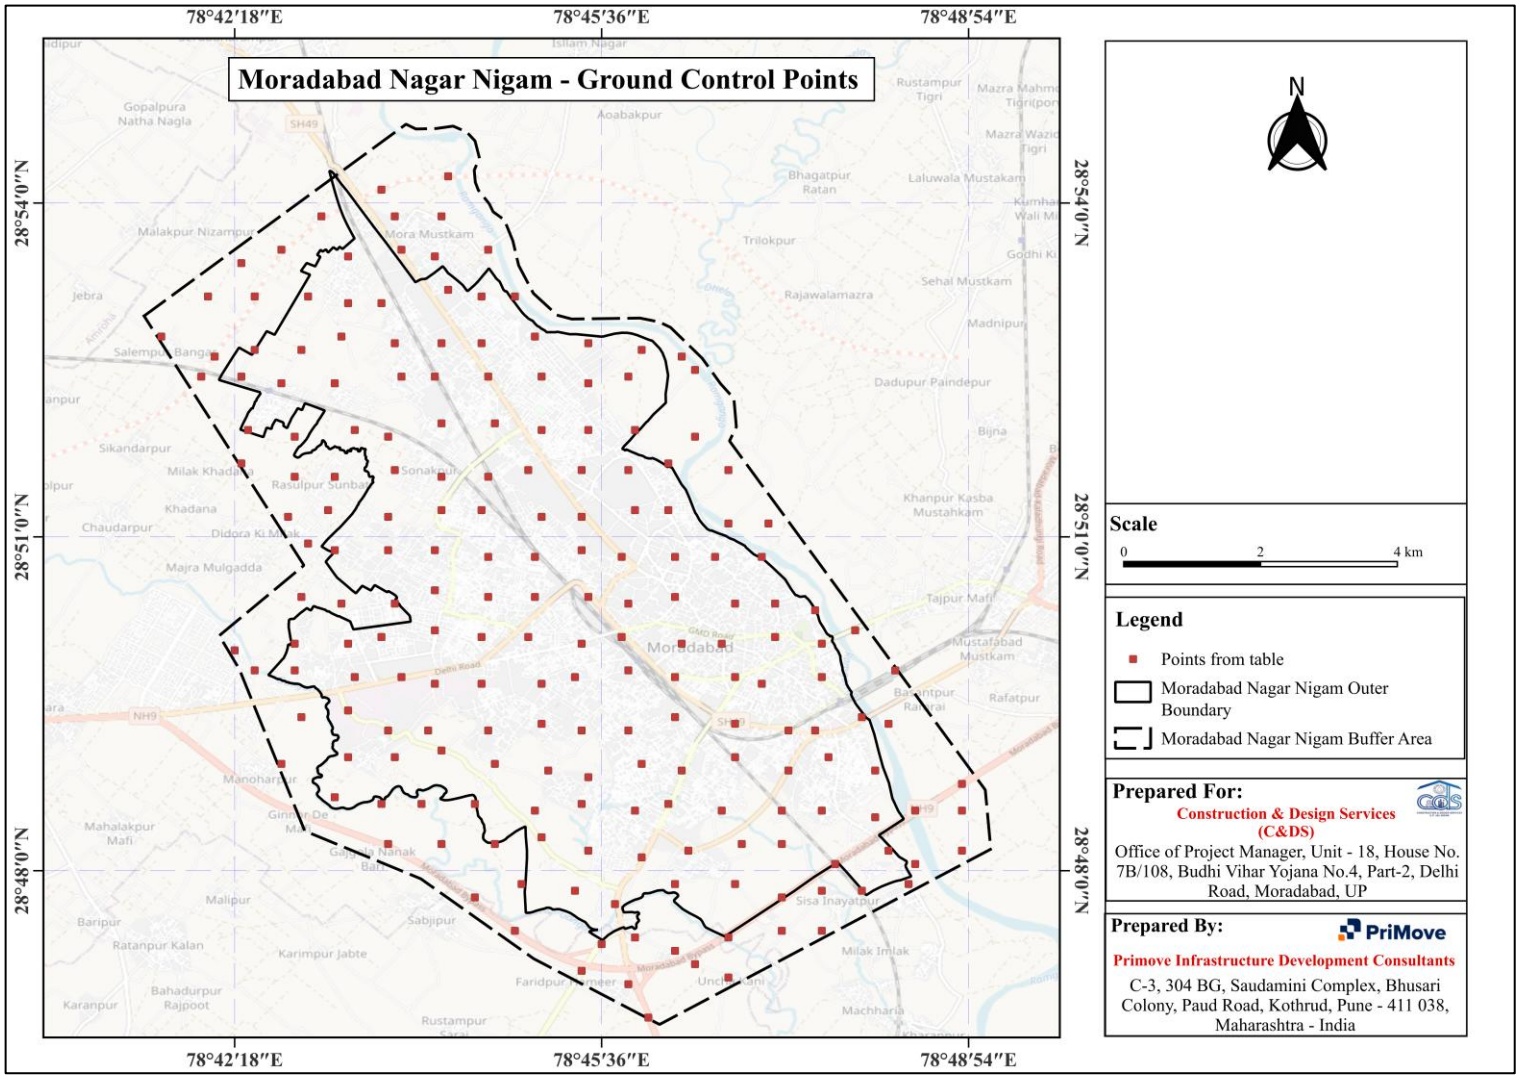


Figure : GCP Marked till reporting phase

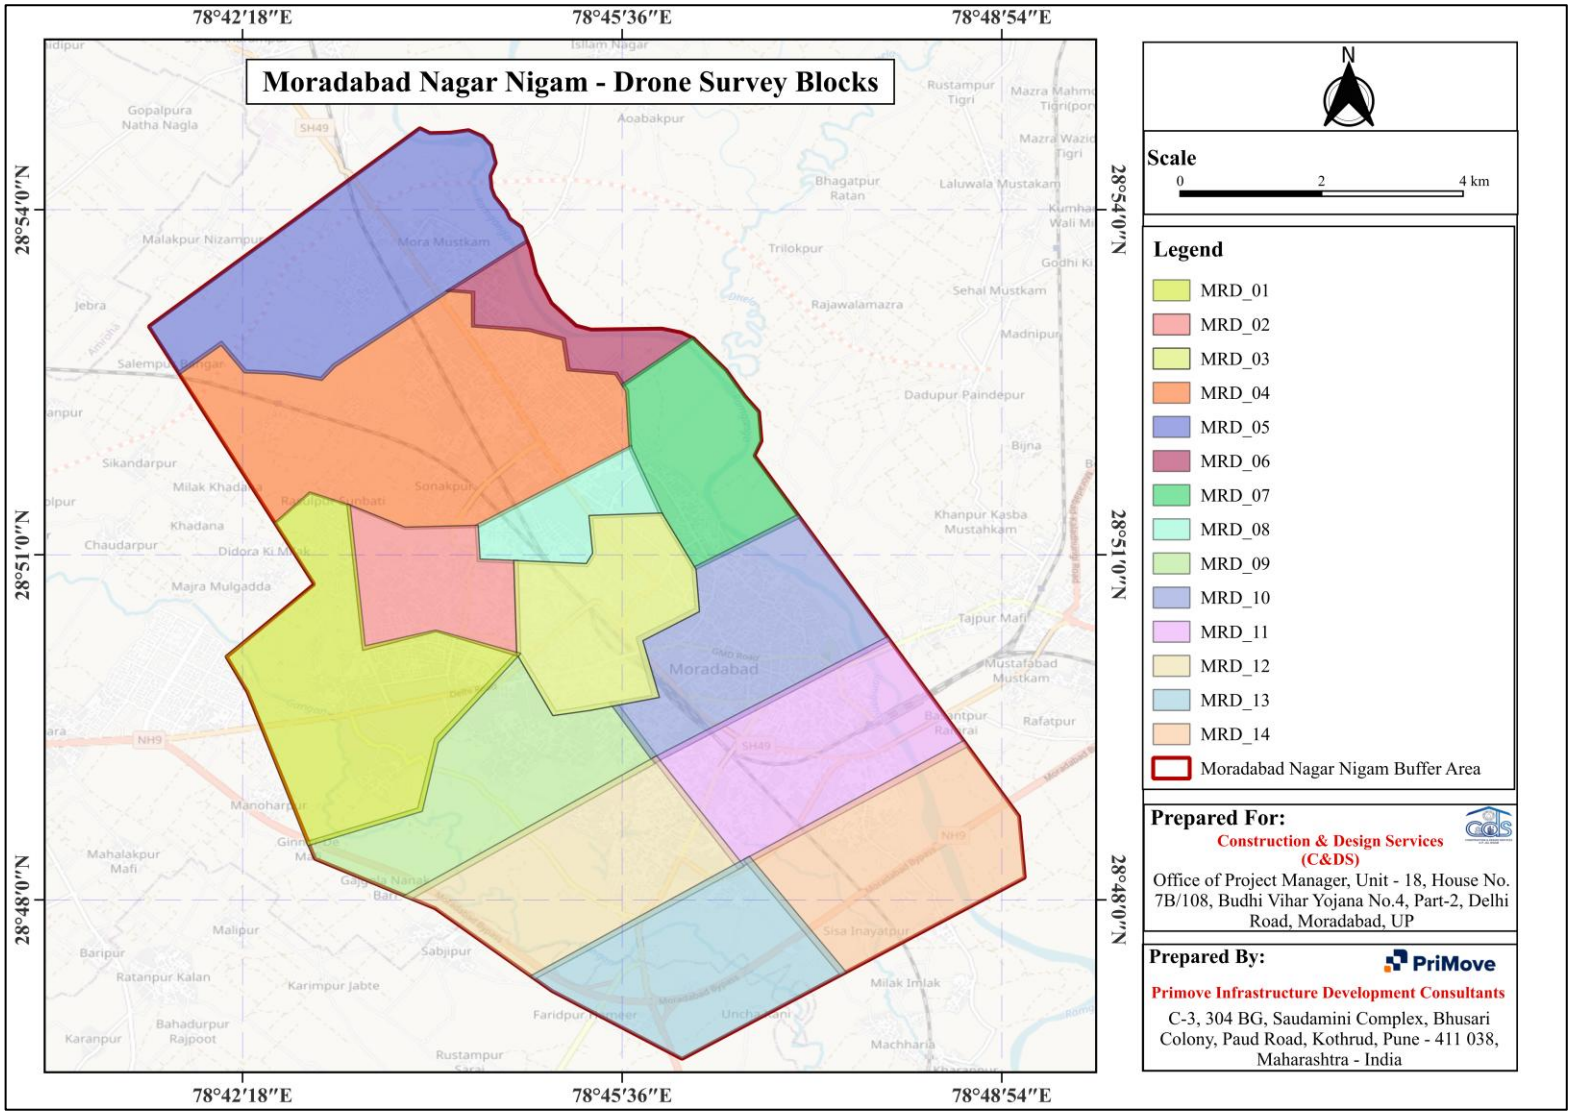


Figure : Drone Survey Completed

Submitted by: PriMove Infrastructure Consultants Pvt. Ltd. **Date:** 6/11/2026
